



City of Detroit

Inspector's Daily Report

7/23/2020 10:49 AM

FieldManager 5.3c

Contract: _PW-7018, City of Detroit Resurfacing 2020

IDR Date 7/17/2020	Day of Week Friday	Seq. No. 1	Import Date N/A	Project Engineer Jim Petronski - WSP	Construction Engineer Abdul Sidique - City of Detroit
Inspector's Initials-Name DW Damian Welborne				Federal Project Number	Elec. Attachments None
Prime Contractor Fort Wayne Contracting / Ajax Paving Industries, a joint ven					
Entered By DW, Damian Welborne		Revised By CAT, Carly A Taylor		Revision Date 7/23/2020 10:49 AM	Revision No. 1
Temperatures Low: 70 ° F High: 88 ° F		Weather Sunny			



Inspector's Daily Report

Comments

West Grand Boulevard from Linwood Avenue to Grand River Road.

7:00 AM - 5:00 PM

Ajax Paving Industries (API), Foreman Jason Tabani.

API set up arrow boards and cones along eastbound and westbound West Grand Blvd., from Grand River Rd. to Linwood Ave.

Along said stretch API brushed the curbs, swept, applied the bond coat and placed leveling course of 4E3 HMA (2.00 rolled) at a 13.00 ft wide portion of the West Grand Boulevard approach at Linwood Avenue, the Lawton Street cross-over south, the Lawton Street cross-over north, the Wildemere Street cross-over, the Wildemere Street approach north, the Dexter Avenue approach south, the Dexter Avenue cross-over, the Dexter Avenue approach north, the Lawton Street approach south and the Lawton Street approach north.

API also set temporary white stitched striping and furnished road drums along the eastbound and westbound West Grand Boulevard.

And Type 3 barricades have been placed at the sink hole located at Vinewood Street and Grand River Road.

TOTAL - 198.97 tons HMA 4E3 placed.

TOTAL - 368 gallons emulsified bond coat placed.

- - Note: HMA load # 1, "waste" from the Monroe Street work was delivered to West Grand Boulevard with 37.04 tons (HMA ticket remained with Monroe Street inspection staff).

- - Note: Ajax emulsified bond coat ticket totals Monroe Street and West Grand Boulevard work.

Visitors:

- None approached to or sought after by the writer.

Traffic:

- No incidents today. Sink hole at Vinewood Street remains barricaded with barrels and caution tape.

Attachments:

- Ajax Plant # 7 tickets # 2 through 7; and,
- Ajax bond coat ticket.

Covid-19 check: 96.9°F



Inspector's Daily Report

7/23/2020 10:49 AM

FieldManager 5.3c

Contractors

Contractor's Name	Personnel	No.	Hrs.	Equipment	No.	Hrs.
Ajax Paving Industries, Inc.	Flagger	5	37.50	Backhoe, Cat 430F	1	9.50
	Flagger Foreman	1	7.50	Broom, J. Deere	1	9.50
	Laborer	5	37.50	Paver, Cat AP1055F	1	7.50
	Operator	2	19.00	Portable Toilet	1	9.50
	Operator	2	15.00	Roller, Cat CB36B	1	7.50
	Operator Foreman (Jason)	1	7.50	Roller, Cat CB54	1	7.50
	Teamster	1	8.00	Roller, Cat CB54xW	1	9.50
				Street Sweeper (Municipal Sweeping)	1	8.00
				Tack Truck, Rosco	1	9.50
				Water Truck	1	9.50
				Water Truck	1	7.50

Item Postings

Item/Material Description	Item Code	Prop. Line	Project	Category	Quantity	Unit	Location	Brkdwn ID	Attn
_ HMA Approach, Modified, Adj	5017031	0975	PW-7018	0000	198.970	Ton	HMA Approaches along Grand Blvd.		
Contractor:									
Ajax Paving Industries, Inc.									
Bond Coat, Emulsified Asphalt SS-1H						368.00	Gal		
Material Remarks: This quantity was shared with Monroe.									
HMA, 4E3						198.97	Ton		
Material Remarks: Ajax Plant #7									

Reviewed By: Carly Taylor Carly Taylor
Jul 31 2020 7:59 AM
(Signature)

(Date)

Cold Milling HMA Approach Surface, Modified

DATE: 20200714

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Industrial

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020


PROJECT ENGINEER: Jim Petronski

LOCATION: Detroit, Mi.

SHEETS: 1 of 7

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Dexter	North Bound	W. Grand Blvd	14	27	0	0	14	15
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
423.2	47.02	378.0	0.0	45.2				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	10,343.67	5.17
Date of Completion		

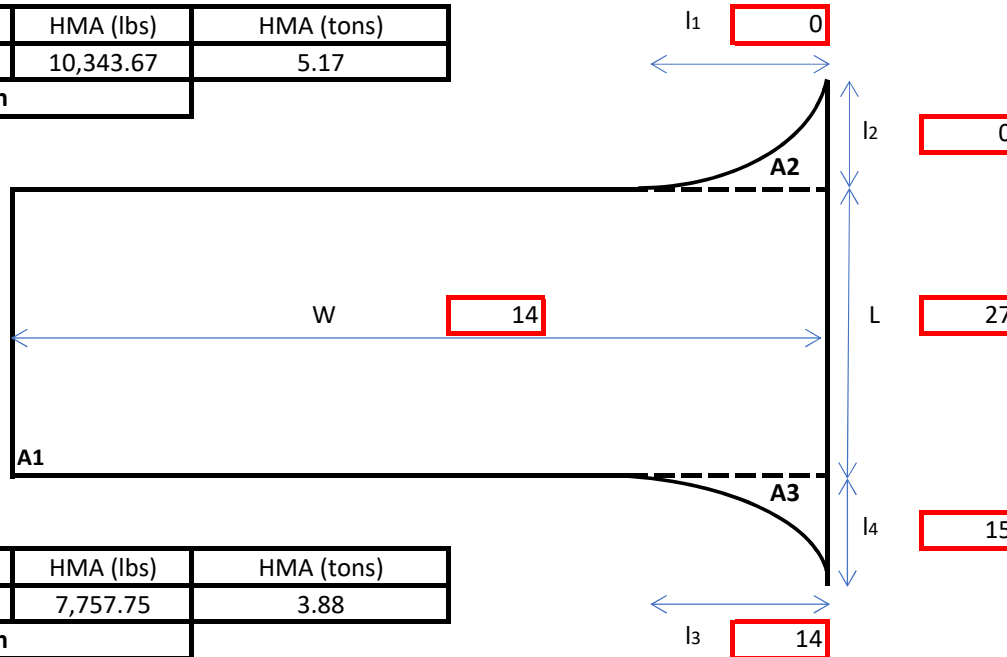

MDOT 4E5	HMA (lbs)	HMA (tons)
165	7,757.75	3.88
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott

REVIEWED BY: _____

DATE: _____

DATE: _____

Cold Milling HMA Approach Surface, Modified

DATE: 20200714

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Industrial

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020


PROJECT ENGINEER: Jim Petronski

LOCATION: Detroit, Mi.

SHEETS: 2 of 7

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Dexter	W. Grand Blvd	North Side	18	65	22	40	15	29
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
1,452.7	161.41	1170.0	189.2	93.5				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	35,511.06	17.76
Date of Completion		

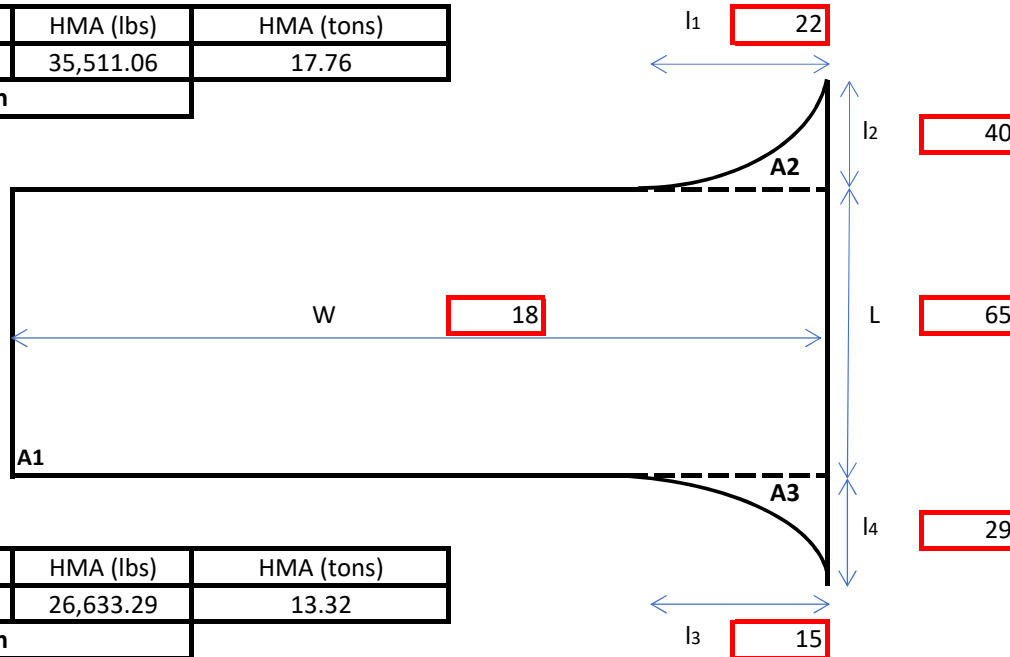

MDOT 4E5	HMA (lbs)	HMA (tons)
165	26,633.29	13.32
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott

REVIEWED BY: _____

DATE: _____

DATE: _____

Cold Milling HMA Approach Surface, Modified

DATE: 20200714

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Industrial

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020


PROJECT ENGINEER: Jim Petronski

LOCATION: Detroit, Mi.

SHEETS: 3 of 7

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Dexter	South Bound	W. Grand Blvd.	14	23	0	0	0	0
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
322.0	35.78	322.0	0.0	0.0				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	7,871.11	3.94
Date of Completion		

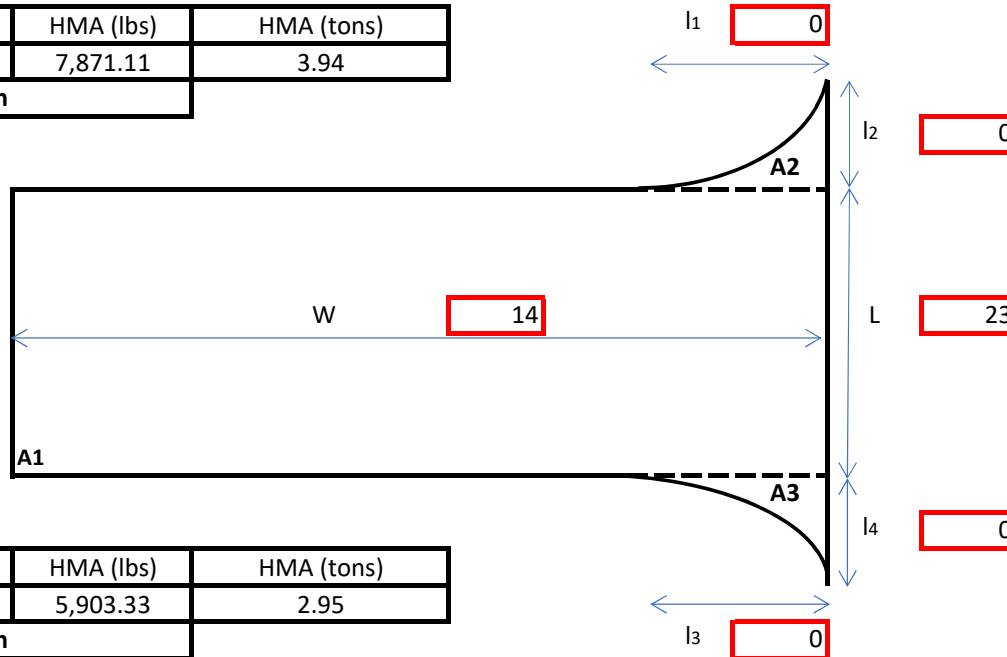

MDOT 4E5	HMA (lbs)	HMA (tons)
165	5,903.33	2.95
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott

REVIEWED BY: _____

DATE: _____

DATE: _____

Cold Milling HMA Approach Surface, Modified

DATE: 20200713

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Industrial

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020


PROJECT ENGINEER: Jim Petronski

LOCATION: Detroit, Mi.

SHEETS: 4 of 7

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Lawton	W. Grand Blvd	North Side	16	30	16	23	16	15
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
610.7	67.86	480.0	79.1	51.6				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	14,928.71	7.46
Date of Completion		

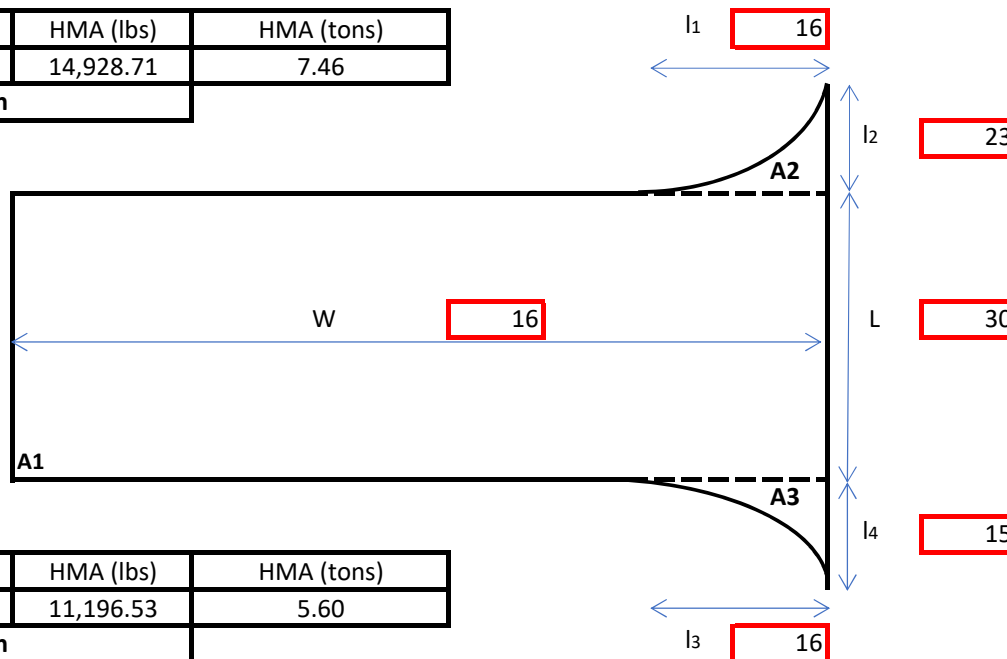

MDOT 4E5	HMA (lbs)	HMA (tons)
165	11,196.53	5.60
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott

REVIEWED BY: _____

DATE: _____

DATE: _____

Cold Milling HMA Approach Surface, Modified

DATE: 20200713

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Industrial

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020


PROJECT ENGINEER: Jim Petronski

LOCATION: Detroit, Mi.

SHEETS: 5 of 7

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Lawton	W. Grand Blvd	South Side	16.5	36	16.5	14	16.5	11
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
682.7	75.85	594.0	49.7	39.0				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	16,687.92	8.34
Date of Completion		

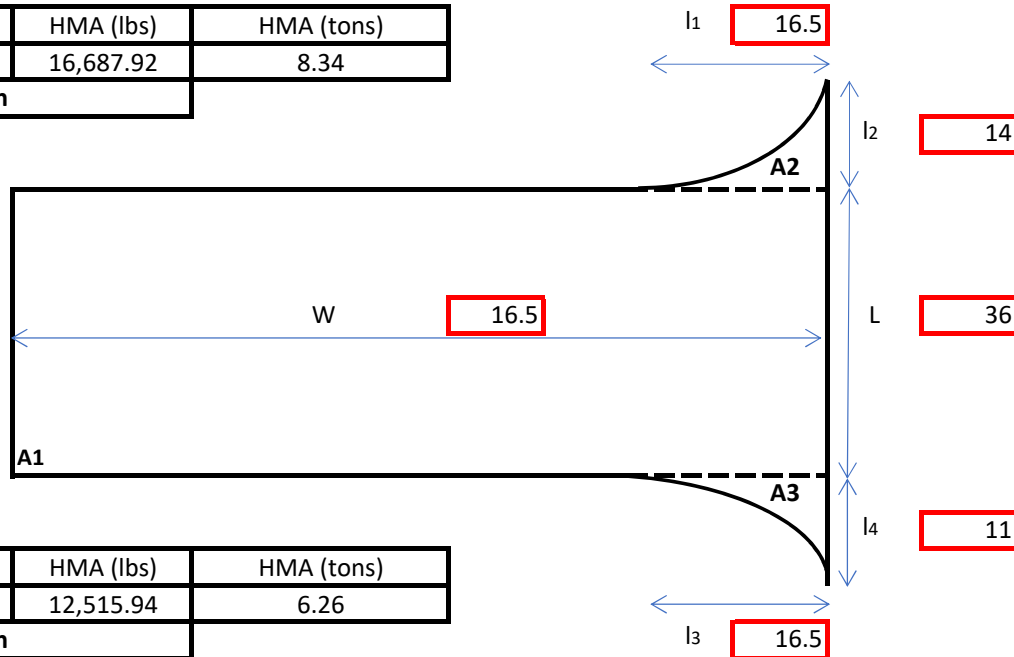

MDOT 4E5	HMA (lbs)	HMA (tons)
165	12,515.94	6.26
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott

REVIEWED BY: _____

DATE: _____

DATE: _____

Cold Milling HMA Approach Surface, Modified

DATE: 20200714

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Industrial

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020


PROJECT ENGINEER: Jim Petronski

LOCATION: Detroit, Mi.

SHEETS: 6 of 7

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Vinewood	W. Grand Blvd	Grand River	49	18	39	35	0	0
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
1,175.5	130.61	882.0	293.5	0.0				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	28,733.83	14.37
Date of Completion		

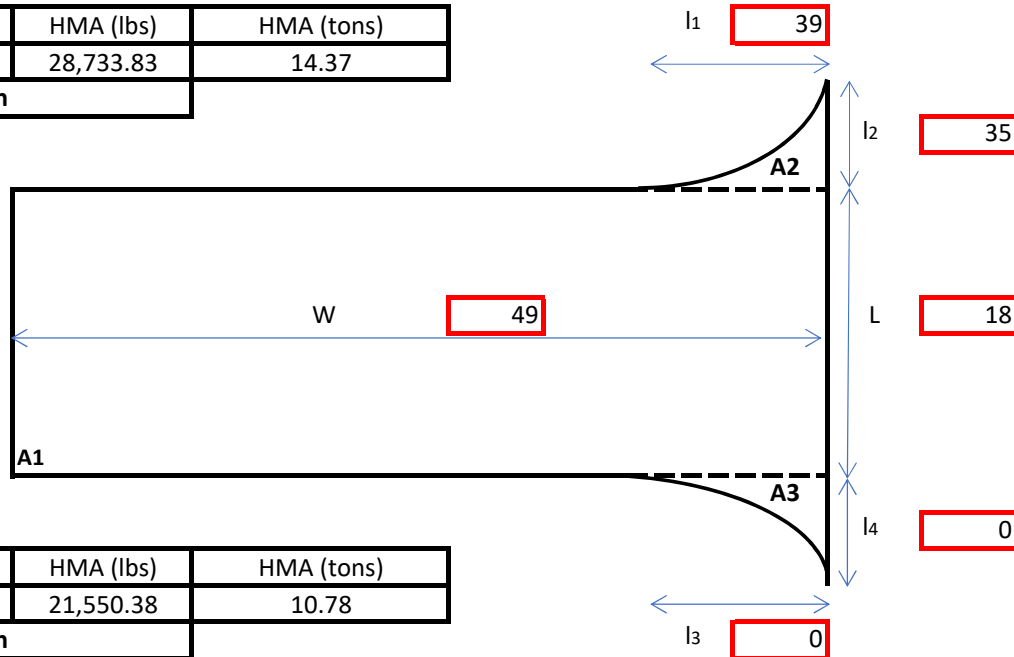

MDOT 4E5	HMA (lbs)	HMA (tons)
165	21,550.38	10.78
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott

REVIEWED BY: _____

DATE: _____

DATE: _____

Cold Milling HMA Approach Surface, Modified

DATE: 20200713

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Industrial

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020


PROJECT ENGINEER: Jim Petronski

LOCATION: Detroit, Mi.

SHEETS: 7 of 7

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Wildemere	W. Grand Blvd	North Side	15	20	13	14	15	13
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
381.1	42.34	300.0	39.1	41.9				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	9,314.68	4.66
Date of Completion		

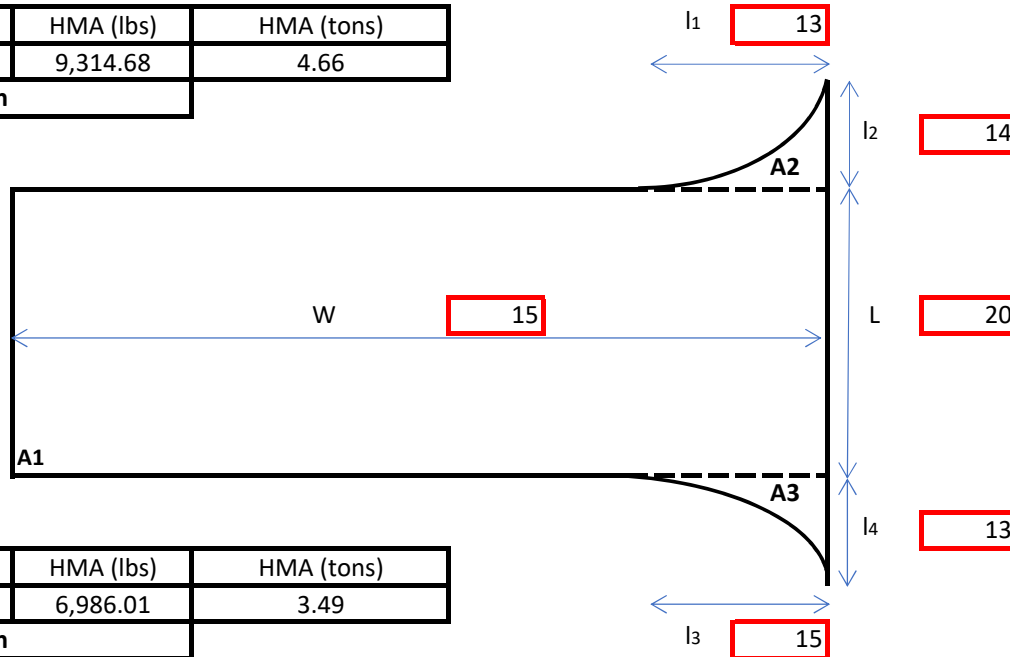

MDOT 4E5	HMA (lbs)	HMA (tons)
165	6,986.01	3.49
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott

REVIEWED BY: _____

DATE: _____

DATE: _____



City of Detroit

Inspector's Daily Report

7/21/2020 12:28 PM

FieldManager 5.3c

Contract: _PW-7018, City of Detroit Resurfacing 2020

IDR Date 7/17/2020	Day of Week Friday	Seq. No. 1	Import Date 7/21/2020	Project Engineer Jim Petronski - WSP	Construction Engineer Abdul Sidique - City of Detroit
Inspector's Initials-Name DW Damian Welborne				Federal Project Number	Elec. Attachments None
Prime Contractor Fort Wayne Contracting / Ajax Paving Industries, a joint ven					
Entered By DW, Damian Welborne		Revised By		Revision Date	Revision No.
Temperatures Low: 70 ° F High: 88 ° F		Weather Sunny			



Inspector's Daily Report

Comments

West Grand Boulevard from Linwood Avenue to Grand River Road.

7:00 AM - 5:00 PM

Ajax Paving Industries (API), Foreman Jason Tabani.

API set up arrow boards and cones along eastbound and westbound West Grand Blvd., from Grand River Rd. to Linwood Ave.

Along said stretch API brushed the curbs, swept, applied the bond coat and placed leveling course of 4E3 HMA (2.00 rolled) at a 13.00 ft wide portion of the West Grand Boulevard approach at Linwood Avenue, the Lawton Street cross-over south, the Lawton Street cross-over north, the Wildemere Street cross-over, the Wildemere Street approach north, the Dexter Avenue approach south, the Dexter Avenue cross-over, the Dexter Avenue approach north, the Lawton Street approach south and the Lawton Street approach north.

API also set temporary white stitched striping and furnished road drums along the eastbound and westbound West Grand Boulevard.

And Type 3 barricades have been placed at the sink hole located at Vinewood Street and Grand River Road.

TOTAL - 198.97 tons HMA 4E3 placed.

TOTAL - 368 gallons emulsified bond coat placed.

- - Note: HMA load # 1, "waste" from the Monroe Street work was delivered to West Grand Boulevard with 37.04 tons (HMA ticket remained with Monroe Street inspection staff).

- - Note: Ajax emulsified bond coat ticket totals Monroe Street and West Grand Boulevard work.

Visitors:

- None approached to or sought after by the writer.

Traffic:

- No incidents today. Sink hole at Vinewood Street remains barricaded with barrels and caution tape.

Attachments:

- Ajax Plant # 7 tickets # 2 through 7; and,
- Ajax bond coat ticket.

Covid-19 check: 96.9*f



City of Detroit

Inspector's Daily Report

7/21/2020 12:28 PM

FieldManager 5.3c

Contractors

Contractor's Name	Personnel	No.	Hrs.	Equipment	No.	Hrs.
Ajax Paving Industries, Inc.	Flagger	5	37.50	Backhoe, Cat 430F	1	9.50
	Flagger Foreman	1	7.50	Broom, J. Deere	1	9.50
	Laborer	5	37.50	Paver, Cat AP1055F	1	7.50
	Operator	2	19.00	Portable Toilet	1	9.50
	Operator	2	15.00	Roller, Cat CB36B	1	7.50
	Operator Foreman (Jason)	1	7.50	Roller, Cat CB54	1	7.50
	Teamster	1	8.00	Roller, Cat CB54xW	1	9.50
				Street Sweeper (Municipal Sweeping)	1	8.00
				Tack Truck, Rosco	1	9.50
				Water Truck	1	9.50
				Water Truck	1	7.50

Item Postings

Item/Material Description	Item Code	Prop. Line	Project	Category	Quantity	Unit	Location	Brkdwn ID	Attn
HMA, 4E3	_50100510260	PW-7018		0000	198.970	Ton	West Grand Boulevard from Linwood Avenue to Grand River Road.		
Contractor: Ajax Paving Industries, Inc.									

Change to HMA Approach

Item Remarks: HMA load # 1, "waste" from the Monroe Street work was delivered to West Grand Boulevard with 37.04 tons (HMA ticket remained with Monroe Street inspection staff).

Bond Coat, Emulsified Asphalt SS-1H

368.00 Gal

Material Remarks: Material: Ajax.
Field identified and accepted.

HMA, 4E3

198.97 Ton

Material Remarks: Material: Ajax Plant # 7.
Field identified and accepted.

Reviewed By: _____
(Signature)

(Date)
