



City of Detroit

Inspector's Daily Report

7/30/2020 10:51 AM

FieldManager 5.3c

Contract: _PW-7018, City of Detroit Resurfacing 2020

IDR Date 7/23/2020	Day of Week Thursday	Seq. No. 1	Import Date N/A	Project Engineer Jim Petronski - WSP	Construction Engineer Abdul Siddiqui - City of Detroit
Inspector's Initials-Name DH Dwight Harris				Federal Project Number	Elec. Attachments None
Prime Contractor Fort Wayne Contracting / Ajax Paving Industries, a joint ven					
Entered By DH, Dwight Harris		Revised By CAT, Carly A Taylor		Revision Date 8/4/2020 3:14 PM	Revision No. 1
Temperatures Low: 70 ° F High: 87 ° F		Weather Sunny			
Comments Ajax Paving used vac truck with sweeper to clean surfaces, sprayed bond coat, to place 4E3 HMA material in approaches on carpenter between Dequndre and Conant. Rollers were used for compaction. Flaggers, arrow boards and barricades were in place for traffic control. Job site safe and secure at the end of the day.					

Contractors

Contractor's Name	Personnel	No.	Hrs.	Equipment	No.	Hrs.
Ajax Paving Industries, Inc.	Flagers	5	8.00	Paver	1	8.00
	Foreman	1	8.00	Roller	2	8.00
	Labors	6	8.00	Spray Truck	1	8.00
	Operators	7	8.00	Stake truck	1	8.00
				Tractor w/Broom	1	8.00



City of Detroit

Inspector's Daily Report

7/30/2020 10:51 AM

FieldManager 5.3c

Item Postings

Item/Material Description	Item Code	Prop. Line	Project	Category	Quantity	Unit	Location	Brkdwn ID	Attn
_ HMA Approach, Modified, Adj Contractor:	5017031	0975	PW-7018	0000	144.980	Ton	Approaches on Carpenter street, between Dequindre and Conant.		
Ajax Paving Industries, Inc.									
Item Remarks: Final Field Measured									
Bond Coat, Emulsified Asphalt SS-1H							105.00 Gal		
Material Remarks: VI and accepted, Ajax Plant #7									
HMA, 4E3							144.98 Ton		
Material Remarks: Ajax Plant #7									

Reviewed By: Carly Taylor Carly Taylor
Aug 17 2020 9:31 AM
(Signature)

(Date)

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 7/20/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 1 of 21

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Arlington	Carpenter	North Side	12.5	26	5.5	4.5	8.5	9
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
346.8	38.53	325.0	5.3	16.4				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	8,476.57	4.24
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	26.0
SYD	5.78

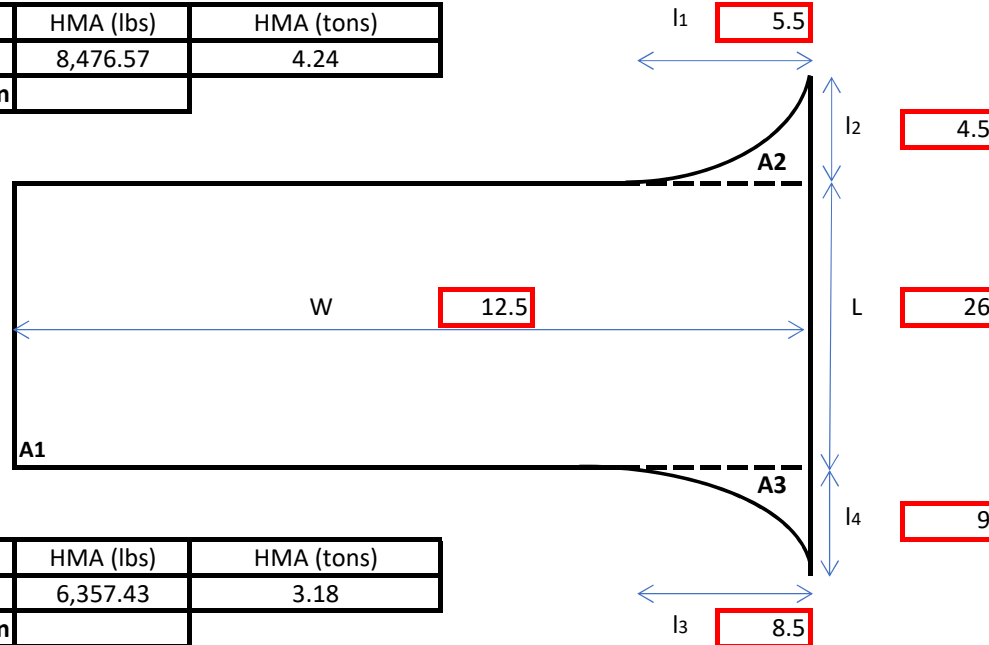

MDOT 5E3	HMA (lbs)	HMA (tons)
165	6,357.43	3.18
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott

DATE:

REVIEWED BY:

DATE:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 7/20/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 4 of 21

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Fleming	Carpenter	South Side	12	27	14	10	8	8
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
367.9	40.87	324.0	30.1	13.8				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	8,992.13	4.50
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	27.0
SYD	6.00

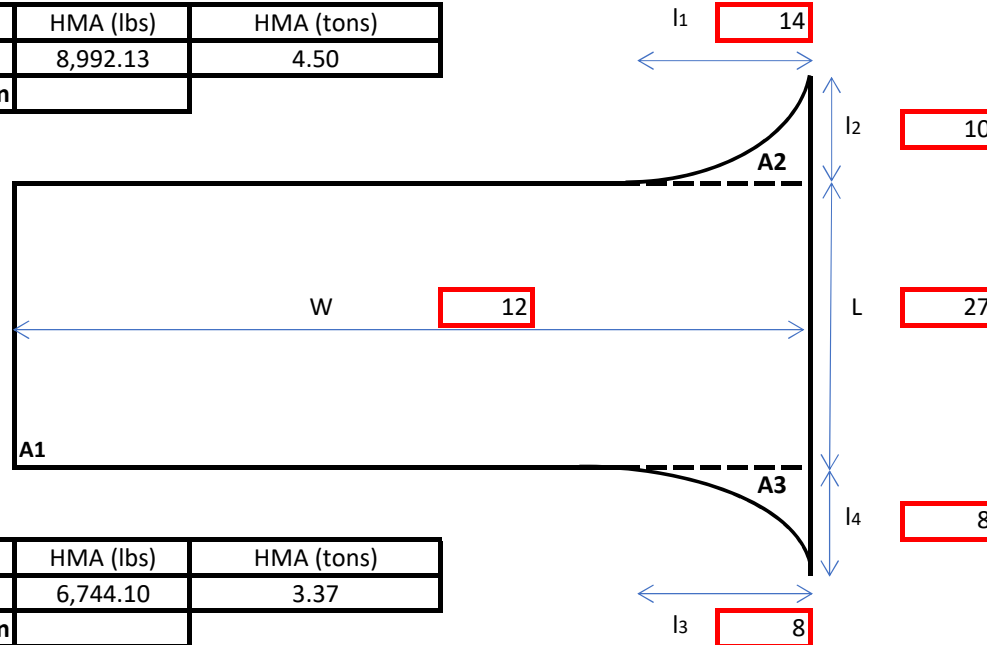

MDOT 5E3	HMA (lbs)	HMA (tons)
165	6,744.10	3.37
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott

DATE:

REVIEWED BY:

DATE:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 7/20/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 7 of 21

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Goddard	Carpenter	North Side	14	26	8.5	9	9	9
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)				
		364.0	16.4	17.4	Location No.: A1			
397.9	44.21							

MDOT 4E3	HMA (lbs)	HMA (tons)
220	9,725.53	4.86
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	26.0
SYD	5.78

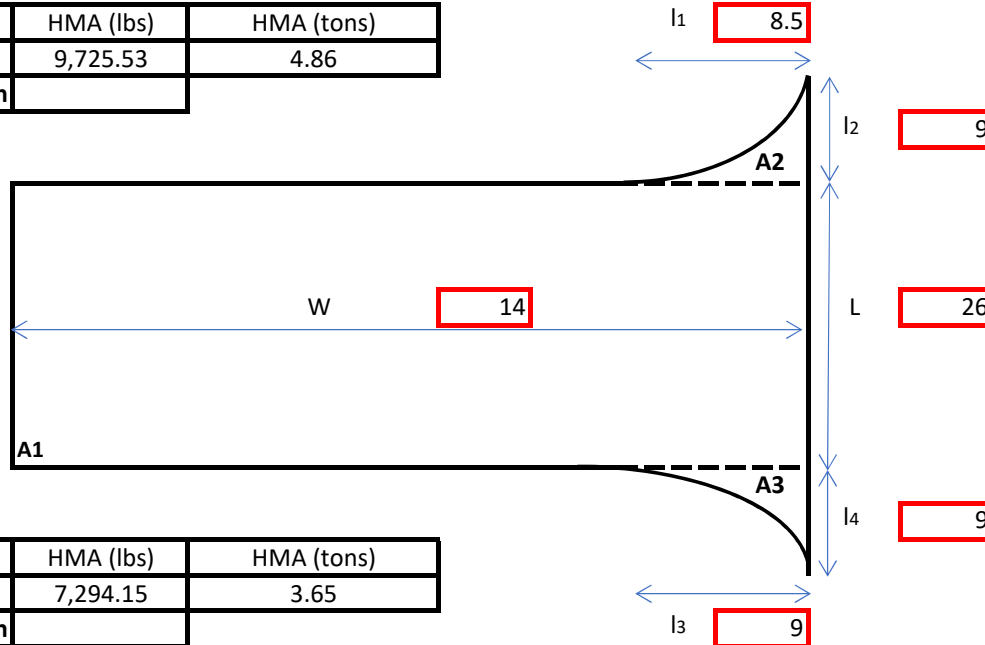

MDOT 5E3	HMA (lbs)	HMA (tons)
165	7,294.15	3.65
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott

DATE:

REVIEWED BY:

DATE:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 7/20/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 10 of 21

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Lumpkin	Carpenter	South Side	11	29	14	10	14	9
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
376.2	41.80	319.0	30.1	27.1				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	9,195.76	4.60
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	29.0
SYD	6.44

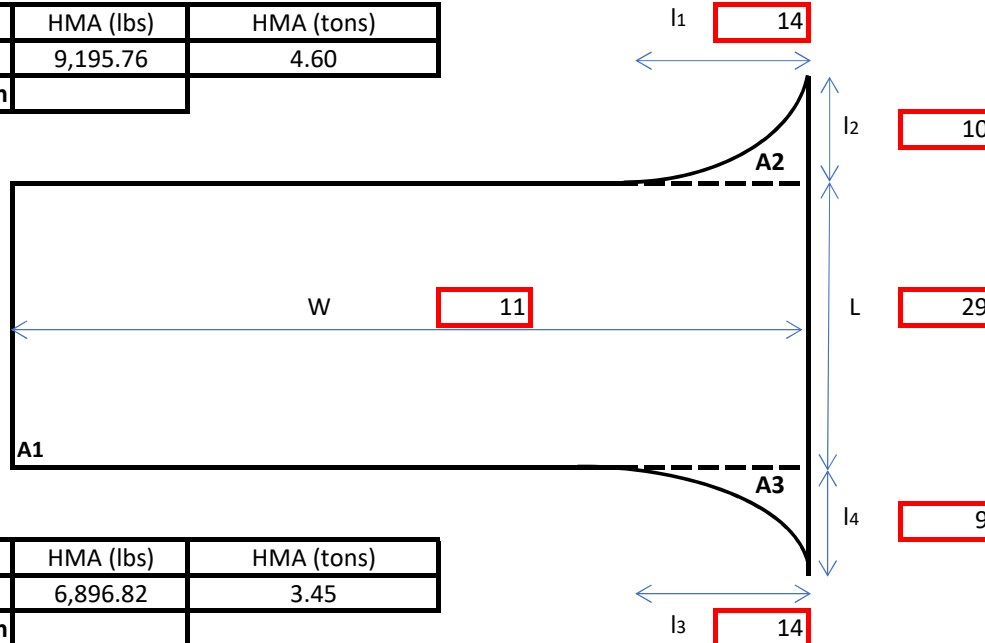

MDOT 5E3	HMA (lbs)	HMA (tons)
165	6,896.82	3.45
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott

DATE:

REVIEWED BY:

DATE:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 7/20/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 11 of 21

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Mackay	Carpenter	North Side	11	27	6.5	4.5	7	6
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
312.3	34.70	297.0	6.3	9.0				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	7,634.46	3.82
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	27.0
SYD	6.00

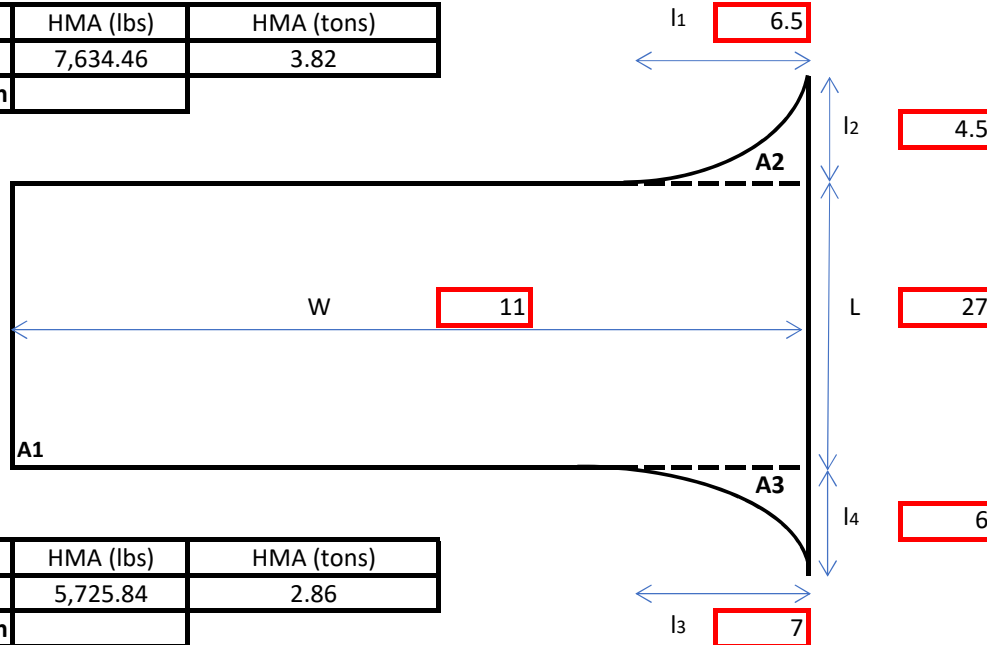

MDOT 5E3	HMA (lbs)	HMA (tons)
165	5,725.84	2.86
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott

DATE: _____

REVIEWED BY: _____

DATE: _____

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 7/20/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 12 of 21

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Mackay	Carpenter	South Side	4	33	6.5	12	6	11
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
163.0	18.11	132.0	16.8	14.2				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	3,983.47	1.99
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	33.0
SYD	7.33

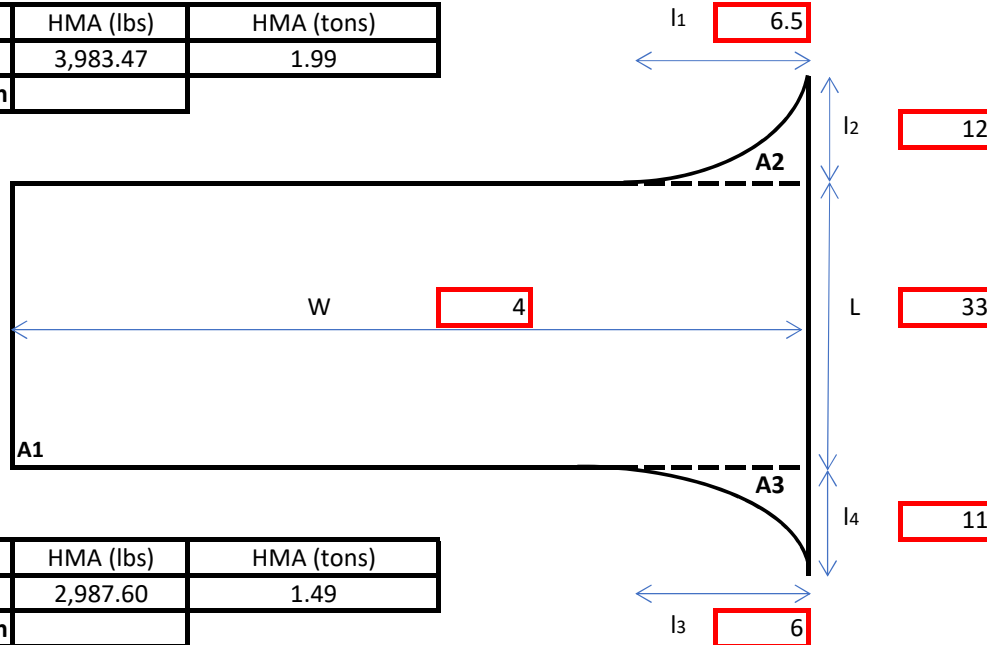

MDOT 5E3	HMA (lbs)	HMA (tons)
165	2,987.60	1.49
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott

DATE: _____

REVIEWED BY: _____

DATE: _____

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 7/20/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 13 of 21

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Main	Carpenter	North Side	13	25.5	7	8	9	7
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
357.1	39.68	331.5	12.0	13.5				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	8,728.74	4.36
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	25.5
SYD	5.67

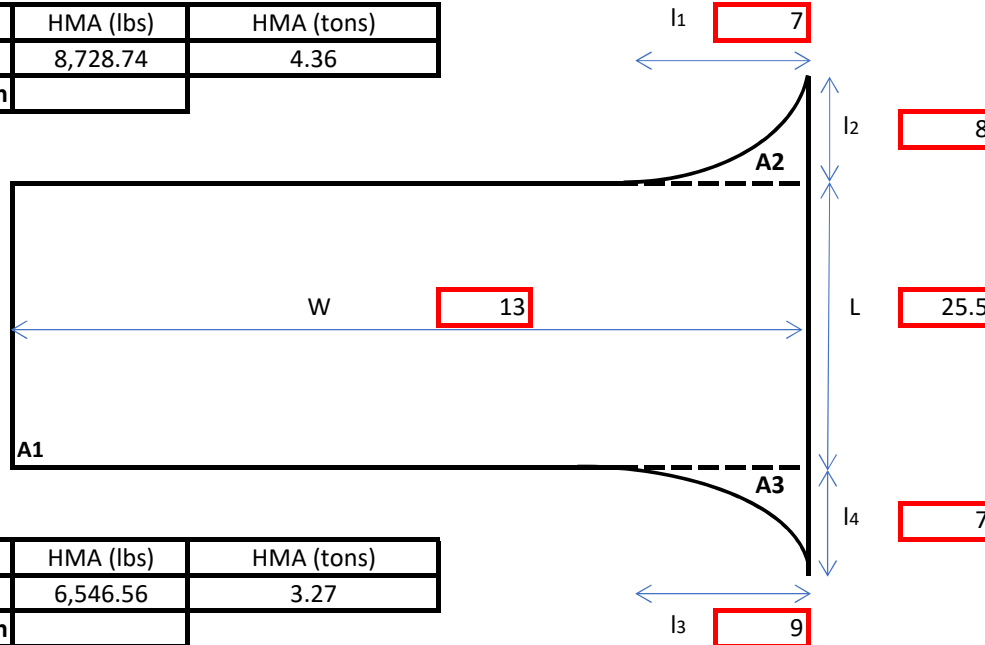

MDOT 5E3	HMA (lbs)	HMA (tons)
165	6,546.56	3.27
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott

DATE:

REVIEWED BY:

DATE:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 7/20/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 21 of 21

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
St. Aubin	Carpenter	South Side	13	35	15	15	15	11
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
538.9	59.87	455.0	48.4	35.5				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	13,171.89	6.59
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	35.0
SYD	7.78

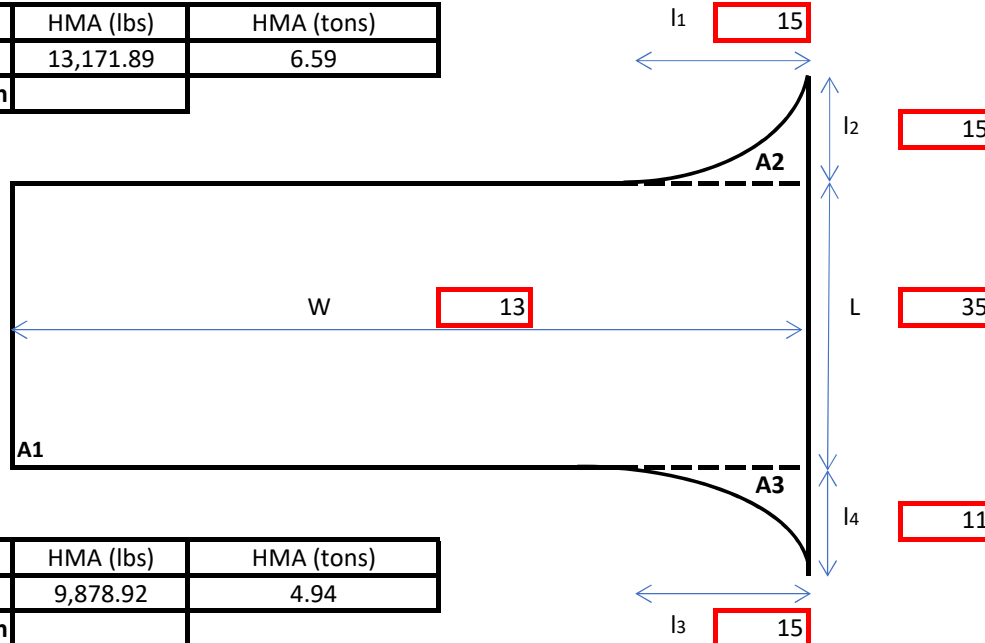

MDOT 5E3	HMA (lbs)	HMA (tons)
165	9,878.92	4.94
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott

DATE:

REVIEWED BY:

DATE:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 7/21/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 2 of 21

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Charest	Carpenter	North Side	12.5	28	7	8.5	7.5	8
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
375.7	41.74	350.0	12.8	12.9				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	9,183.59	4.59
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	28.0
SYD	6.22

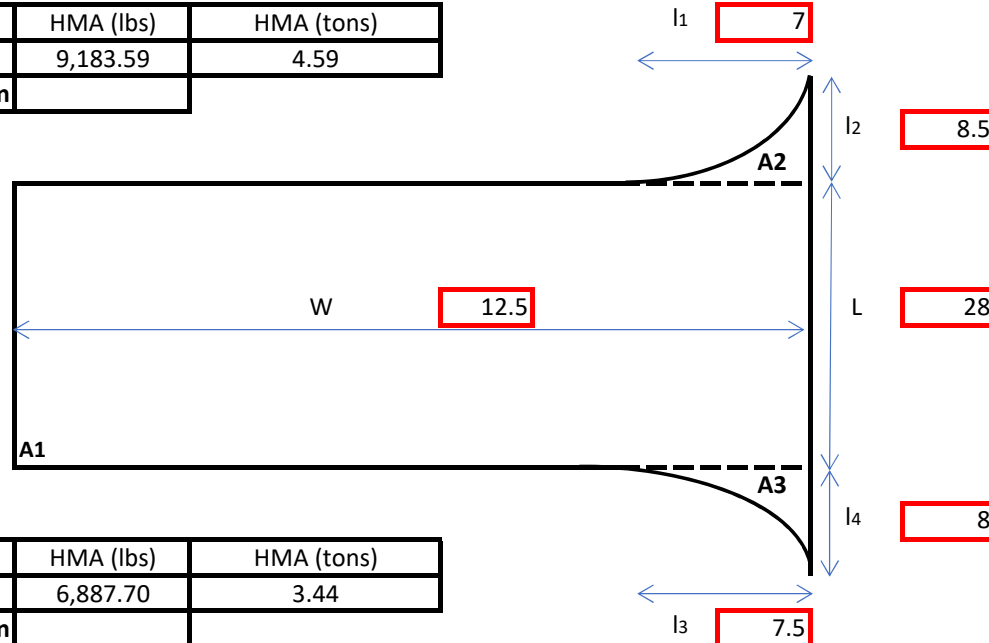

MDOT 5E3	HMA (lbs)	HMA (tons)
165	6,887.70	3.44
Date of Completion		

FIELD INSPECTOR: _____

DATE: _____

REVIEWED BY: _____

DATE: _____

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 7/21/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 3 of 21

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Charest	Carpenter	South Side	12.5	29	6	5.5	8	7
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
381.6	42.40	362.5	7.1	12.0				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	9,328.86	4.66
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	29.0
SYD	6.44

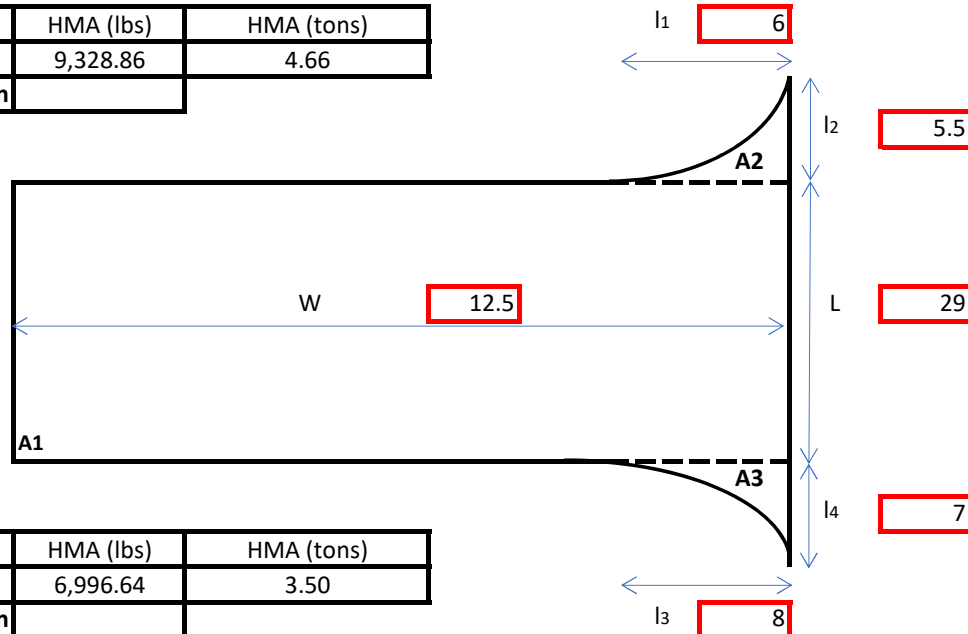

MDOT 5E3	HMA (lbs)	HMA (tons)
165	6,996.64	3.50
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott

DATE: _____

REVIEWED BY: _____

DATE: _____

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 7/21/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 5 of 21

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Gallagher	Carpenter	North Side	11	27	7	6.5	9	7
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
320.3	35.59	297.0	9.8	13.5				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	7,830.23	3.92
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	27.0
SYD	6.00

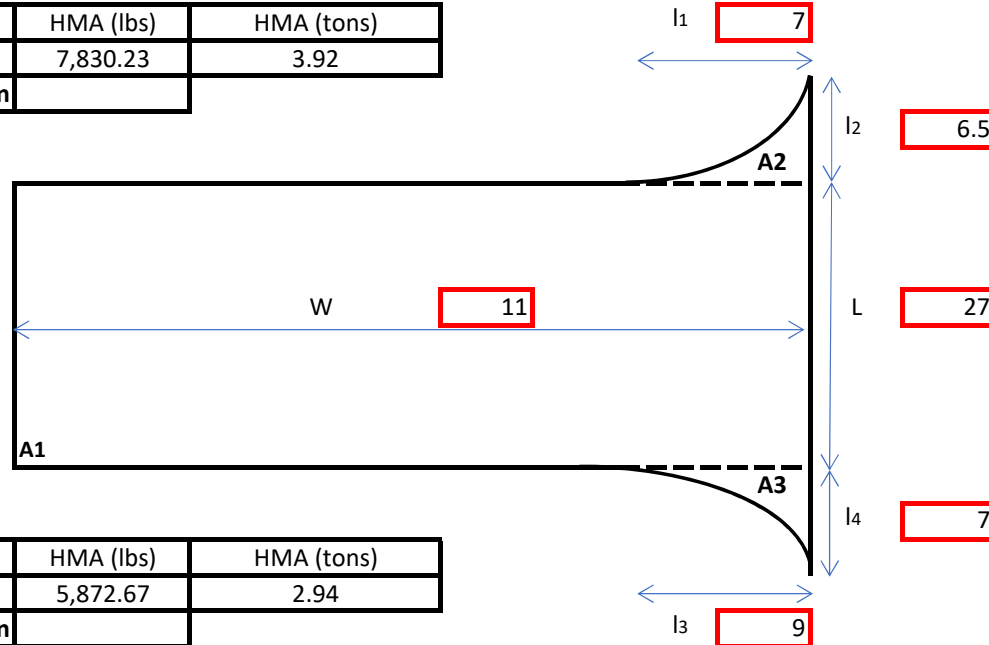

MDOT 5E3	HMA (lbs)	HMA (tons)
165	5,872.67	2.94
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott

DATE:

REVIEWED BY:

DATE:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 7/21/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 6 of 21

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Gallagher	Carpenter	South Side	13	26	6.5	5	7	7.5
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
356.3	39.59	338.0	7.0	11.3				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	8,708.94	4.35
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	26.0
SYD	5.78

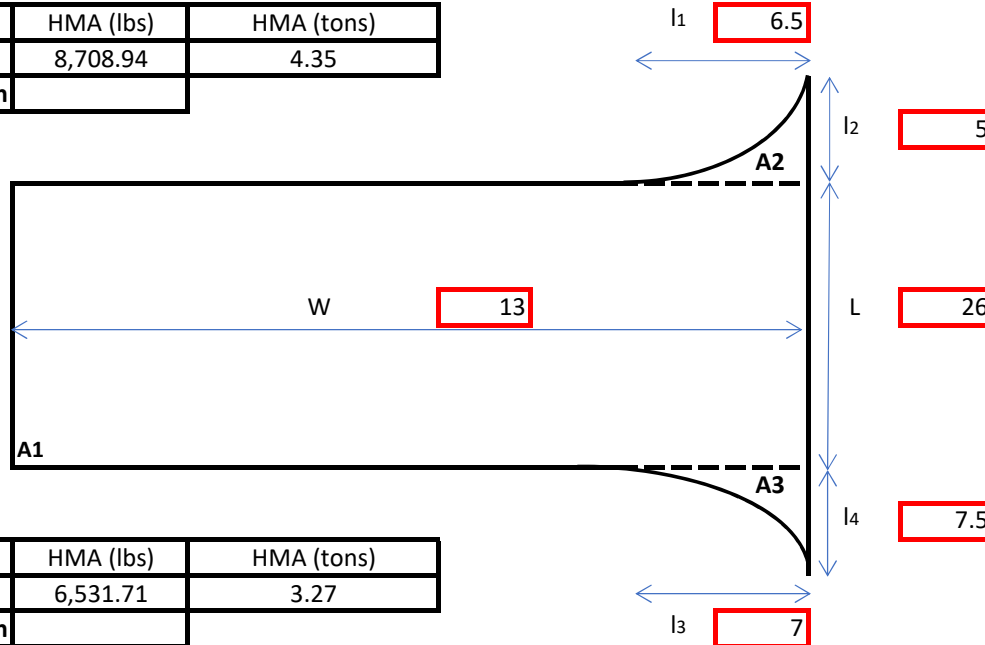

MDOT 5E3	HMA (lbs)	HMA (tons)
165	6,531.71	3.27
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott

DATE:

REVIEWED BY:

DATE:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 7/21/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 8 of 21

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Klinger	Carpenter	North Side	11	24	6	8.5	10	8
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
292.2	32.46	264.0	11.0	17.2				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	7,141.81	3.57
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	24.0
SYD	5.33

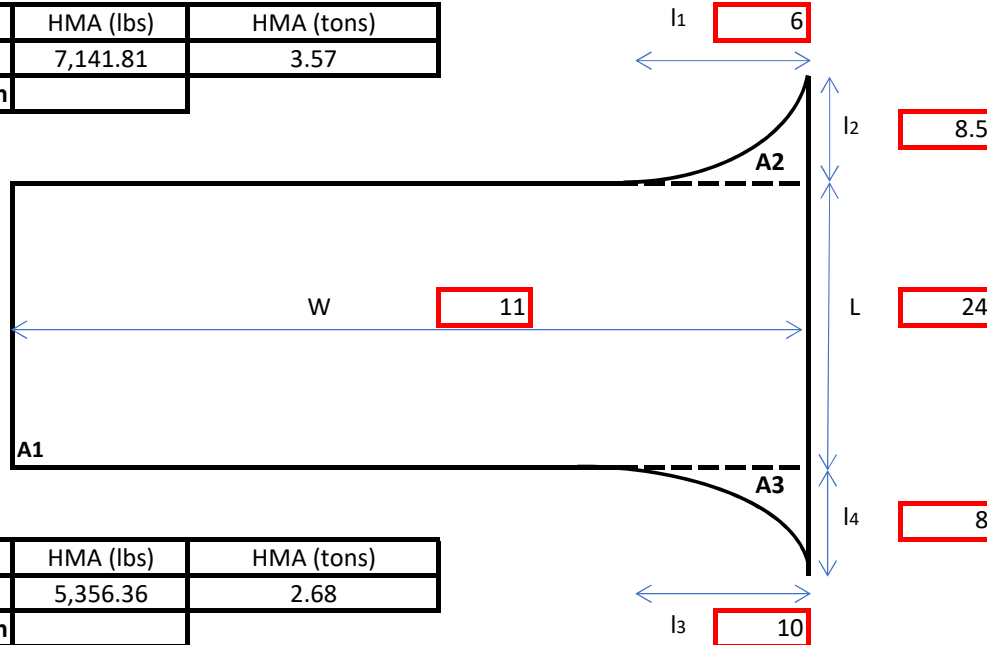

MDOT 5E3	HMA (lbs)	HMA (tons)
165	5,356.36	2.68
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott

REVIEWED BY:

DATE:

DATE:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 7/21/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 9 of 21

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Klinger	Carpenter	South Side	13.5	30	0	0	8	8.5
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
419.6	46.62	405.0	0.0	14.6				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	10,257.38	5.13
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	30.0
SYD	6.67

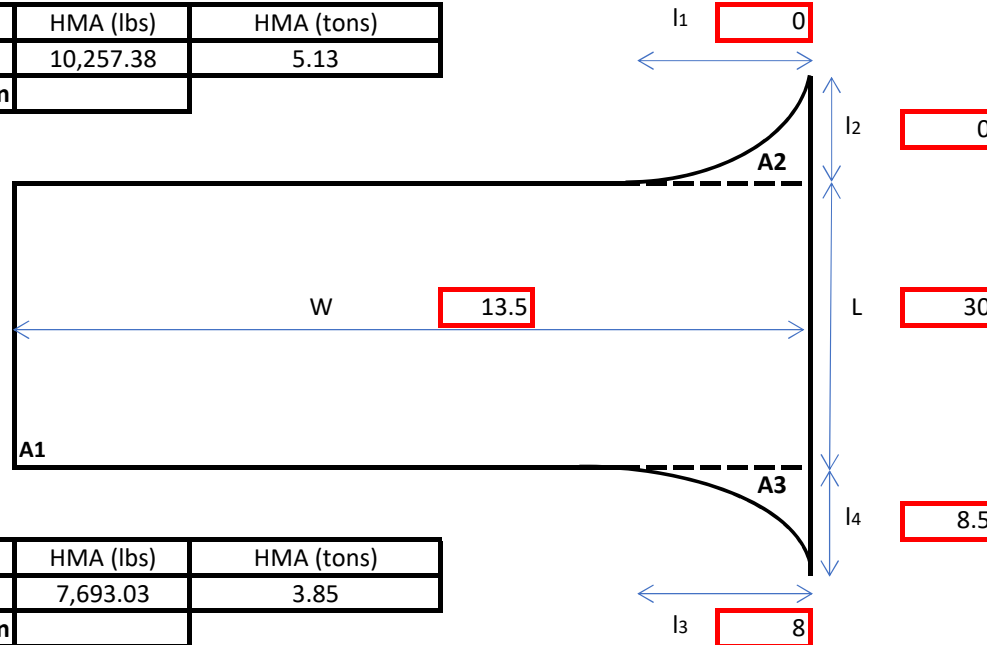

MDOT 5E3	HMA (lbs)	HMA (tons)
165	7,693.03	3.85
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott

DATE:

REVIEWED BY:

DATE:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 7/21/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 14 of 21

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
McDougall	Carpenter	North Side	10	28	6	7.5	10.5	8
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
307.7	34.19	280.0	9.7	18.1				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	7,522.41	3.76
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	28.0
SYD	6.22

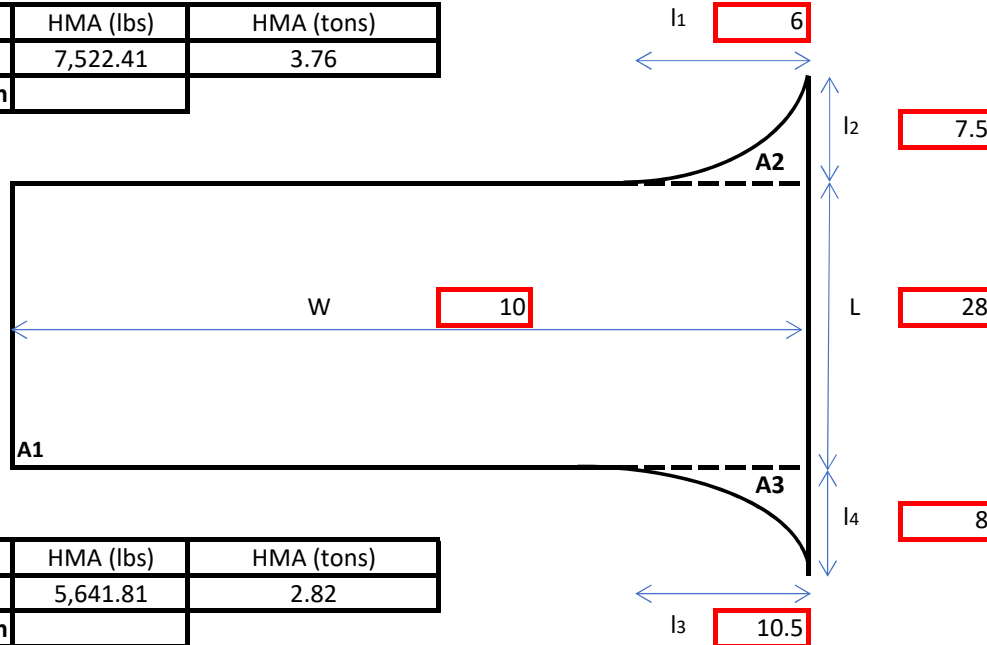

MDOT 5E3	HMA (lbs)	HMA (tons)
165	5,641.81	2.82
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott

DATE: _____

REVIEWED BY: _____

DATE: _____

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 7/21/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 15 of 21

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
McDougall	Carpenter	South Side	13.5	30	7	9.5	7	7
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
429.8	47.76	405.0	14.3	10.5				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	10,507.02	5.25
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	30.0
SYD	6.67

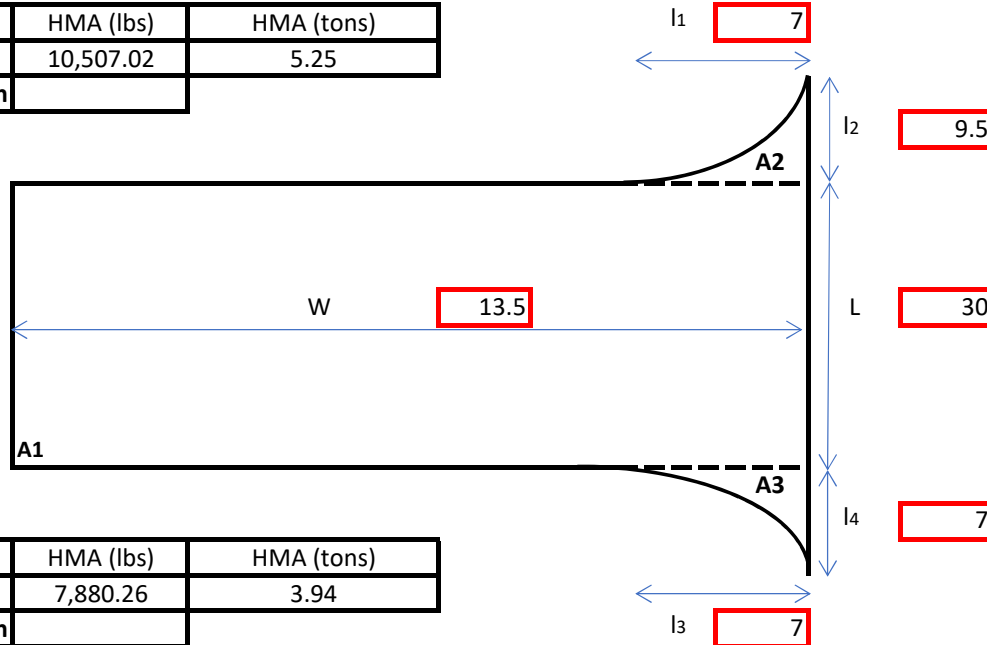

MDOT 5E3	HMA (lbs)	HMA (tons)
165	7,880.26	3.94
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott

DATE: _____

REVIEWED BY: _____

DATE: _____

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 7/21/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 16 of 21

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Mitchell	Carpenter	North Side	13	25.5	8	7.5	10	7.5
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
360.5	40.06	331.5	12.9	16.1				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	8,812.83	4.41
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	25.5
SYD	5.67

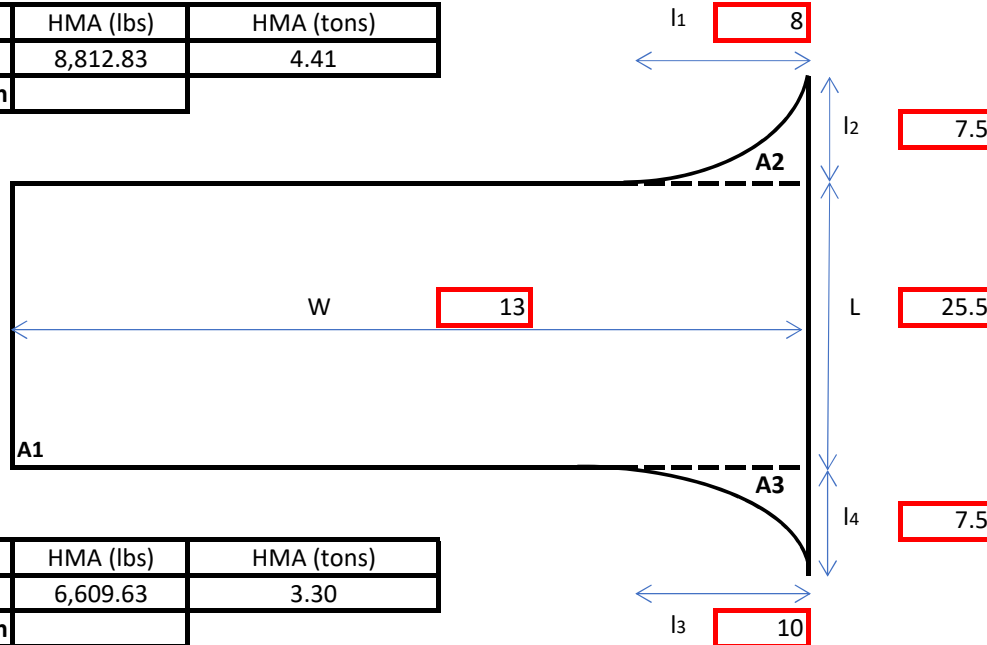

MDOT 5E3	HMA (lbs)	HMA (tons)
165	6,609.63	3.30
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott

DATE:

REVIEWED BY:

DATE:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 7/21/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 17 of 21

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Mitchell	Carpenter	South Side	12	28.5	7.5	8.5	10	8.5
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)				
		342.0	13.7	18.3	Location No.: A1			
374.0	41.55							

MDOT 4E3	HMA (lbs)	HMA (tons)
220	9,141.76	4.57
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	28.5
SYD	6.33

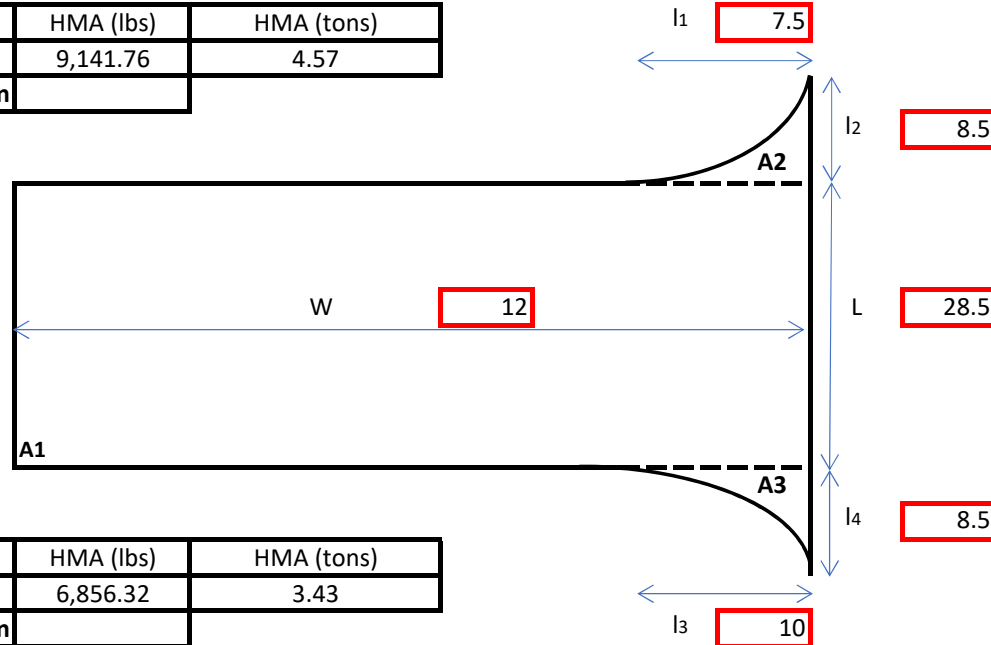

MDOT 5E3	HMA (lbs)	HMA (tons)
165	6,856.32	3.43
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott

DATE:

REVIEWED BY:

DATE:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 7/21/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 18 of 21

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Moran	Carpenter	North Side	10	29.5	7	8	7.5	8
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
319.9	35.55	295.0	12.0	12.9				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	7,820.76	3.91
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	29.5
SYD	6.56

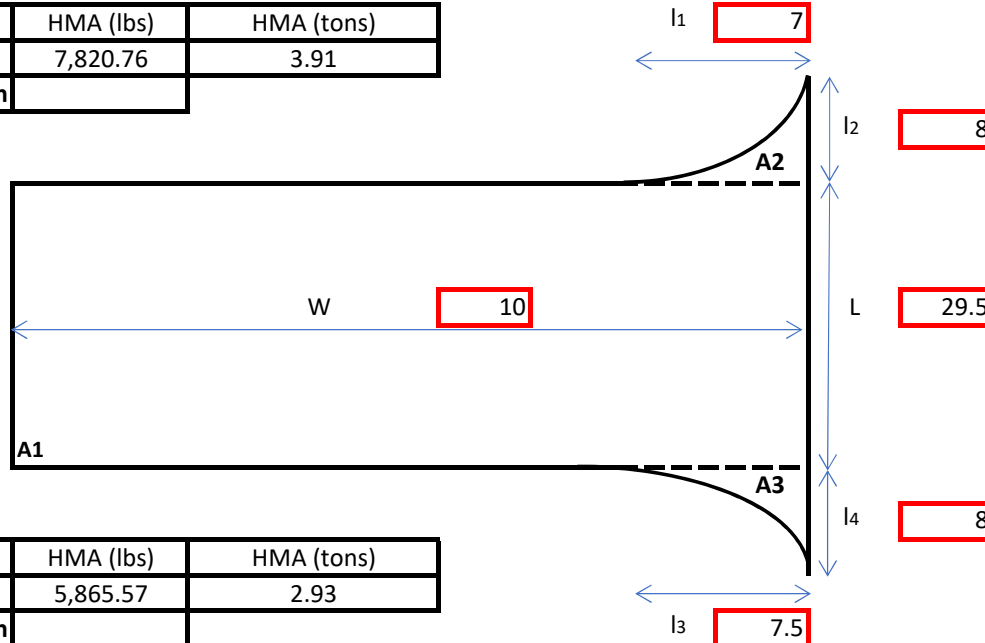

MDOT 5E3	HMA (lbs)	HMA (tons)
165	5,865.57	2.93
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott

DATE:

REVIEWED BY:

DATE:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 7/21/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 19 of 21

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Moran	Carpenter	South Side	12	28	4.5	4.5	7	8
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
352.4	39.15	336.0	4.4	12.0				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	8,614.07	4.31
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	28.0
SYD	6.22

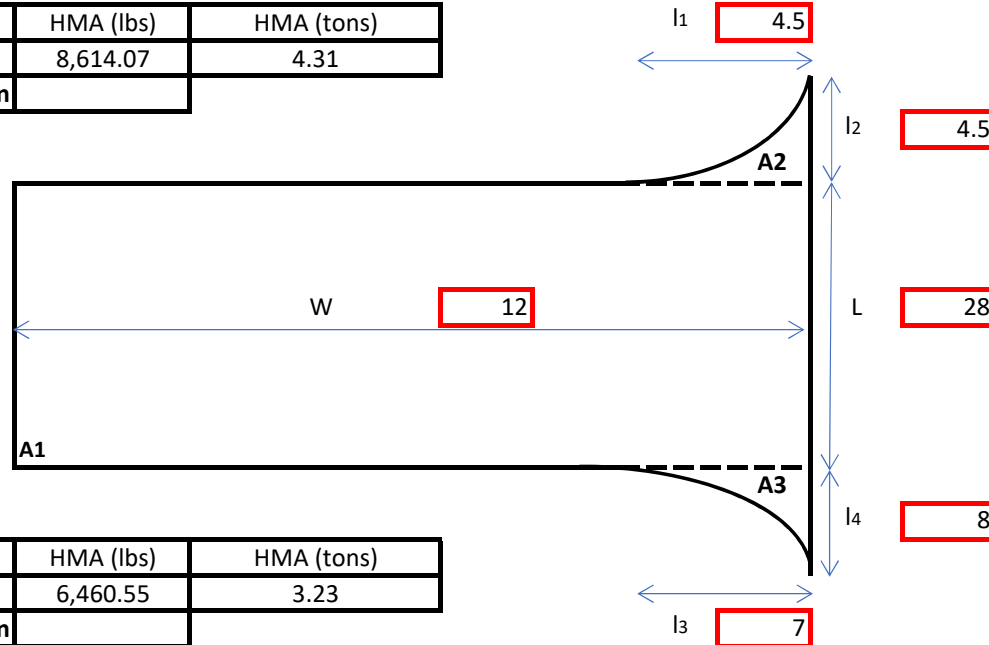

MDOT 5E3	HMA (lbs)	HMA (tons)
165	6,460.55	3.23
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott

DATE:

REVIEWED BY:

DATE:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 7/21/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 20 of 21

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Sobieski	Carpenter	South Side	13.5	28	7	5	8	7
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
397.6	44.17	378.0	7.5	12.0				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	9,718.26	4.86
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	28.0
SYD	6.22

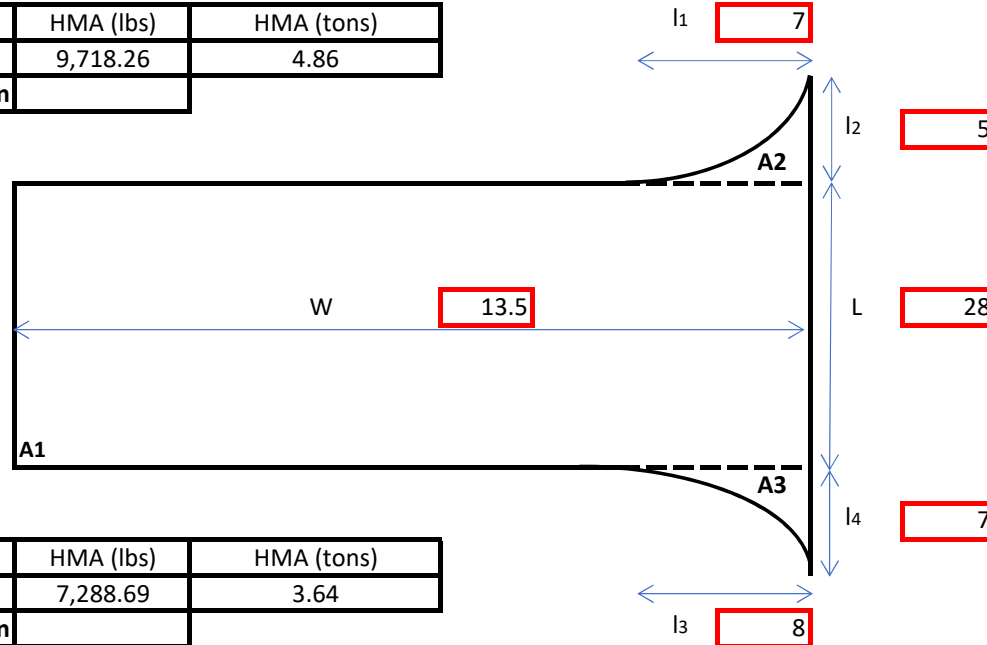

MDOT 5E3	HMA (lbs)	HMA (tons)
165	7,288.69	3.64
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott

DATE:

REVIEWED BY:

DATE:
