



City of Detroit

Inspector's Daily Report

7/29/2020 4:31 PM

FieldManager 5.3c

Contract: _PW-7018, City of Detroit Resurfacing 2020

IDR Date 7/27/2020	Day of Week Monday	Seq. No. 1	Import Date 7/31/2020	Project Engineer Jim Petronski - WSP	Construction Engineer Abdul Siddiqui - City of Detroit
Inspector's Initials-Name DW Damian Welborne				Federal Project Number	Elec. Attachments None
Prime Contractor Fort Wayne Contracting / Ajax Paving Industries, a joint ven					
Entered By DW, Damian Welborne		Revised By		Revision Date	Revision No.
Temperatures Low: 77 ° F High: 88 ° F		Weather Mostly Cloudy			

Comments

Wyoming Avenue from 6 Mile road to 8 Mile Road.

Ten Mile Creek (TMC), Superintendent Kourtney Glecklere.

6:00 AM - 4:00 PM

- TMC set up arrowboard and traffic cones along, and alerted owners so that vehicles had not to be towed from, northbound and southbound Wyoming Ave., from Outer Dr. to 8 Mile Rd.

- Along Wyoming Ave. TMC brushed the curbs, butt milled at the ROW limits of each intersecting street, butt milled the limits of the mainline section, milled the pavement of the mainline section, close milled around encountered structures, post brushed and post street-swept the milled work.

TOTAL - 17,408.60 SYD milled today.

Visitors:

- None approached, or sought after by, the writer.

Traffic:

- No incidents today.

Attachments:

- Wyoming Ave. Cold Milling Mainline sheet;
- Norfolk St. east side Cold Milling Approach sheet;
- Norfolk St. west side Cold Milling Approach sheet;
- Chipewa St. east side Cold Milling Approach sheet;
- Chipewa St. west side Cold Milling Approach sheet;
- Pembroke St. east side Cold Milling Approach sheet;
- - Note: Pembroke west side composed of existing concrete pavement;
- - Note: St. Martins St. ROW closed; and,
- St. Martins St. west side Cold Milling Approach sheet;

Covid-19 check: 97.3*f



Inspector's Daily Report

7/29/2020 4:31 PM

FieldManager 5.3c

Contractors

Contractor's Name	Personnel	No.	Hrs.	Equipment	No.	Hrs.
Tenmile Creek Excavating, LLC	Flagger	1	18.00	Broom, Superior DT74J	1	9.00
	Laborer	3	27.00	Miller, Wirtgon W220i	1	9.00
	Operator	5	45.00	Miller, Wirtgon W50Ri	1	9.00
	Operator (Progressive Sweep)	1	4.50	Mini Loader, Mustang 4000	1	9.00
	Superintendent (Kourtney)	1	9.00	Street Seeper, Elgin Bear (Progressive Sweep)	1	4.50
				Water Truck, Mack	2	18.00

Item Postings

Item/Material Description	Item Code	Prop. Line	Project	Category	Quantity	Unit	Location	Brkdwn ID	Attn
Cold Milling HMA Surface, Modified	_5017011	0280	PW-7018	0000	17,353.220	Syd	Wyoming Avenue from 6 Mile road to 8 Mile Road.		
Contractor: Ajax Paving Industries, Inc.									
Item Remarks: Wyoming Ave. from 8 Mile Rd. south side to Outer Dr. north side mainline with approaches.									
Pavt for Butt Joints, Rem	_501000	0240	PW-7018	0000	6.890	Syd	Wyoming Avenue from 6 Mile road to 8 Mile Road.		
Contractor: Fort Wayne Contracting / Ajax Paving Industries, a joint ven									
Item Remarks: Wyoming Ave. at Norfolk St. west side approach.									
Pavt for Butt Joints, Rem	_501000	0240	PW-7018	0000	8.220	Syd	Wyoming Avenue from 6 Mile road to 8 Mile Road.		
Contractor: Fort Wayne Contracting / Ajax Paving Industries, a joint ven									
Item Remarks: Wyoming Ave. at Pembroke St. east side approach.									
Pavt for Butt Joints, Rem	_501000	0240	PW-7018	0000	6.890	Syd	Wyoming Avenue from 6 Mile road to 8 Mile Road.		
Contractor: Fort Wayne Contracting / Ajax Paving Industries, a joint ven									
Item Remarks: Wyoming Ave. at Norfolk St. east side approach.									
Pavt for Butt Joints, Rem	_501000	0240	PW-7018	0000	6.890	Syd	Wyoming Avenue from 6 Mile road to 8 Mile Road.		
Contractor: Fort Wayne Contracting / Ajax Paving Industries, a joint ven									
Item Remarks: Wyoming Ave. at Chippewa St. west side approach.									
Pavt for Butt Joints, Rem	_501000	0240	PW-7018	0000	6.440	Syd	Wyoming Avenue from 6 Mile road to 8 Mile Road.		
Contractor: Fort Wayne Contracting / Ajax Paving Industries, a joint ven									
Item Remarks: Wyoming Ave. at St. Martins St. west side approach.									
Pavt for Butt Joints, Rem	_501000	0240	PW-7018	0000	6.670	Syd	Wyoming Avenue from 6 Mile road to 8 Mile Road.		
Contractor: Fort Wayne Contracting / Ajax Paving Industries, a joint ven									
Item Remarks: Wyoming Ave. at Chippewa St. east side approach.									
Pavt for Butt Joints, Rem	_501000	0240	PW-7018	0000	9.110	Syd	Wyoming Avenue from 6 Mile Road to 8 Mile Road.		
Contractor: Fort Wayne Contracting / Ajax Paving Industries, a joint ven									
Item Remarks: Wyoming Ave. at Outer Dr. end.									



City of Detroit

Inspector's Daily Report

7/29/2020 4:31 PM

FieldManager 5.3c

Item Postings

Item/Material Description	Item Code	Prop. Line	Project	Category	Quantity	Unit	Location	Brkdwn ID	Attn
Pavt for Butt Joints, Rem	_501000	0240	PW-7018	0000	9.110	Syd	Wyoming Avenue from 6 Mile Road to 8 Mile Road.		
Contractor: Fort Wayne Contracting / Ajax Paving Industries, a joint ven									
Item Remarks: Wyoming Ave. at 8 Mile Rd. end.									

Reviewed By: Carly Taylor Carly Taylor
Aug 17 2020 9:40 AM
(Signature)

(Date)



Cold Milling HMA Surface, Modified & Projected HMA Quantities

DATE: 20200727

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Industrial

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski

LOCATION: Wyoming Avenue, Detroit, MI

SHEETS: 1 of 1

Main Street	Wyoming Avenue	Street Width (ft)	Street Length (ft)	Mainline HMA (syd)	Area	Mix 4E3 @ 2 inches	Mix 5E3 @ 1.5 inches	PROJECTED HMA (lbs)	PROJECTED 4E3 HMA (tons)	PROJECTED HMA (lbs)	PROJECTED 5E3 HMA (tons)	Date of Completion
No. 1	Start End	North & South Bound 8 Mile to Outer Drive	41	3744.33	17,057.50	220	165	3752650.7	1876.3	2,814,488.1	1,407.24	
No. 2	Start End				0.00	220	165	0.0	0.0	0.0	0.00	
No. 3	Start End				0.00	220	165	0.0	0.0	0.0	0.00	
No. 4	Start End				0.00	220	165	0.0	0.0	0.0	0.00	
No. 5	Start End				0.00	220	165	0.0	0.0	0.0	0.00	
No.	Start End				0.00	220	165	0.0	0.0	0.0	0.00	
No.	Start End				0.00	220	165	0.0	0.0	0.0	0.00	
No.	Start End				0.00	220	165	0.0	0.0	0.0	0.00	
No.	Start End				0.00	220	165	0.0	0.0	0.0	0.00	
No.	Start End				0.00	0		0.0	0.0	0.0	0.00	
No.	Start End				0.00	0		0.0	0.0	0.0	0.00	
No.	Start End				0.00	0		0.0	0.0	0.0	0.00	
No.	Start End				0.00	0		0.0	0.0	0.0	0.00	
Today Total Quantities				17,057.50				3,752,650.7	1,876.3	2,814,488.1	1,407.24	

FIELD INSPECTOR: D. Welborne

DATE: 2020 07 27

REVIEWED BY:

DATE:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: _____

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: _____

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Chippewa	Wyoming	East Side	11	30	12.75	12	11.5	8
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
382.7	42.52	330.0	32.9	19.8				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	30.0
SYD	6.67

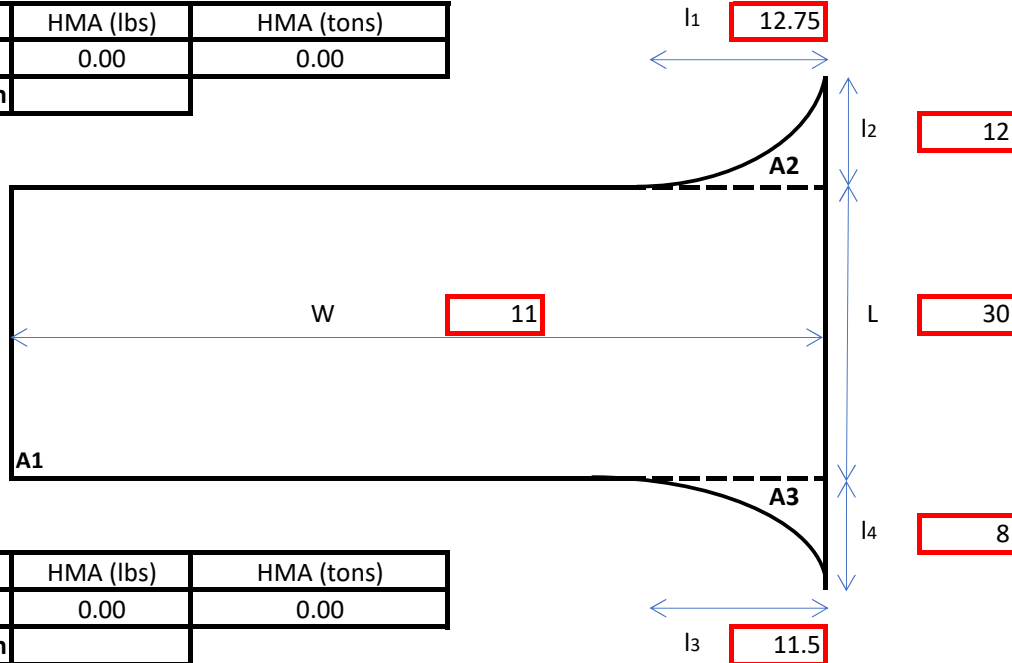

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: _____
REVIEWED BY: _____

DATE: _____
DATE: _____

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: _____

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: _____

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Chippewa	Wyoming	West Side	13	31	9	10	12	10
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
448.2	49.79	403.0	19.4	25.8				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	31.0
SYD	6.89

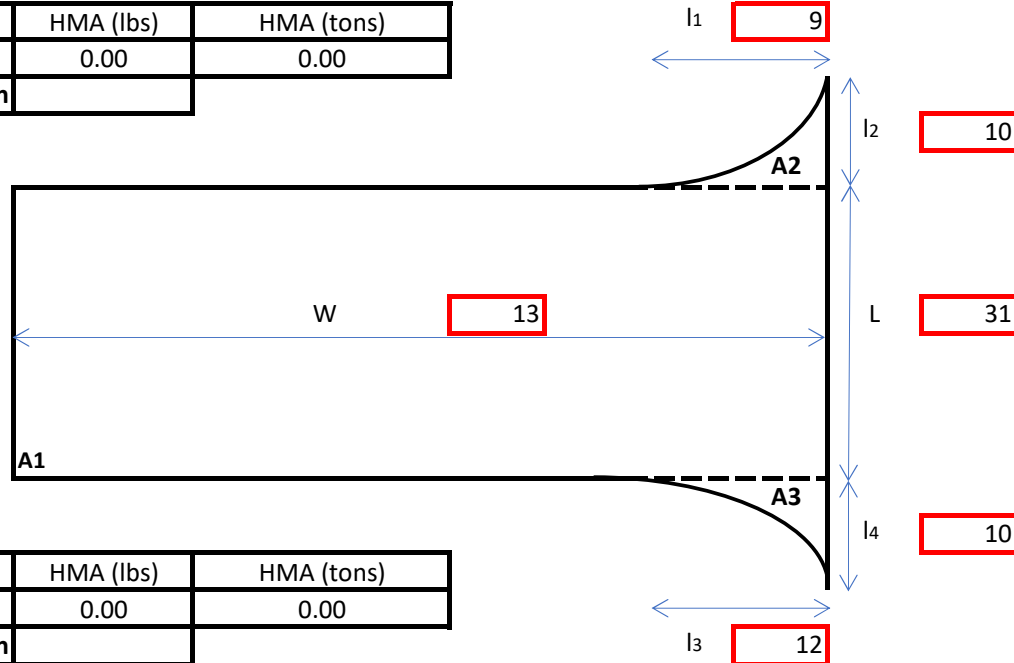

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: _____
REVIEWED BY: _____

DATE: _____
DATE: _____

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: _____

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: _____

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Norfolk	Wyoming	East Side	10.5	31	12	11.5	11.5	10.5
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
381.1	42.35	325.5	29.7	26.0				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	31.0
SYD	6.89

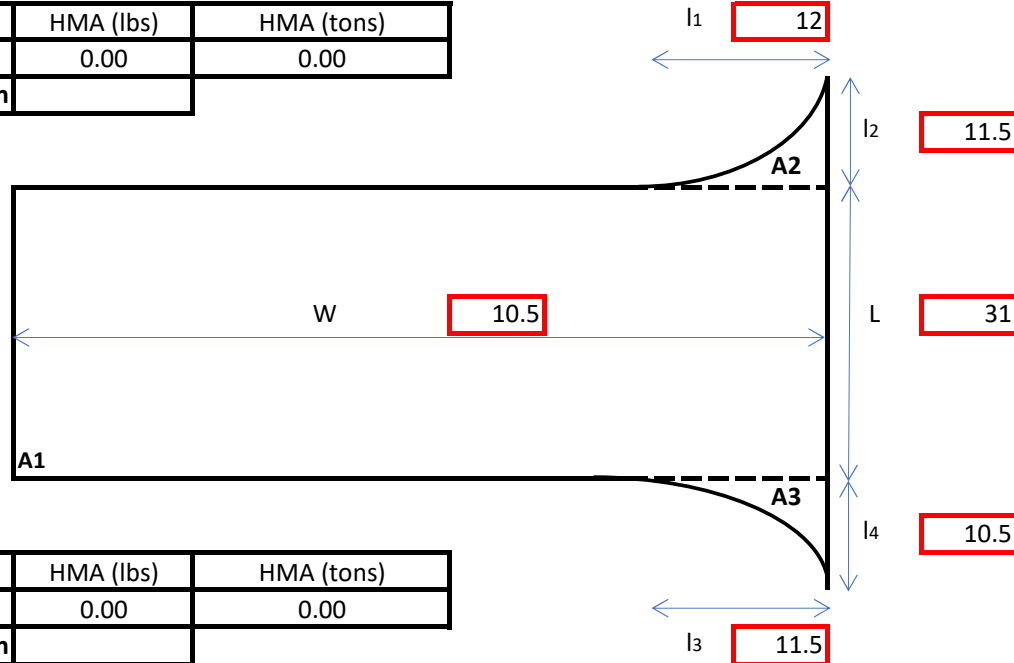

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: _____
REVIEWED BY: _____

DATE: _____
DATE: _____

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: _____

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: _____

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Norfolk	Wyoming	West Side	10.5	31	10	9.5	12.5	11
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
375.5	41.72	325.5	20.4	29.6				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	31.0
SYD	6.89

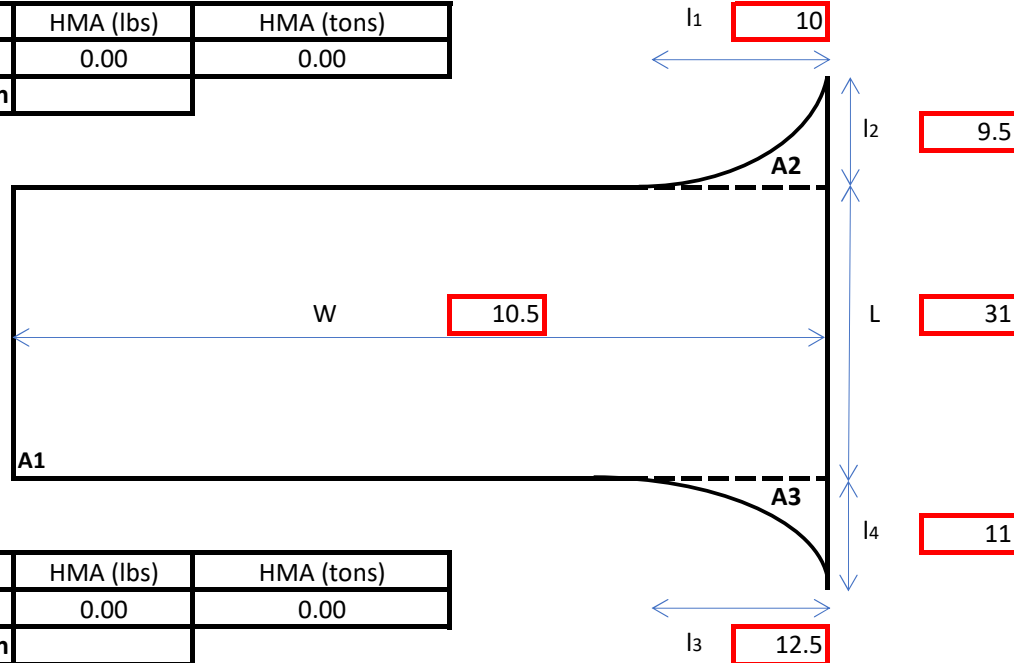

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: _____
REVIEWED BY: _____

DATE: _____
DATE: _____

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: _____

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: _____

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Pembroke	Wyoming	East Side	11.5	37	13.5	12.5	12	9
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
485.0	53.89	425.5	36.3	23.2				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	37.0
SYD	8.22

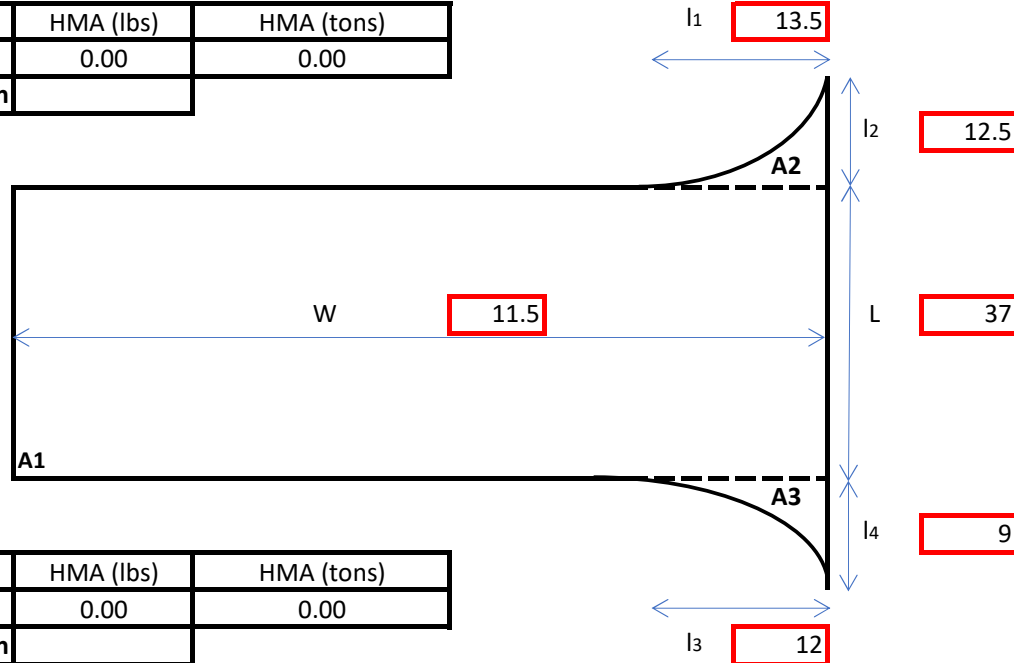

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: _____
REVIEWED BY: _____

DATE: _____
DATE: _____

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: _____

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: _____

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
St. Martins	Wyoming	West Side	39	29	0	0	0	0
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)				
		1131.0	0.0	0.0	Location No.: A1			
1,131.0	125.67							

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	29.0
SYD	6.44

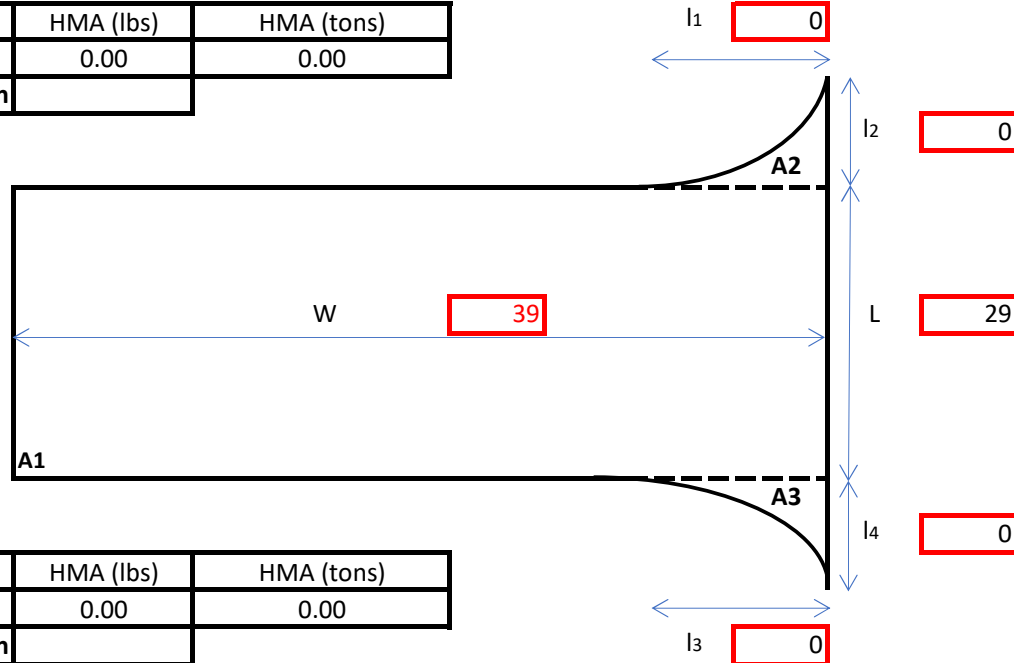

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: D. Welborne

REVIEWED BY: _____

DATE: 2020 07 27

DATE: _____
