



City of Detroit

Inspector's Daily Report

7/29/2020 4:31 PM

FieldManager 5.3c

Contract: _PW-7018, City of Detroit Resurfacing 2020

IDR Date 7/28/2020	Day of Week Tuesday	Seq. No. 1	Import Date 7/31/2020	Project Engineer Jim Petronski - WSP	Construction Engineer Abdul Siddiqui - City of Detroit
Inspector's Initials-Name DW Damian Welborne				Federal Project Number	Elec. Attachments None
Prime Contractor Fort Wayne Contracting / Ajax Paving Industries, a joint ven					
Entered By DW, Damian Welborne		Revised By		Revision Date	Revision No.
Temperatures Low: 68 ° F High: 86 ° F		Weather Sunny			

Comments

Wyoming Avenue from 6 Mile road to 8 Mile Road.

Ten Mile Creek (TMC), Superintendent Kaurtney Glecklere.

6:00 AM - 1:30 PM

- TMC set up arrowboard and traffic cones along, and alerted owners so that vehicles had not to be towed from, northbound and southbound Wyoming Ave., from Margareta St. to 7 Mile Rd. and from 7 Mile Rd. to Outer Dr.

- Along Wyoming Ave. TMC brushed the curbs, butt milled at the ROW limits of each intersecting street, butt milled the limits of the mainline section at the northern end, milled the pavement of the mainline section, close milled around encountered structures, post brushed and post street-swept the milled work.

TOTAL - 6,399.08 SYD milled today.

Visitors:

- None approached, or sought after by, the writer.

Traffic:

- No incidents today.

Attachments:

- Wyoming Ave. Cold Milling Mainline sheet;
- Cambridge St east side Cold Milling Approach sheet;
- - Note: Cambridge west side approach composed of existing concrete pavement;
- Clarita St. east side Cold Milling Approach sheet;
- Clarita St. west side Cold Milling Approach sheet;
- Margareta St. east side Cold Milling Approach sheet; and,
- Margareta St. west side Cold Milling Approach sheet

Covid-19 check: 97.3*f



Inspector's Daily Report

7/29/2020 4:31 PM

FieldManager 5.3c

Contractors

Contractor's Name	Personnel	No.	Hrs.	Equipment	No.	Hrs.
Tenmile Creek Excavating, LLC	Flagger	2	16.00	Broom, Superior DT74J	1	8.00
	Laborer	3	24.00	Miller, Wirtgon W220i	1	8.00
	Operator	5	40.00	Miller, Wirtgon W50Ri	1	8.00
	Operator (Progressive Sweep)	1	4.00	Mini Loader, Mustang 4000	1	8.00
	Superintendent (Kaurtney)	1	8.00	Street Seeper, Elgin Bear (Progressive Sweep)	1	4.00
				Water Truck, Mack	2	16.00

Item Postings

Item/Material Description	Item Code	Prop. Line	Project	Category	Quantity	Unit	Location	Brkdwn ID	Attn
Cold Milling HMA Surface, Modified	_50170110280	PW-7018		0000	6,370.630	Syd	Wyoming Avenue from 6 Mile Road to 8 Mile Road.		
Contractor: Tenmile Creek Excavating, LLC									
Item Remarks: Wyoming Ave. from Outer Dr. south side to 7 Mile Rd. northside mainline with approaches.									
Cold Milling HMA Surface, Modified	_50170110280	PW-7018		0000	7,280.930	Syd	Wyoming Avenue from 6 Mile Road to 8 Mile Road.		
Contractor: Tenmile Creek Excavating, LLC									
Item Remarks: Wyoming Ave. from 7 Mile Rd. south side to Margarete St. south side mainline with approaches.									
Pavt for Butt Joints, Rem	_501000£ 0240	PW-7018		0000	12.440	Syd	Wyoming Avenue from 6 Mile Road to 8 Mile Road.		
Contractor: Fort Wayne Contracting / Ajax Paving Industries, a joint ven									
Item Remarks: Wyoming Ave. at 7 Mile Rd. north side approach.									
Pavt for Butt Joints, Rem	_501000£ 0240	PW-7018		0000	6.890	Syd	Wyoming Avenue from 6 Mile Road to 8 Mile Road.		
Contractor: Fort Wayne Contracting / Ajax Paving Industries, a joint ven									
Item Remarks: Wyoming Ave. at Cambridge St. east side approach.									
Pavt for Butt Joints, Rem	_501000£ 0240	PW-7018		0000	12.220	Syd	Wyoming Avenue from 6 Mile Road to 8 Mile Road.		
Contractor: Fort Wayne Contracting / Ajax Paving Industries, a joint ven									
Item Remarks: Wyoming Ave. at 7 Mile Rd. south side approach.									
Pavt for Butt Joints, Rem	_501000£ 0240	PW-7018		0000	6.440	Syd	Wyoming Avenue from 6 Mile Road to 8 Mile Road.		
Contractor: Fort Wayne Contracting / Ajax Paving Industries, a joint ven									
Item Remarks: Wyoming Ave. at Clarita St. east side approach.									
Pavt for Butt Joints, Rem	_501000£ 0240	PW-7018		0000	6.220	Syd	Wyoming Avenue from 6 Mile Road to 8 Mile Road.		
Contractor: Fort Wayne Contracting / Ajax Paving Industries, a joint ven									
Item Remarks: Wyoming Ave. at Margareta St. east side approach.									
Pavt for Butt Joints, Rem	_501000£ 0240	PW-7018		0000	9.110	Syd	Wyoming Avenue from 6 Mile Road to 8 Mile Road.		
Contractor: Fort Wayne Contracting / Ajax Paving Industries, a joint ven									
Item Remarks: Wyoming Ave. at Outer Drive south side approach.									



City of Detroit

Inspector's Daily Report

7/29/2020 4:31 PM

FieldManager 5.3c

Item Postings

Item/Material Description	Item Code	Prop. Line	Project	Category	Quantity	Unit	Location	Brkdwn ID	Attn
Pavt for Butt Joints, Rem Contractor: Fort Wayne Contracting / Ajax Paving Industries, a joint ven Item Remarks: Wyoming Ave. at Clarita St. east side approach.	_501000	0240	PW-7018	0000	6.440	Syd	Wyoming Avenue from 6 Mile Road to 8 Mile Road.		
Pavt for Butt Joints, Rem Contractor: Fort Wayne Contracting / Ajax Paving Industries, a joint ven Item Remarks: Wyoming Ave. at Margareta St. west side approach.	_501000	0240	PW-7018	0000	6.440	Syd	Wyoming Avenue from 6 Mile Road to 8 Mile Road.		

Reviewed By: Carly Taylor Carly Taylor
Aug 17 2020 9:44 AM
(Signature)

(Date)



Cold Milling HMA Surface, Modified & Projected HMA Quantities

DATE: 20200728

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Industrial

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski

LOCATION: Wyoming Avenue, Detroit, MI

SHEETS: 1 of 1

Main Street	Wyoming Avenue	Street Width (ft)	Street Length (ft)	Mainline HMA (syd)	Area	Mix 4E3 @ 2 inches	Mix 5E3 @ 1.5 inches	PROJECTED HMA (lbs)	PROJECTED 4E3 HMA (tons)	PROJECTED HMA (lbs)	PROJECTED 5E3 HMA (tons)	Date of Completion
No. 1	Start End	North & South Bound Outer Drive to Cambridge	41	631	2,874.56	220	165	632402.2	316.2	474,301.7	237.15	
No. 2	Start End	North & South Bound Outer Drive to Rite Aid	41	365	1,662.78	220	165	365811.1	182.9	274,358.3	137.18	
No. 3	Start End	North & South Bound Outer Drive to Rite Aid	15	365	608.33	220	165	133833.3	66.9	100,375.0	50.19	
No. 4	Start End	North & South Bound Rite Aid to 7 Mile n	56	193	1,200.89	220	165	264195.6	132.1	198,146.7	99.07	
No. 5	Start End	North & South Bound 7 Mile s to Bus Stop	55	192	1,173.33	220	165	258133.3	129.1	193,600.0	96.80	
No.	Start End	North & South Bound Bus Stop to Harvest Chch	9	273	273.00	220	165	60060.0	30.0	45,045.0	22.52	
No.	Start End	North & South Bound Bus Stop to Harvest Chch	46	273	1,395.33	220	165	306973.3	153.5	230,230.0	115.12	
No.	Start End	North & South Bound Harvest Chch to Margareta s	46	830	4,242.22	220	165	933288.9	466.6	699,966.7	349.98	
No.	Start End				0.00	220	165	0.0	0.0	0.0	0.00	
No.	Start End				0.00	0		0.0	0.0	0.0	0.00	
No.	Start End				0.00	0		0.0	0.0	0.0	0.00	
No.	Start End				0.00	0		0.0	0.0	0.0	0.00	
No.	Start End				0.00	0		0.0	0.0	0.0	0.00	
Today Total Quantities				13,430.44				2,954,697.8	1,477.3	2,216,023.3	1,108.01	

FIELD INSPECTOR: D. Welborne

DATE: 2020 07 28

REVIEWED BY:

DATE:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: _____

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: _____

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Cambridge	Wyoming	East Side	13	31	13	13	13.5	11.5
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
472.7	52.52	403.0	36.3	33.4				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	31.0
SYD	6.89

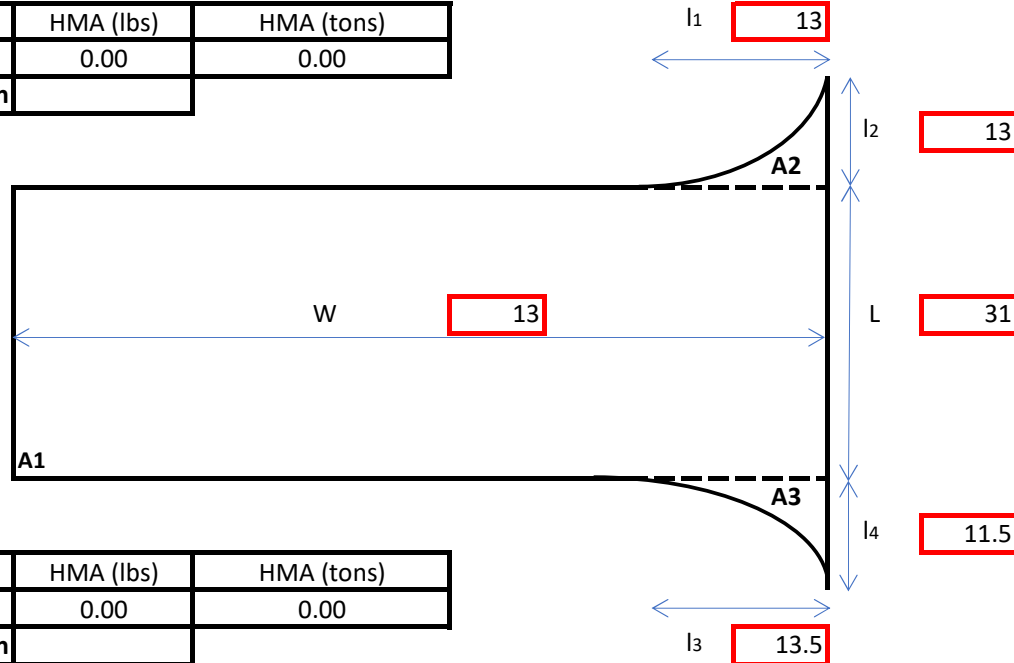

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: _____
REVIEWED BY: _____

DATE: _____
DATE: _____

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: _____

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: _____

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Clarita	Wyoming	East Side	11.5	29	6	5.5	9.5	5.5
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
351.8	39.09	333.5	7.1	11.2				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	29.0
SYD	6.44

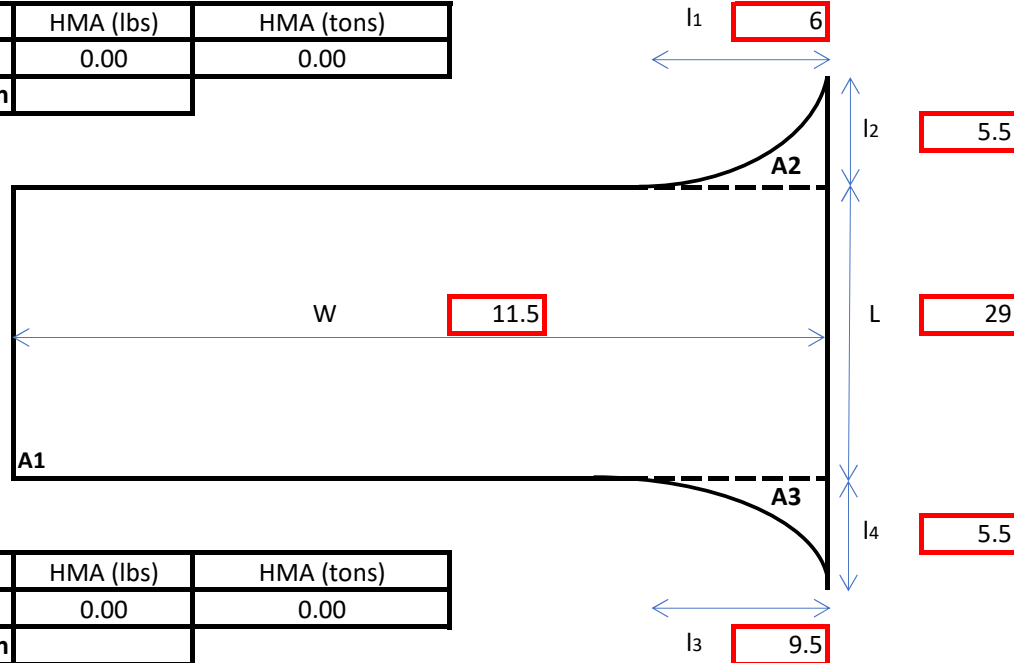

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: _____
REVIEWED BY: _____

DATE: _____
DATE: _____

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: _____

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: _____

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Clarita	Wyoming	West Side	20.5	29	6	6.5	9	9
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
620.3	68.92	594.5	8.4	17.4				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	29.0
SYD	6.44

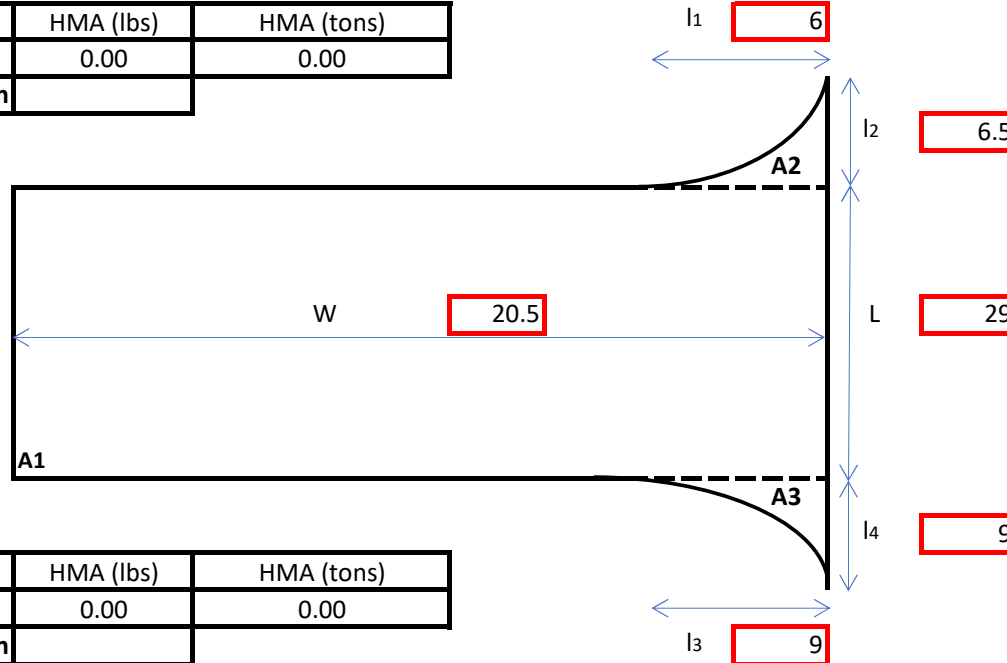

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: _____
REVIEWED BY: _____

DATE: _____
DATE: _____

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: _____

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: _____

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Margaretta	Wyoming	East Side	19	28	8	7.75	11.75	7.5
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
564.3	62.70	532.0	13.3	18.9				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	28.0
SYD	6.22

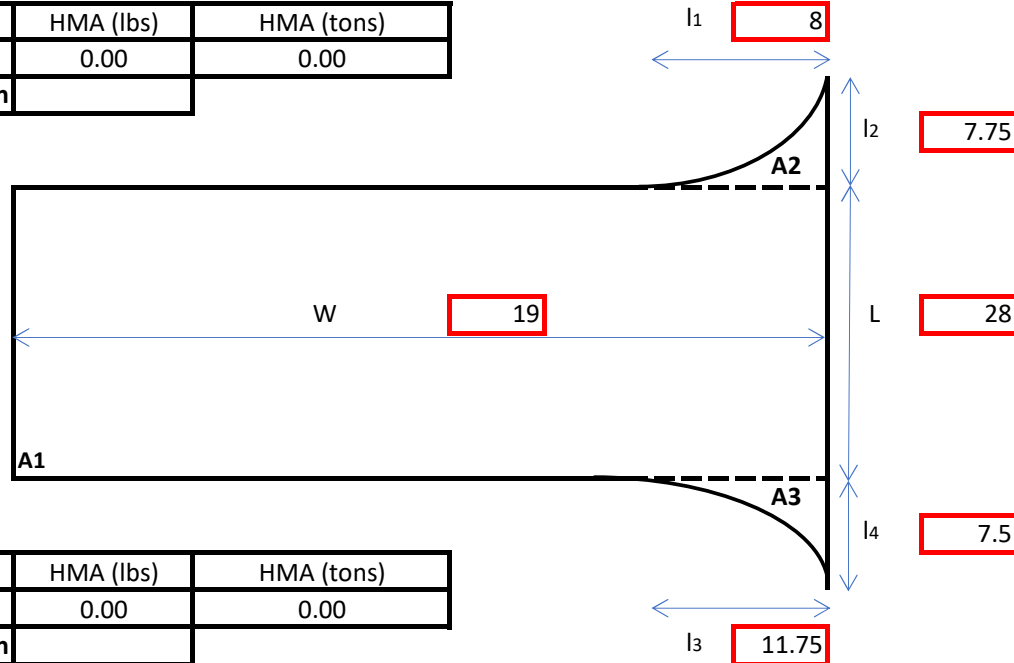

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: _____
REVIEWED BY: _____

DATE: _____
DATE: _____

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: _____

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: _____

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Margaretta	Wyoming	West Side	19.5	29	5	5	5	5.5
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
576.8	64.09	565.5	5.4	5.9				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	29.0
SYD	6.44

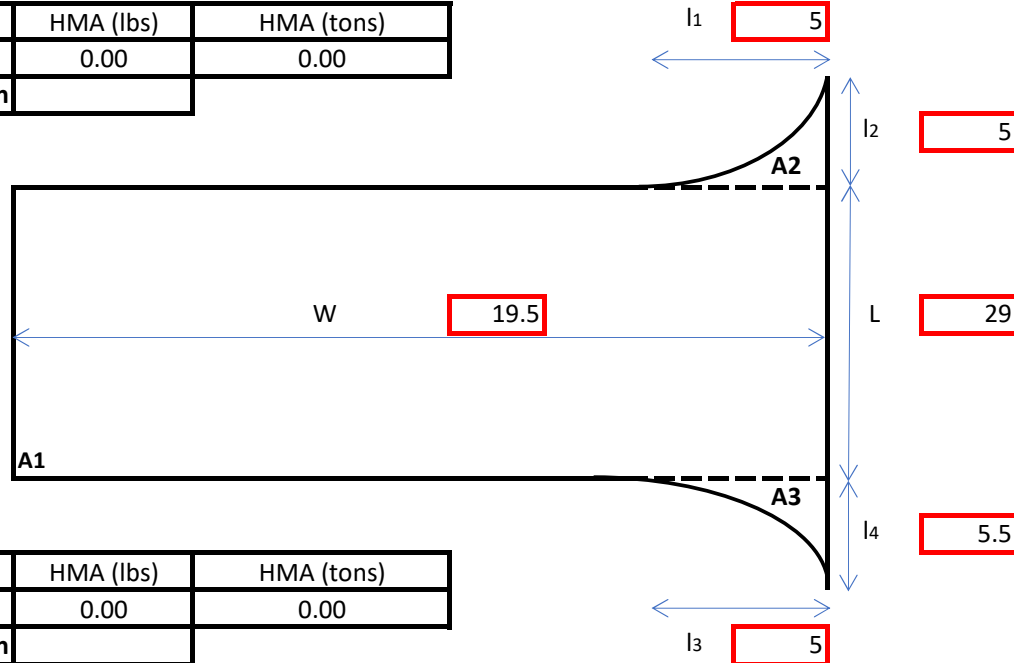

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: _____
REVIEWED BY: _____

DATE: _____
DATE: _____
