



City of Detroit

Inspector's Daily Report

8/4/2020 10:36 AM

FieldManager 5.3c

Contract: _PW-7018, City of Detroit Resurfacing 2020

IDR Date 8/3/2020	Day of Week Monday	Seq. No. 1	Import Date 8/6/2020	Project Engineer Jim Petronski - WSP	Construction Engineer Abdul Siddiqui - City of Detroit
Inspector's Initials-Name LE Lenoris Elliott				Federal Project Number	Elec. Attachments None
Prime Contractor Fort Wayne Contracting / Ajax Paving Industries, a joint ven					
Entered By LE, Lenoris Elliott		Revised By		Revision Date	Revision No.
Temperatures Low: 64 ° F High: 85 ° F		Weather Partly Cloudy			



Inspector's Daily Report

8/4/2020 10:36 AM

FieldManager 5.3c

Comments

STREET LOCATION: Wyoming from McNichols to 8 Mile Road

CONTRACTOR ONSITE:

Ajax Paving Industries
Municipal Sweeping

CONTRACTOR ACTIVITIES:

Ajax Paving Industries: (Site Time 6:00AM to 3:00PM)
Municipal Sweeping: (Site Time 6:00AM to 3:00PM)

The contractor's continued the PW-7018 City of Detroit Resurfacing Project by power sweeping and a total of 142 gallons of the Bond Coat – Emulsified Asphalt Product SS-1H was applied on the existing base course. The application was applied by jet spray on the side street approaches. The contractor placed 167.24 tons of HMA MDOT 4E3 mix from the Ajax Paving Industries Plant No. 7 (Sherwood) in Warren, Michigan. A Caterpillar Paver AP1055F was utilized to place the HMA for the side street approaches in a loose layer ranging from 1.75 to 2.25 inches in thickness and with random depth checks performed by the Somat inspector. To achieve the project density requirements, the compaction operation was performed by using a series of steel drum tandem vibratory rollers. Several in-place HMA temperatures were measured. Refer to the attached Cold Milling HMA Surface, Modified & Projected HMA Quantities for related data and other specific information.

APPROACH LOCATIONS:

Cambridge East Side
Chippewa East Side
Chippewa West Side
Clarita East Side
Clarita West Side
Curtis East Side
Curtis West Side
Margareta East Side
Margareta West Side
Norfolk East Side
Norfolk West Side
Pembroke East Side
Pickford East Side
Pickford West Side
Santa Clara East Side
Santa Clara West Side
Santa Maria East Side
St. Martins East Side
Thatcher East Side

MATERIAL TESTING:

Certified HMA technicians from Ajax Paving Industries and Somat were onsite to perform QC/QA HMA sampling and in-place density testing. The certified technicians informed the inspector that the HMA field test results have met the JMF design in-place density requirements as specified in the project contract/plans and specification.

TRAFFIC CONTROL:

Traffic Control is in place per the proposal, using lighted arrow boards, barrels, and signs.

ATTACHMENTS:

Cold Milling HMA Surface, Modified & Projected HMA Quantities Report

COVID 19 ONSITE TESTING:

Kobi Smith (WSP) performed a body temperature reading by using an infrared temperature gun on myself and reading measured at 96.8 Fahrenheit.



Inspector's Daily Report

8/4/2020 10:36 AM

FieldManager 5.3c

Contractors

Contractor's Name	Personnel	No.	Hrs.	Equipment	No.	Hrs.
Ajax Paving Industries, Inc.	Flagger	5	9.00	Cat 430F Backhoe #M1074	1	9.00
	Labour	4	9.00	Cat AP1055F Paver #AP93	1	9.00
	Operator	5	9.00	Cat CB13 Roller #7066	1	9.00
	Superintendent	1	9.00	Cat CB36B Roller #7075	1	9.00
				Cat CB54 Roller #7033	1	9.00
				Ford Truck - Arrow Board #2044	1	9.00
				GMC Utility Truck #2033	1	9.00
				Low Boy	1	9.00
				Municipal Sweeping	1	9.00
				Peterbilt Tack Truck #9002	1	9.00
				Peterbilt Utility Truck #2089	1	9.00
				Peterbilt Water Truck #9018	1	9.00
				Pickup Truck #1117	1	9.00
				Pickup Truck #1148	1	9.00
				Rubber Tire Trailer #X312	1	9.00
				Tractor Broom Sweeper #M1587	1	9.00

Item Postings

Item/Material Description	Item Code	Prop. Line	Project	Category	Quantity	Unit	Location	Brkdwn ID	Attn
_ HMA Approach, Modified, Adj Contractor: Ajax Paving Industries, Inc.					167.240	Ton	Wyoming from McNichols to 8 Mile		
Bond Coat, Emulsified Asphalt SS-1H					142.00	Gal			
HMA, 4E3					167.24	Ton			
Lighted Arrow, Type C, Furn Contractor: Fort Wayne Contracting / Ajax Paving Industries, a joint ven					0.000 1	Ea	Wyoming from McNichols to 8 Mile		
Arrow Board, Lighted					1.00	Ea			
Lighted Arrow, Type C, Oper Contractor: Fort Wayne Contracting / Ajax Paving Industries, a joint ven					1.000	Ea	Wyoming from McNichols to 8 Mile		

Reviewed By: Carly Taylor Carly Taylor
 Aug 31 2020 12:04 PM
 (Signature)

(Date)

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 8/3/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 1 OF 19

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Cambridge	Wyoming	East Side	15	31	13	13	13.5	11.5
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
534.7	59.41	465.0	36.3	33.4				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	13,070.78	6.54
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	
SYD	0.00

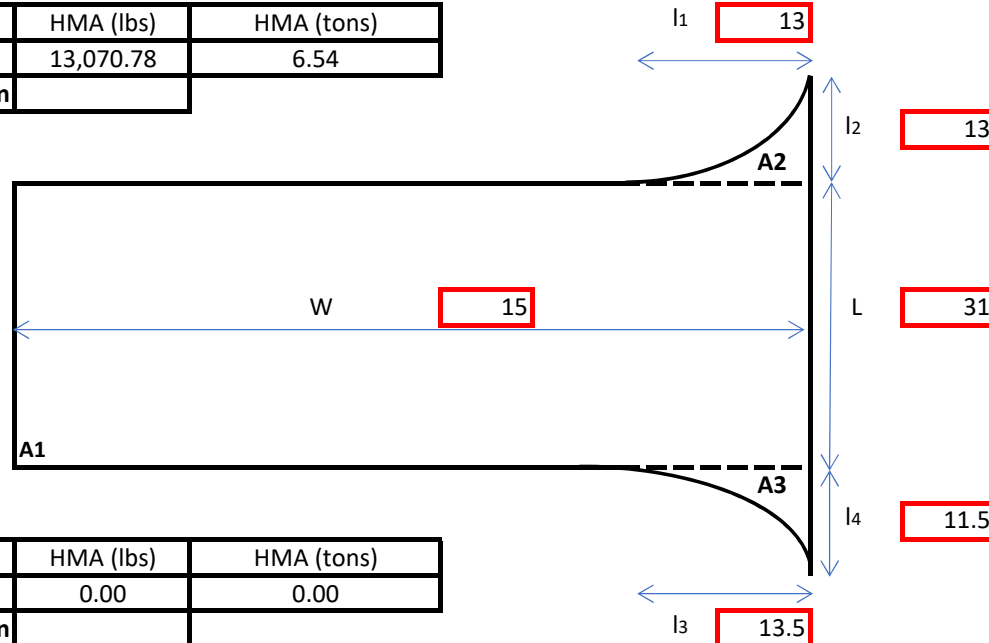

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

DATE: 8/3/2020

REVIEWED BY:

DATE:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 8/3/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 2 OF 19

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Chippewa	Wyoming	East Side	13	30	12.75	12	11.5	8
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
442.7	49.19	390.0	32.9	19.8				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	10,820.94	5.41
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	
SYD	0.00

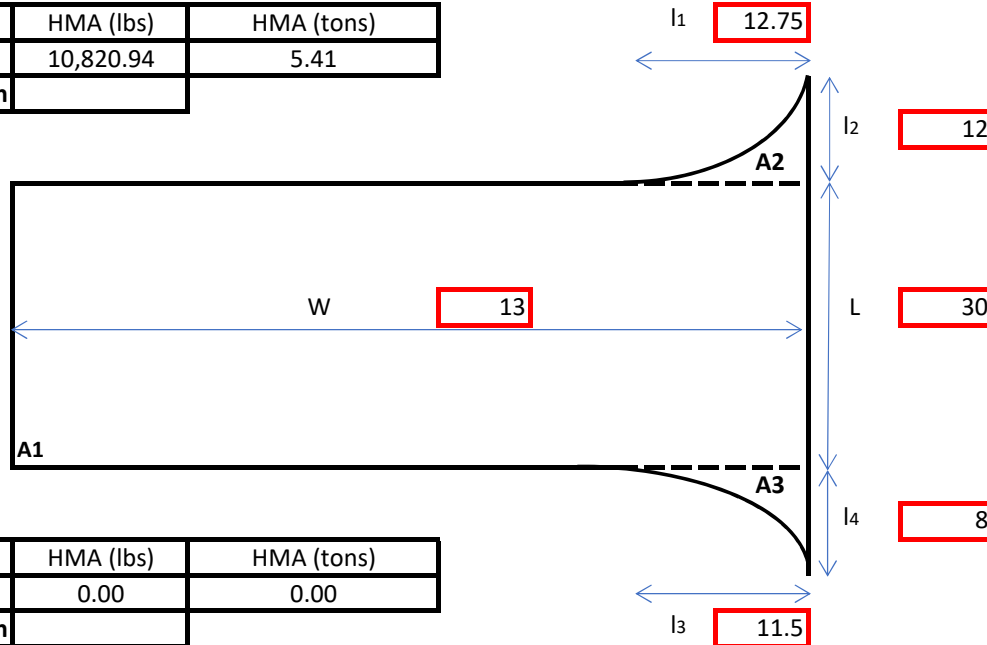

MDOT 5E3	HMA (lbs)	HMA (tons)
0.00	0.00	0.00
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

DATE: 8/3/2020

REVIEWED BY:

DATE:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 8/3/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 3 OF 19

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Chippewa	Wyoming	West Side	15	31	9	10	12	10
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
510.2	56.68	465.0	19.4	25.8				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	
SYD	0.00

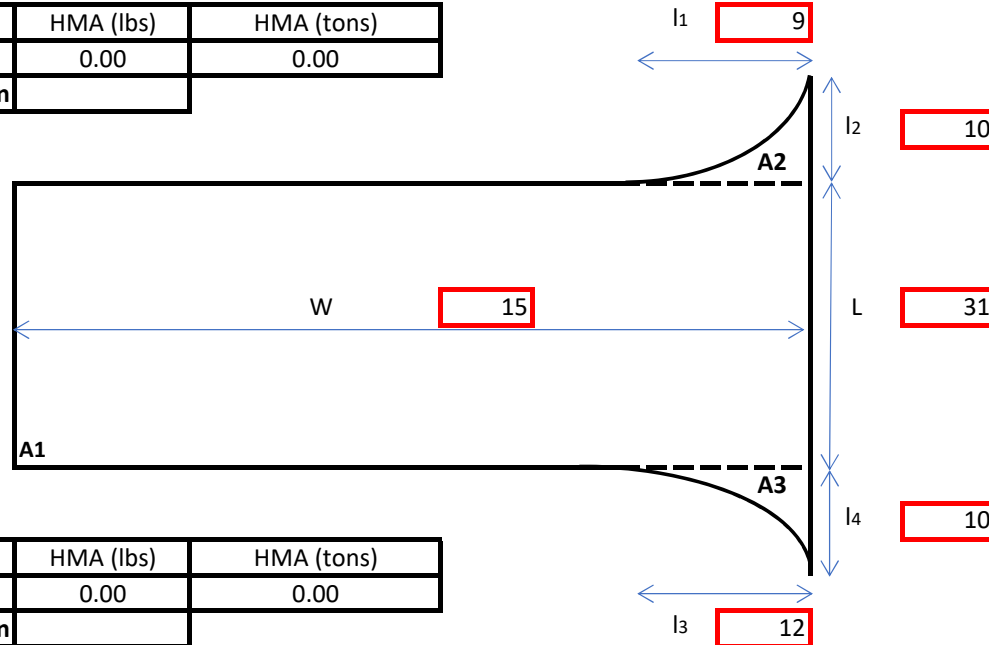

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

DATE: 8/3/2020

REVIEWED BY:

DATE:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 8/3/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 4 OF 19

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Clarita	Wyoming	East Side	13.5	29	6	5.5	9.5	5.5
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
409.8	45.54	391.5	7.1	11.2				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	10,018.04	5.01
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	
SYD	0.00

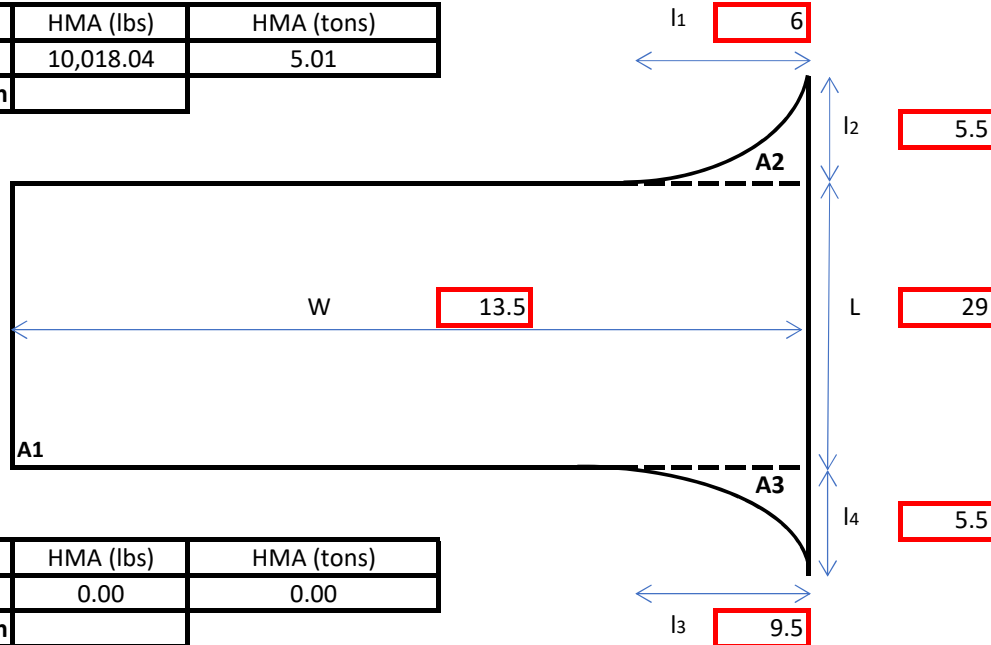

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

DATE: 8/3/2020

REVIEWED BY: _____

DATE: _____

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 8/3/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 5 OF 19

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Clarita	Wyoming	West Side	22.5	29	6	6.5	9	9
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
678.3	75.37	652.5	8.4	17.4				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	16,580.67	8.29
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	
SYD	0.00

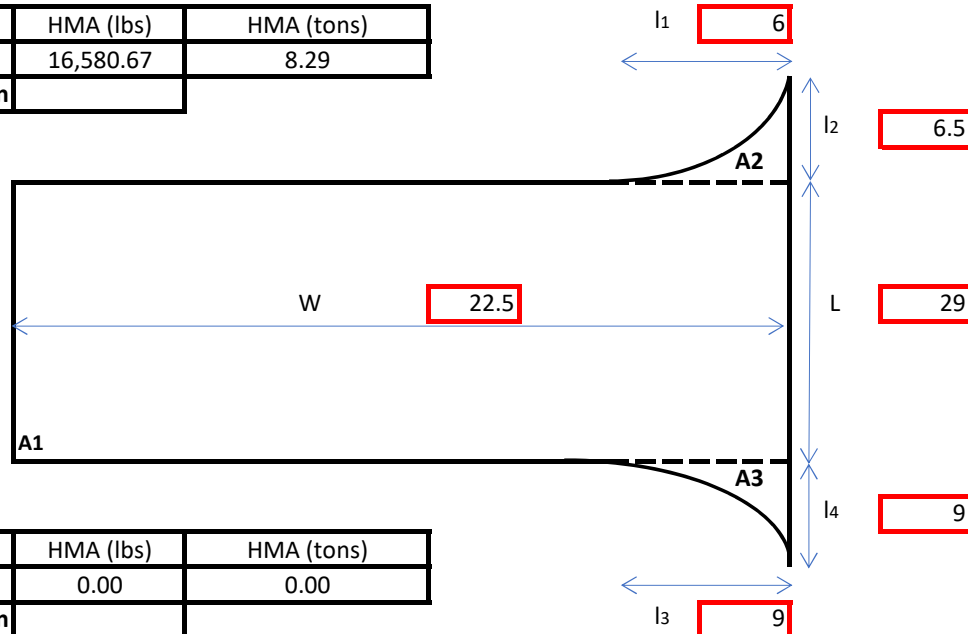

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

DATE: 8/3/2020

REVIEWED BY:

DATE:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 8/3/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 6 OF 19

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Curtis	Wyoming	East Side	36.5	36	8	8	8	6.5
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
1,338.9	148.77	1314.0	13.8	11.2				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	32,729.64	16.36
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	
SYD	0.00

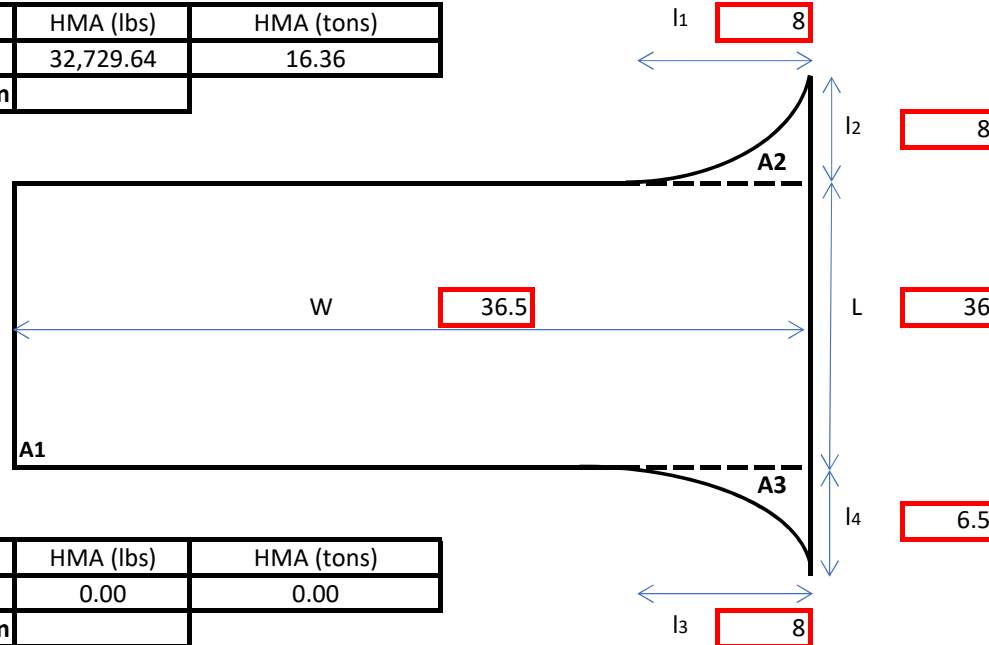

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

DATE: 8/3/2020

REVIEWED BY: _____

DATE: _____

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 8/3/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 7 OF 19

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Curtis	Wyoming	West Side	19	40	11	9	16	12
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
822.6	91.40	760.0	21.3	41.3				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	20,107.14	10.05
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	
SYD	0.00

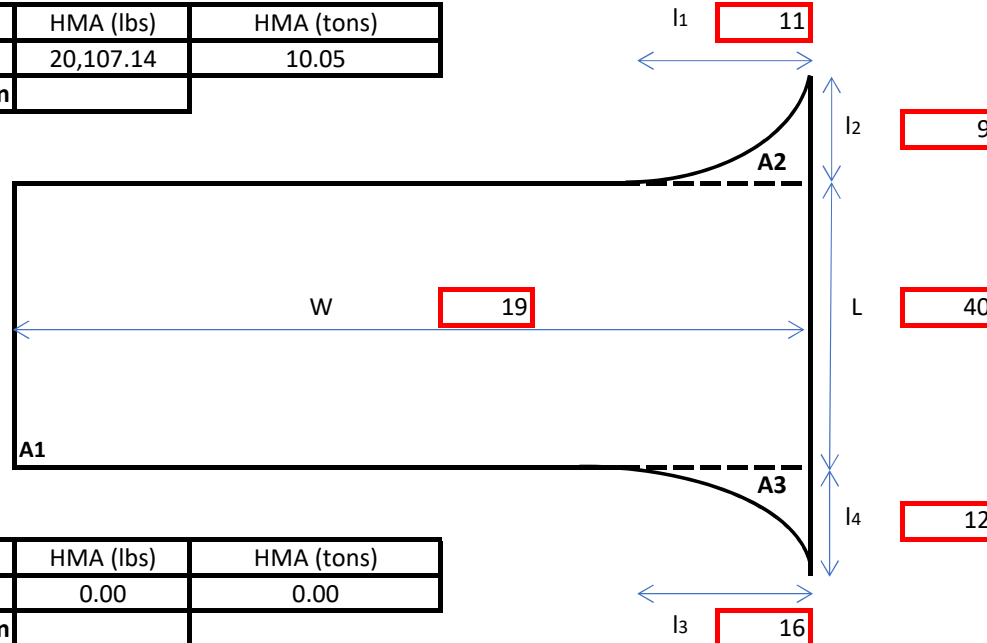

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

DATE: 8/3/2020

DATE:

REVIEWED BY:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 8/3/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 8 OF 19

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Margaretta	Wyoming	East Side	21	28	8	7.75	11.75	7.5
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
620.3	68.92	588.0	13.3	18.9				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	15,162.32	7.58
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	
SYD	0.00

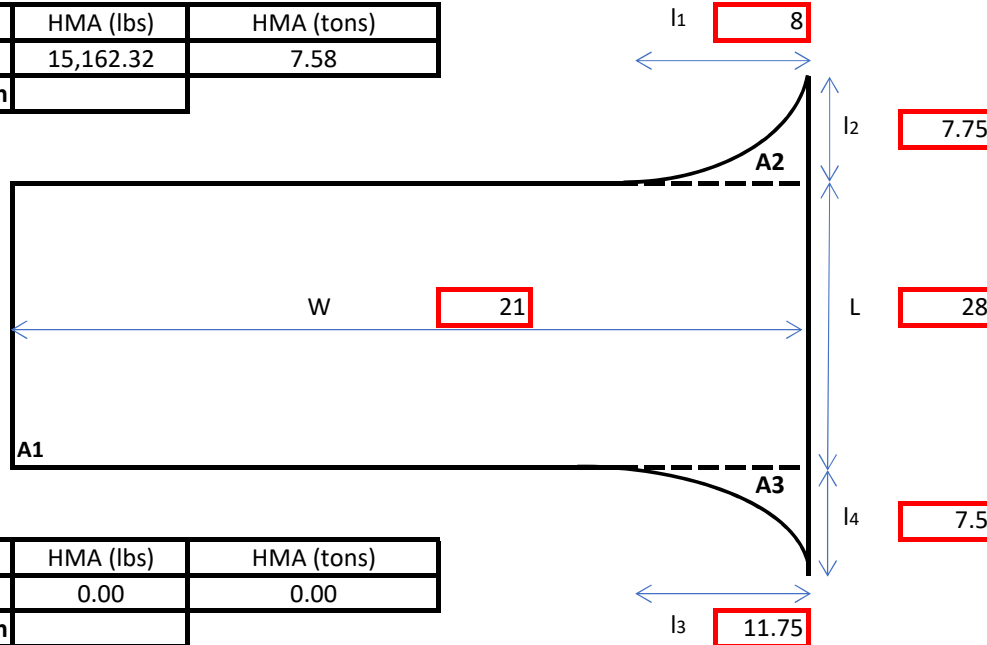

MDOT 5E3	HMA (lbs)	HMA (tons)
0.00	0.00	0.00
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

DATE: 8/3/2020

DATE:

REVIEWED BY:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 8/3/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 9 OF 19

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Margaretta	Wyoming	West Side	21.5	29	5	5	5	5.5
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
634.8	70.53	623.5	5.4	5.9				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	15,517.03	7.76
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	
SYD	0.00

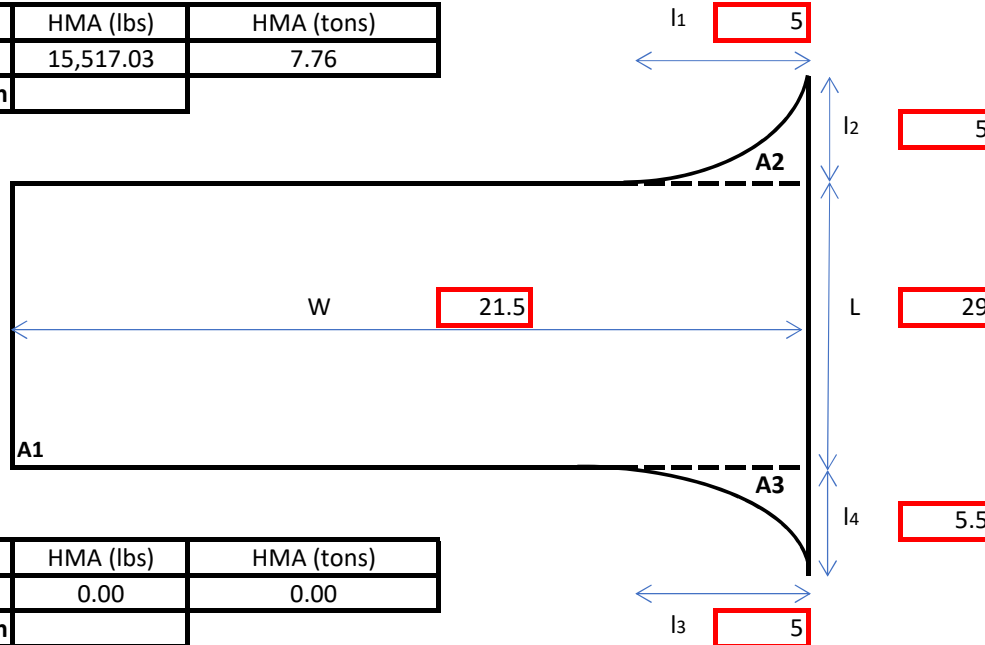

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

DATE: 8/3/2020

DATE:

REVIEWED BY:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 8/3/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 10 OF 19

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Norfolk	Wyoming	East Side	12.5	31	12	11.5	11.5	10.5
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
443.1	49.24	387.5	29.7	26.0				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	10,832.10	5.42
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	
SYD	0.00

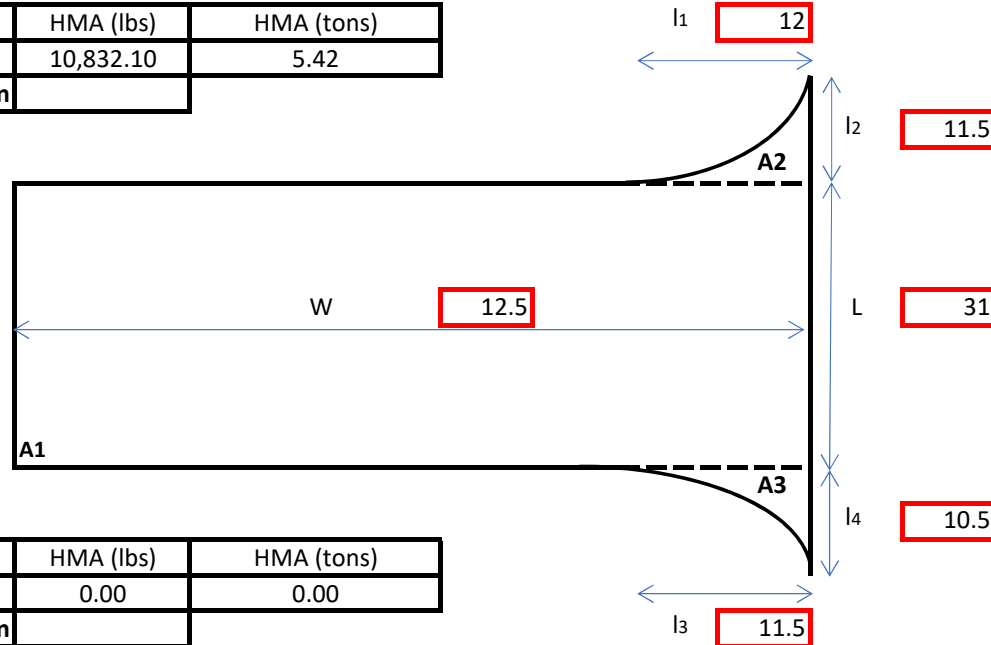

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

DATE: 8/3/2020

DATE:

REVIEWED BY:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 8/3/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 11 OF 19

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Norfolk	Wyoming	West Side	12.5	31	10	9.5	12.5	11
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
437.5	48.61	387.5	20.4	29.6				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	10,694.14	5.35
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	
SYD	0.00

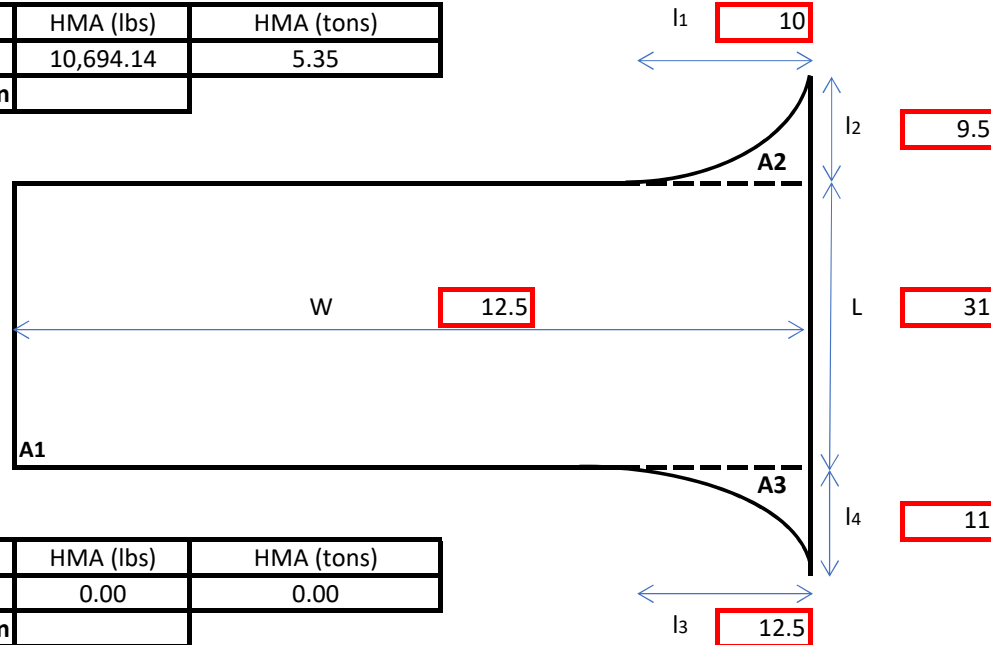

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

DATE: 8/3/2020

DATE:

REVIEWED BY:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 8/3/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 12 OF 19

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Pembroke	Wyoming	East Side	13.5	37	13.5	12.5	12	9
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
559.0	62.11	499.5	36.3	23.2				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	13,664.48	6.83
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	
SYD	0.00

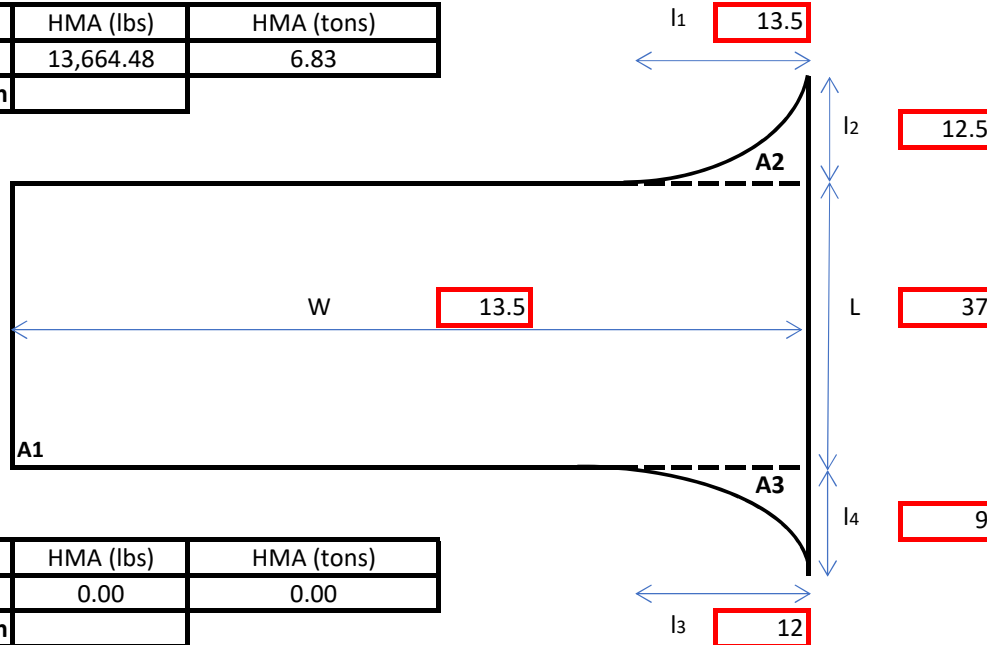

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

DATE: 8/3/2020

REVIEWED BY:

DATE:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 8/3/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 13 OF 19

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Pickford	Wyoming	East Side	22.5	29	7.5	5.9	7.25	7
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
672.9	74.77	652.5	9.5	10.9				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	16,449.28	8.22
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	
SYD	0.00

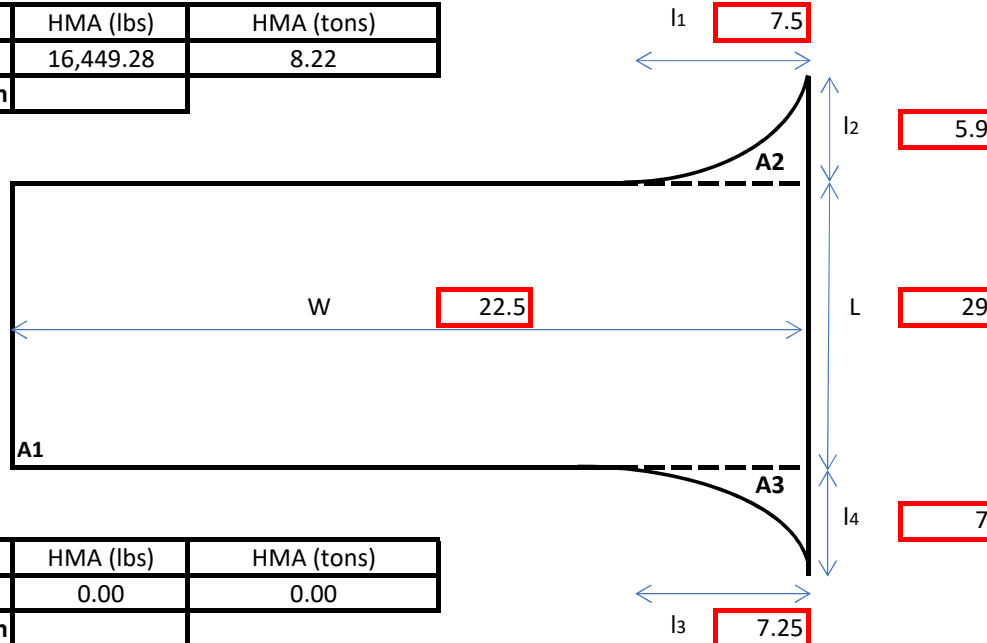

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

DATE: 8/3/2020

REVIEWED BY:

DATE:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 8/3/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 14 OF 19

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Pickford	Wyoming	West Side	26.5	31	5.5	5.5	8	8
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
841.8	93.53	821.5	6.5	13.8				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	20,576.45	10.29
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	
SYD	0.00

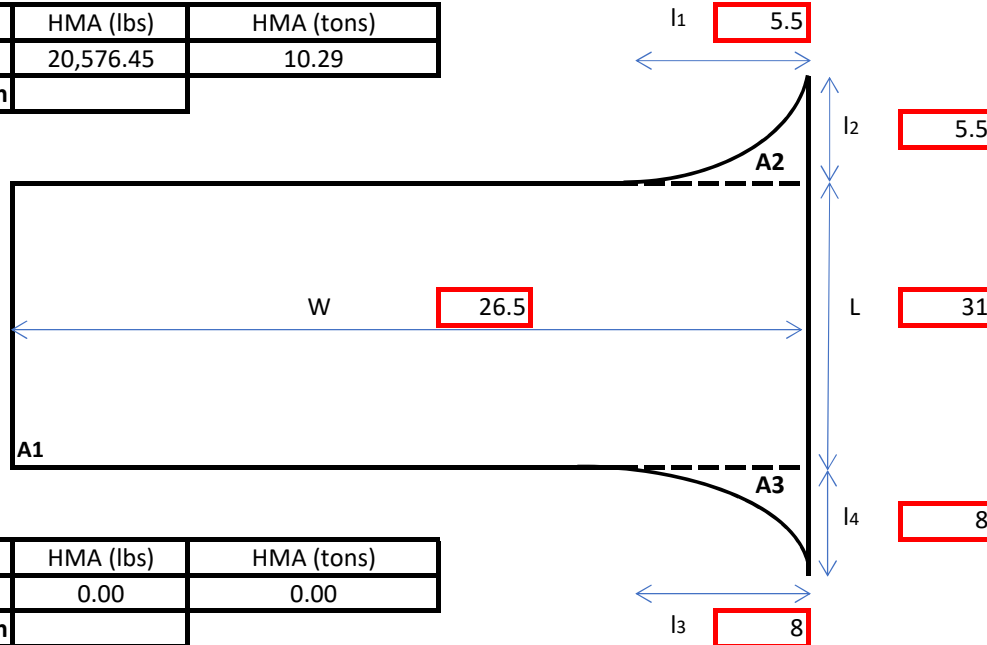

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

DATE: 8/3/2020

REVIEWED BY:

DATE:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 8/3/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 15 OF 19

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Santa Clara	Wyoming	East Side	27	29	6.8	6	8.9	5
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
801.3	89.04	783.0	8.8	9.6				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	19,588.30	9.79
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	
SYD	0.00

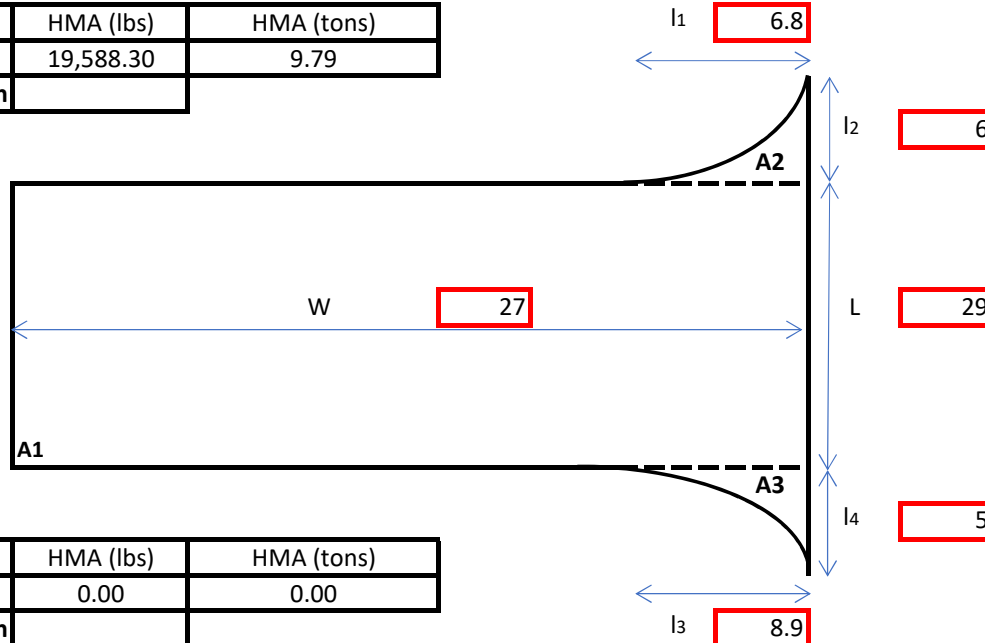

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

DATE: 8/3/2020

DATE:

REVIEWED BY:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 8/3/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 16 OF 19

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Santa Clara	Wyoming	West Side	14	30	7	5.9	8	7
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
440.9	48.99	420.0	8.9	12.0				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	10,778.03	5.39
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	
SYD	0.00

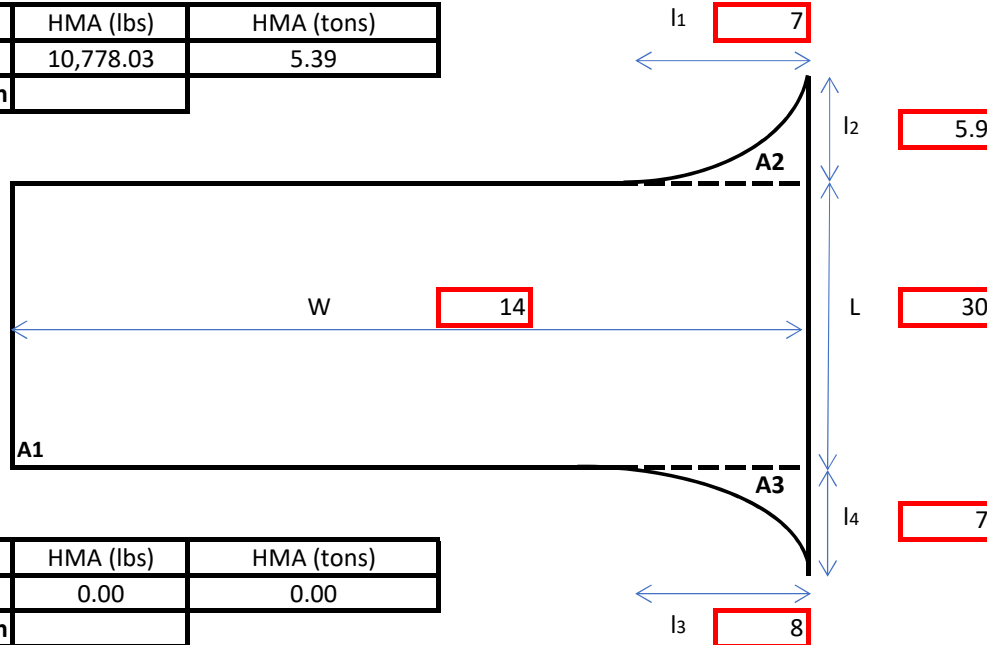

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

DATE: 8/3/2020

DATE:

REVIEWED BY:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 8/3/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 17 OF 19

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Santa Maria	Wyoming	East Side	20	29	7	5.7	7.8	6
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
598.6	66.52	580.0	8.6	10.1				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	14,633.43	7.32
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	
SYD	0.00

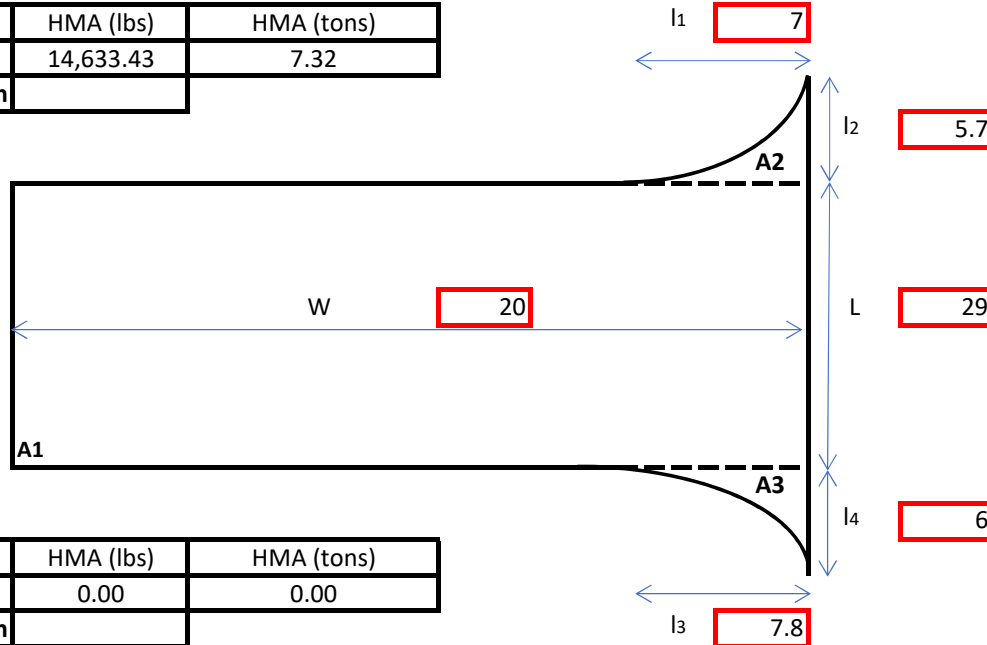

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

DATE: 8/3/2020

DATE:

REVIEWED BY:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 8/3/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 18 OF 19

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
St. Martins	Wyoming	West Side	41	29	0	0	0	0
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
1,189.0	132.11	1189.0	0.0	0.0				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	29,064.44	14.53
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	
SYD	0.00

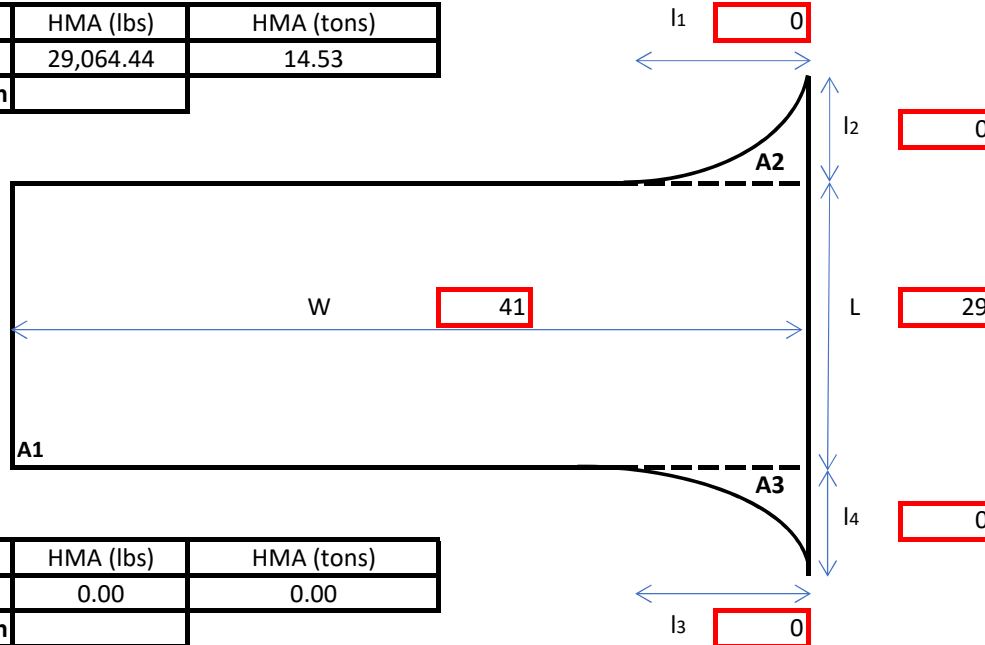

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

DATE: 8/3/2020

DATE:

REVIEWED BY:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 8/3/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 19 OF 19

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Thatcher	Wyoming	East Side	11	28	9	5.5	8	6.9
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
330.5	36.72	308.0	10.6	11.9				

MDOT 4E3	HMA (lbs)	HMA (tons)
220	8,079.15	4.04
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	
SYD	0.00

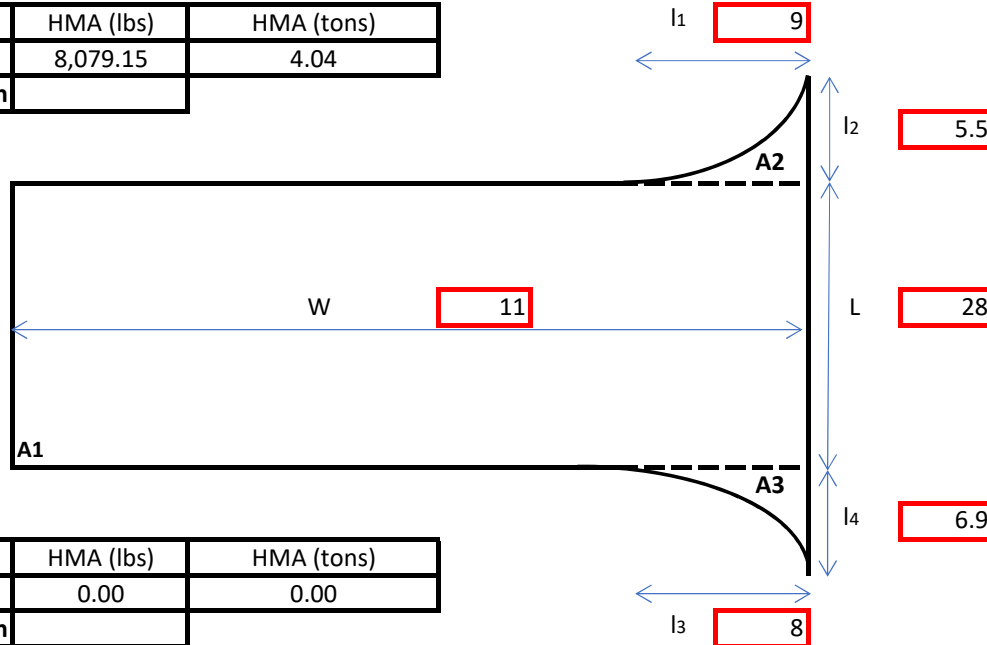

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

DATE: 8/3/2020

DATE:

REVIEWED BY:
