



City of Detroit

Inspector's Daily Report

8/5/2020 8:11 AM

FieldManager 5.3c

Contract: _PW-7018, City of Detroit Resurfacing 2020

IDR Date 8/4/2020	Day of Week Tuesday	Seq. No. 1	Import Date 8/6/2020	Project Engineer Jim Petronski - WSP	Construction Engineer Abdul Siddiqui - City of Detroit
Inspector's Initials-Name LE Lenoris Elliott				Federal Project Number	Elec. Attachments None
Prime Contractor Fort Wayne Contracting / Ajax Paving Industries, a joint ven					
Entered By LE, Lenoris Elliott		Revised By		Revision Date	Revision No.
Temperatures Low: 62 ° F High: 75 ° F		Weather Partly Cloudy			



Inspector's Daily Report

8/5/2020 8:11 AM

FieldManager 5.3c

Comments

STREET LOCATION: Tireman from Spinoza to Southfield SD

CONTRACTOR ONSITE:

Tenmile Creek Excavating (7:00AM to 1:00PM)

Progressive Sweeping (7:00AM to 1:00PM)

CONTRACTOR ACTIVITIES:

Tenmile Creek Excavating, cold milled the HMA surface on Tireman from Spinoza to Southfield Service Drive. Also, the side street approaches were milled at the following locations:

Brace at North & South Sides

Greenview at North & South Sides

Faust at North & South Sides

Penrod at North & South Sides

Rosemont at North & South Sides

Ashton at North & South Sides

The contractor milled the existing HMA surface in depths ranging from 3.25 to 3.75 inches, followed by power sweeping the milled surface. Somat was onsite for inspection and observation of the milling crew.

REMOVAL QUANTITIES:

Tireman Street at 8,991.11 SYD

Side Street approaches at 591.80 SYD

Butt Joints at 87.22 SYD

MATERIAL TESTING:

None

TRAFFIC CONTROL:

Traffic Control is in place per the proposal, using lighted arrow boards, barrels, and signs.

ATTACHMENTS:

Tireman Daily Summary Report

STREET LOCATION:

This writer laid out and marked the removal areas as needed for sidewalk, curb and approaches at following location:

- SB JC Lodge SD from Vassar to Keeler

POSTING ITEMS:

None

ATTACHMENTS:

None

COVID 19 ONSITE TESTING:

Kobi Smith (WSP) performed a body temperature reading by using an infrared temperature gun on myself and reading measured at 97.1 Fahrenheit.



City of Detroit

Inspector's Daily Report

8/5/2020 8:11 AM

FieldManager 5.3c

Contractors

Contractor's Name	Personnel	No.	Hrs.	Equipment	No.	Hrs.
Tenmile Creek Excavating, LLC	Labour	7	6.00	Chevy 3500HD Pickup Truck	1	6.00
	Operator	3	6.00	Chevy Pickup Truck (Duramax)	1	6.00
	Superintendent	1	6.00	Freightliner Truck (Water)	1	6.00
				Interstate Trailer 400LA	1	6.00
				John Deere 332G Skid Steer	1	6.00
				Kenworth Lowboy	1	6.00
				Mack Truck (Water)	1	6.00
				Rubber Tire Trailer #422	1	6.00
				Superior Broom Sweeper DT74J	1	6.00
				Wirtgen W220i Mill Machine	1	6.00
				Wirtgen W50i Mill Machine	1	6.00

Item Postings

Item/Material Description	Item Code	Prop. Line	Project	Category	Quantity	Unit	Location	Brkdwn ID	Attn
_ Cold Milling HMA Surface, Modified	_50170110280	PW-7018		0000	8,991.110	Syd	Tireman from Spinoza to Southfield Service Drive.		
Contractor: Tenmile Creek Excavating, LLC									
HMA Surface, Rem	_50100050230	PW-7018		0000	591.800	Syd	Tireman side street approaches from Spinoza to Southfield.		
Contractor: Tenmile Creek Excavating, LLC									
Brace at North & South Sides									
Greenvew at North & South Sides									
Faust at North & South Sides									
Penrod at North & South Sides									
Rosemont at North & South Sides									
Ashton at North & South Sides									



City of Detroit

Inspector's Daily Report

8/5/2020 8:11 AM

FieldManager 5.3c

Item Postings

Item/Material Description	Item Code	Prop. Line	Project	Category	Quantity	Unit	Location	Brkdwn ID	Attn
Pavt for Butt Joints, Rem Contractor: Tenmile Creek Excavating, LLC	_501000	0240	PW-7018	0000	87.220	Syd	Side street approaches. Brace at North & South Sides Greenview at North & South Sides Faust at North & South Sides Penrod at North & South Sides Rosemont at North & South Sides Ashton at North & South Sides Tireman at Southfield		

Reviewed By: Carly Taylor Carly Taylor
Aug 31 2020 12:05 PM
(Signature)

(Date)

Cold Milling HMA Approach Surface, Butt Joints Rem, Modified & Projected HMA Quantity

DATE: 8/4/2020	OWNER: City of Detroit
JOB NUMBER: PW-7018	CONTRACTOR: Ajax Paving Industries
PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020	PROJECT ENGINEER: Jim Petronski
LOCATION: Detroit, MI	SHEETS: 1 OF 1

TIREMAN from Stahelin to Southfield SD

Item Code 5010005 HMA Surface, Rem	
Surface Area (sft.)	5,326.21
Surface Area (syd.)	591.80
A1 (sft.)	4,814.00
A2 (sft.)	235.50
A3 (sft.)	276.71

Item Code 5010008 Pavt for Butt Joints, Rem	
Width (ft.)	2.00
Length (ft.)	392.50
SYD	87.22

Approaches Projected HMA 4E3	
HMA (lbs.)	0.00
HMA (tons)	0.00

Approaches Projected HMA 5E3	
HMA (lbs.)	0.00
HMA (tons)	0.00

Item Code 5017011 _Cold Milling HMA Surface, Modified					
Main Street		Tireman	Street Width (ft)	Street Length (ft)	Mainline HMA Area (syd)
No.1 End	Start End	Spinoza to Southfield Service Dr.	40.00	2023.00	8,991.11
MDOT MIXES			PROJECTED HMA (lbs)		PROJECTED HMA (tons)
Mix 4E3 @ 2"		220	0.00		0.00
Mix 5E3 @ 1.5"		165	0.00		0.00

Item Code _2040055 Sidewalk, Rem			Item Code _8027011 _Sidewalk, Conc, 4", Mod.	Item Code _8027012 _Sidewalk, Conc, 6", Mod.	Item Code _8037010 _Sidewalk, Conc, Tree Roots 4"	Item Code 8037011 _Sidewalk, Conc, Tree Roots 6"
	SYD's	SFT				
Rem.	0.00					
4 in.						
6 in.						
4"Root						
6"Root						

Item Code _2047002 _Curb, Rem, Mod.		Item Code _6037001 _Curb, Detail CD, Mod	Item Code _8030030 _Curb Ramp Open, Conc	Item Code _2047001 _Inter, Curb, Walk, 2ft Rem	Item Code 8037001 _Inter, Curb, Walk, 2ft Mod
	LFT				
Removal (ft)	0				
Curb, Conc, Detail CD (ft)					
Ramp Opening Curb (ft)					
2 ft Integral Rem. (ft)					
2 ft Integral (ft)					

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

REVIEWED BY:

DATE: 8/4/2020

DATE:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 8/4/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 1 OF 13

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Brace	Tireman	South Side	12	30	7.6	7.5	10.1	10.3
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
394.6	43.84	360.0	12.2	22.3				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	31.0
SYD	6.89

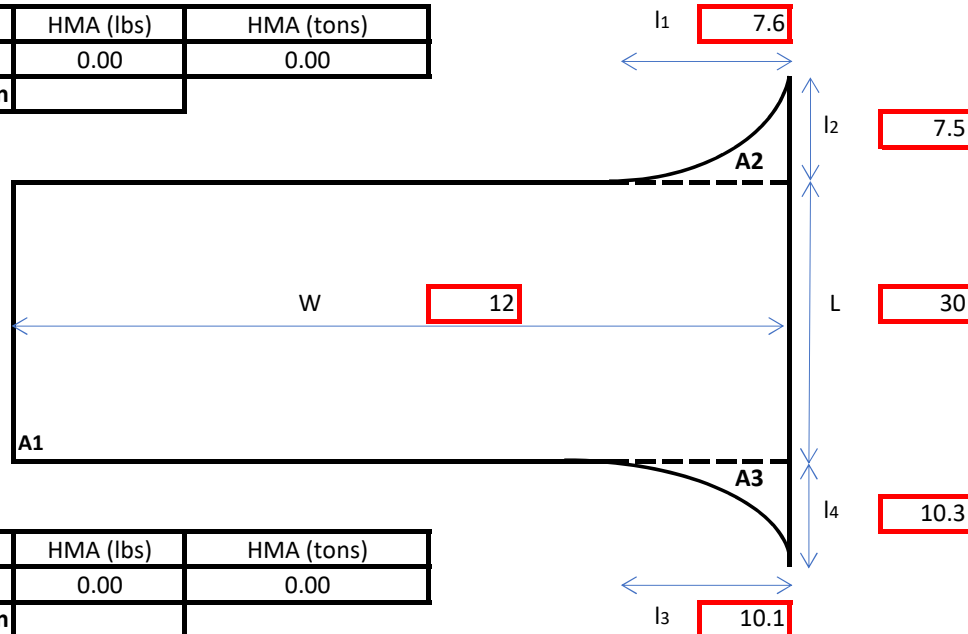

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

DATE: 8/4/2020

REVIEWED BY:

DATE:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 8/4/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 2 OF 13

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Greenview	Tireman	South Side	14	30	11	10	11.6	11.6
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
472.5	52.50	420.0	23.6	28.9				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	30.0
SYD	6.67

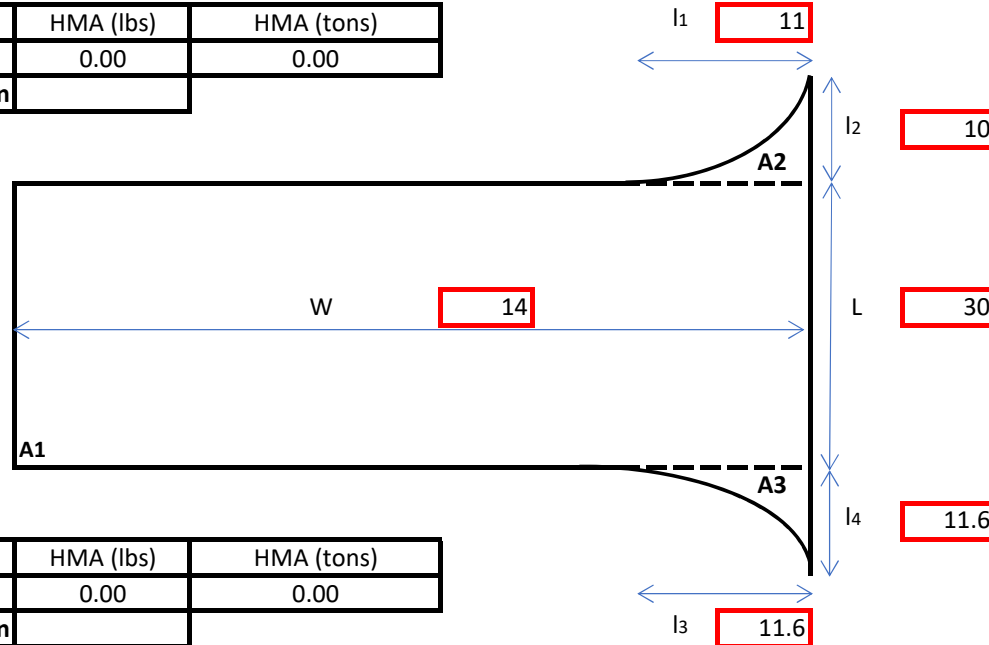

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

DATE: 8/4/2020

REVIEWED BY: _____

DATE: _____

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 8/4/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 3 OF 13

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Faust	Tireman	South Side	10	30	10	10.5	10.1	13.5
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
351.8	39.09	300.0	22.5	29.3				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	29.4
SYD	6.53

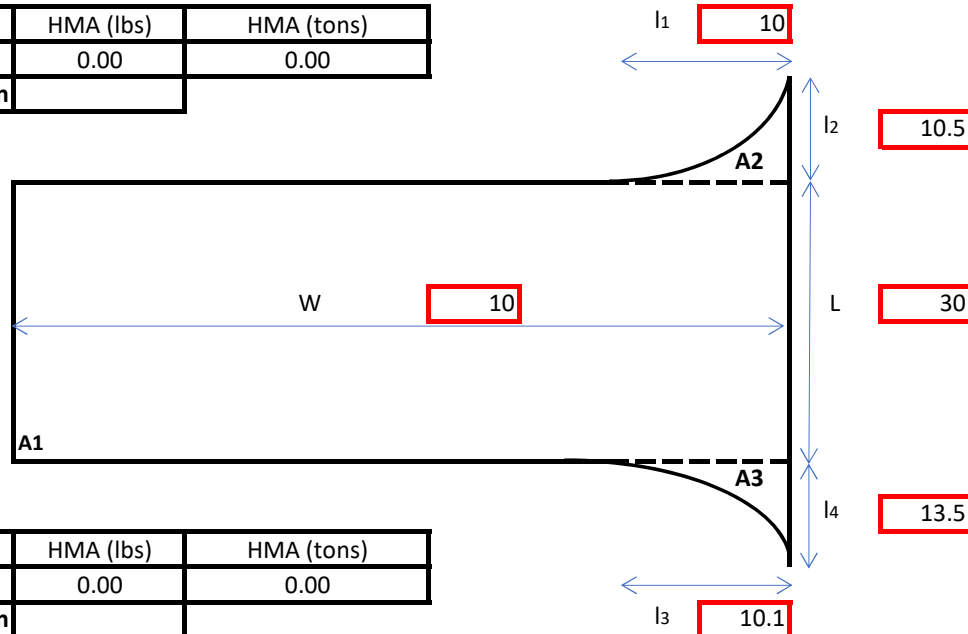

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

DATE: 8/4/2020

REVIEWED BY:

DATE:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 8/4/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 4 OF 13

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Penrod	Tireman	South Side	8	26	9.5	8.5	8.8	8.8
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)				
		208.0	17.3	16.6			Location No.: A1	
241.9	26.88							

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	25.5
SYD	5.67

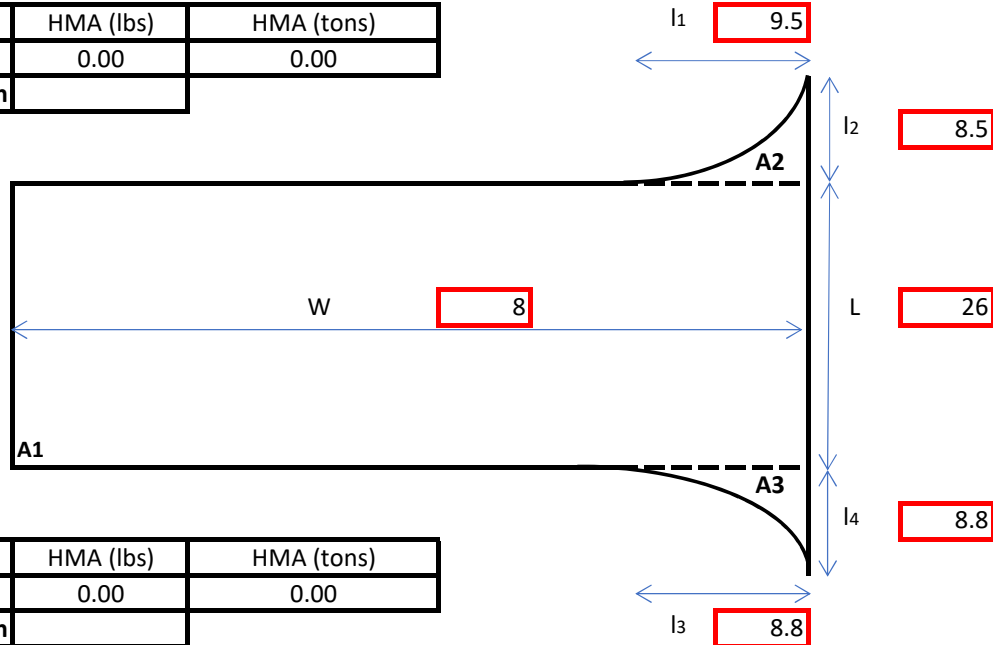

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

DATE: 8/4/2020

REVIEWED BY:

DATE:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 8/4/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 5 OF 13

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Rosemont	Tireman	South Side	16	26	8	10.2	9	9.6
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
452.1	50.23	416.0	17.5	18.5				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	24.2
SYD	5.38

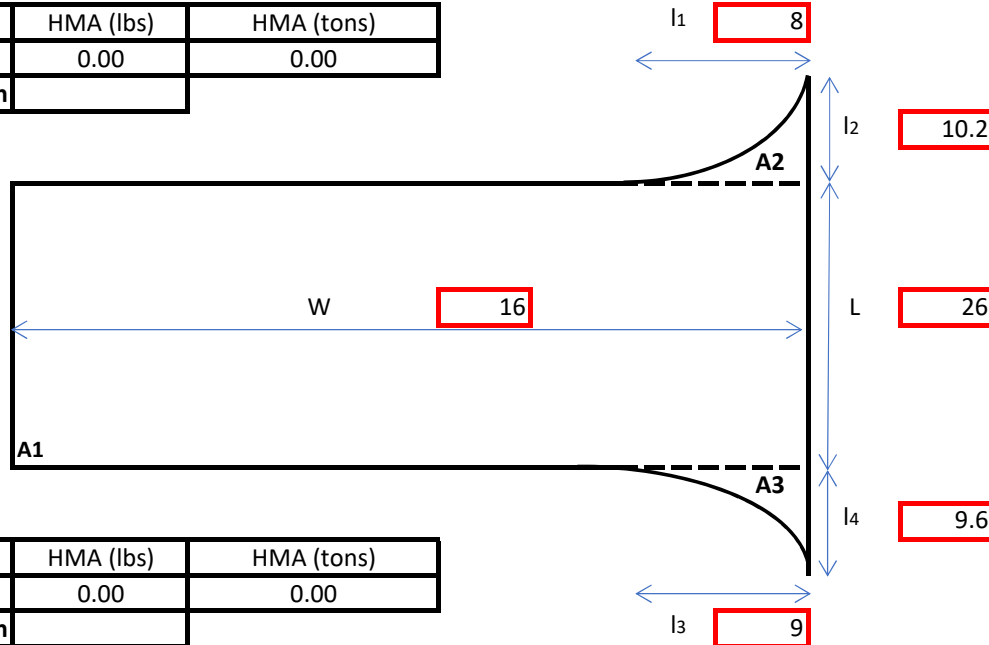

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

DATE: 8/4/2020

REVIEWED BY:

DATE:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 8/4/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 6 OF 13

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Ashton	Tireman	South Side	10	26	8	8.8	9.1	10.5
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
295.6	32.85	260.0	15.1	20.5				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	26.0
SYD	5.78

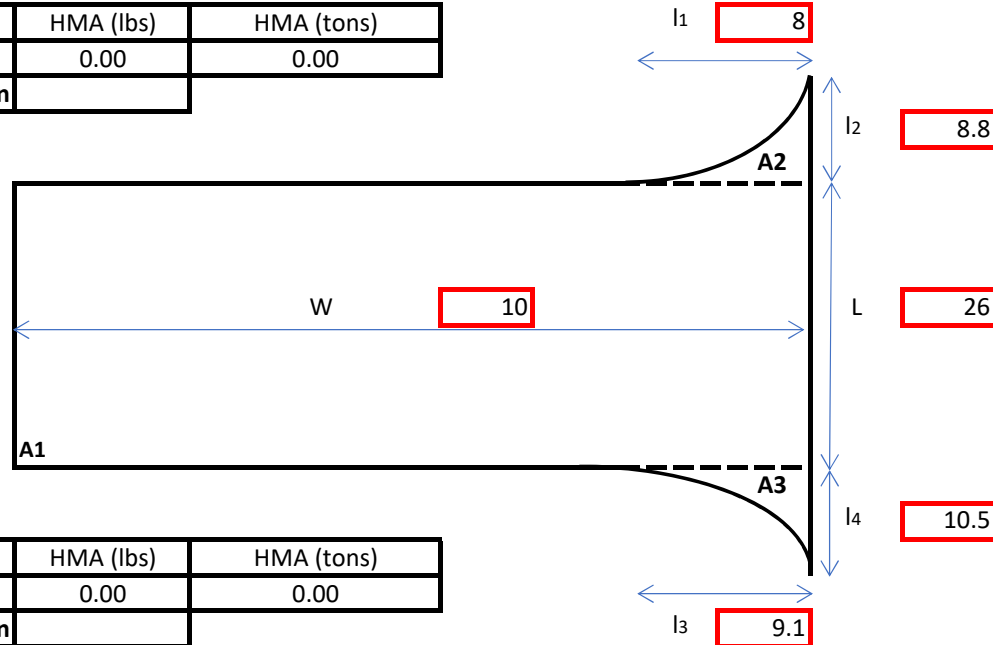

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

DATE: 8/4/2020

DATE:

REVIEWED BY:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 8/4/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 7 OF 13

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Tireman	Southfield	West Side	0	40	0	0	0	0
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
0.0	0.00	0.0	0.0	0.0				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	40.0
SYD	8.89

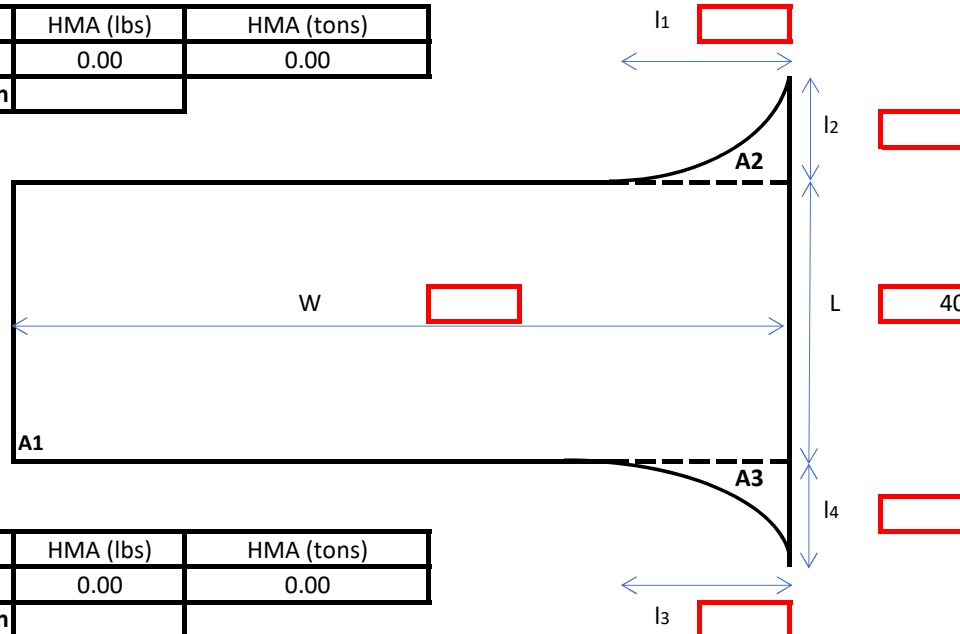

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

DATE: 8/4/2020

REVIEWED BY:

DATE:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 8/4/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 8 OF 13

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Ashton	Tireman	North Side	9	26	9.5	6.3	8.8	7
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
260.1	28.90	234.0	12.8	13.2				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	25.1
SYD	5.58

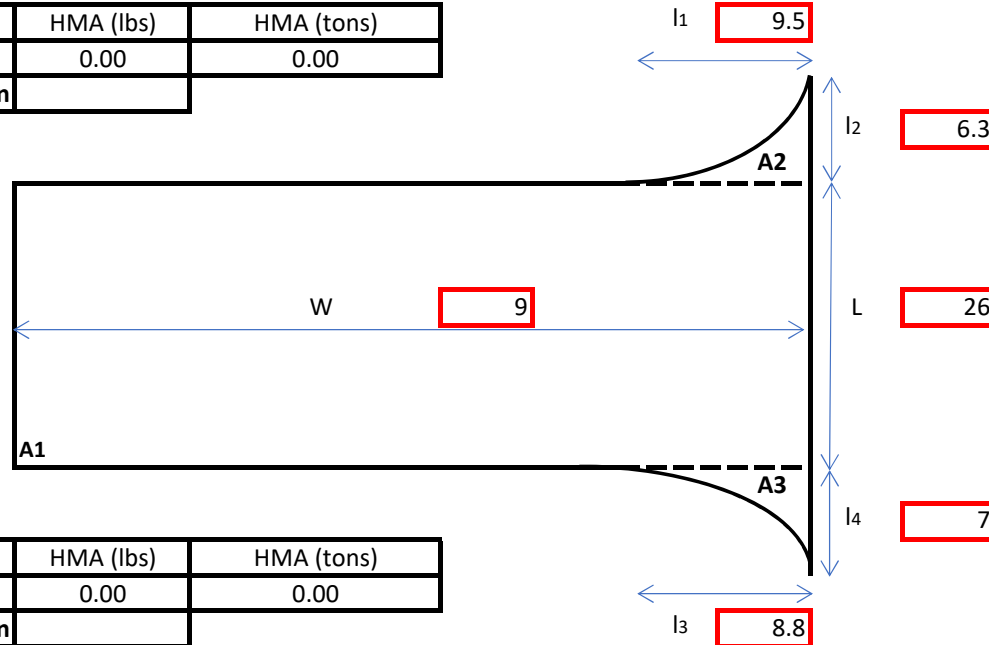

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

DATE: 8/4/2020

REVIEWED BY: _____

DATE: _____

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 8/4/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 9 OF 13

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Rosemont	Tireman	North Side	12	26	8.9	8.3	9.2	10
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
347.6	38.62	312.0	15.9	19.7				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	26.2
SYD	5.82

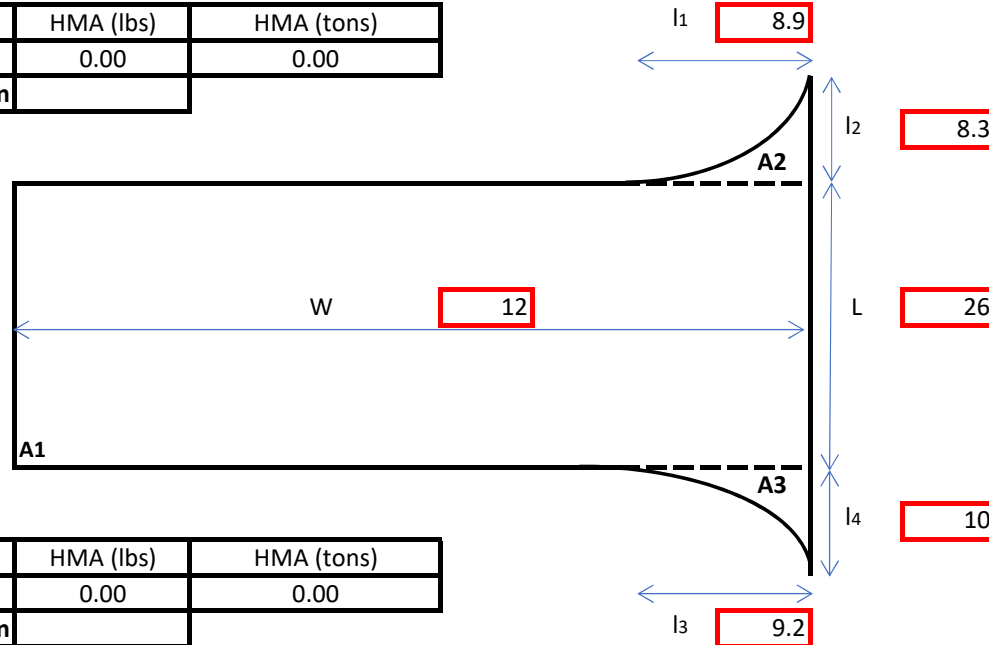

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

DATE: 8/4/2020

REVIEWED BY: _____

DATE: _____

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 8/4/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 10 OF 13

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Penrod	Tireman	North Side	9	26	9	7.6	10	8.1
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)				
		234.0	14.7	17.4	Location No.: A1			
266.1	29.56							

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	26.0
SYD	5.78

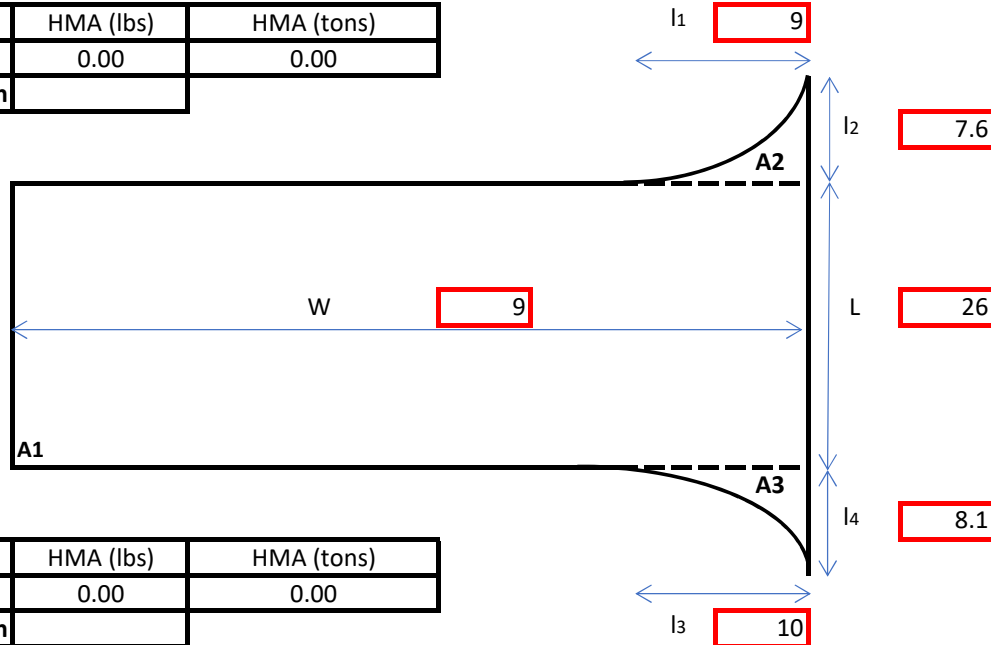

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

DATE: 8/4/2020

DATE:

REVIEWED BY:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 8/4/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 11 OF 13

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Faust	Tireman	North Side	24	30	8.1	9	11.6	10
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
760.5	84.50	720.0	15.6	24.9				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	36.0
SYD	8.00

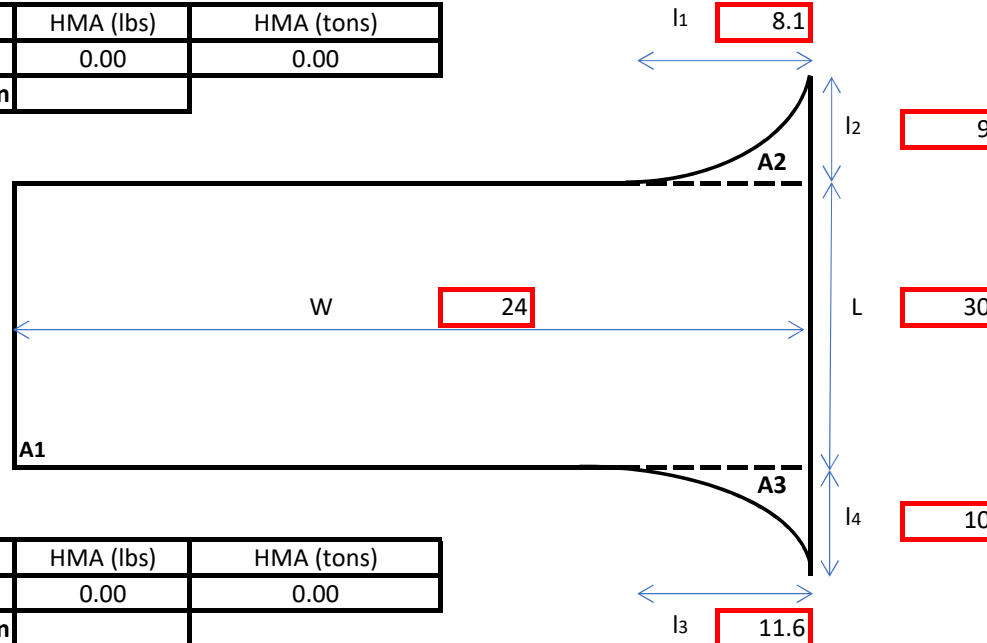

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

DATE: 8/4/2020

REVIEWED BY: _____

DATE: _____

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 8/4/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 12 OF 13

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Greenview	Tireman	North Side	24	30	12	11.3	13	11.7
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
781.7	86.86	720.0	29.1	32.6				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	36.5
SYD	8.11

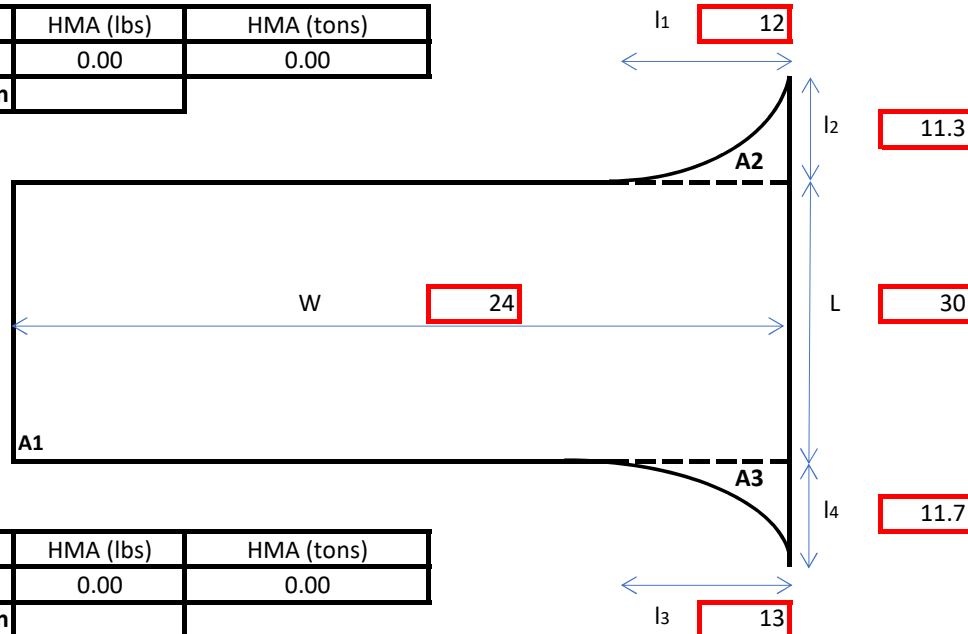

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

DATE: 8/4/2020

REVIEWED BY:

DATE:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: 8/4/2020

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 13 OF 13

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Brace	Tireman	North Side	21	30	13	14	12.7	12
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
701.8	77.97	630.0	39.1	32.7				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	2.0
Length (ft.)	36.6
SYD	8.13

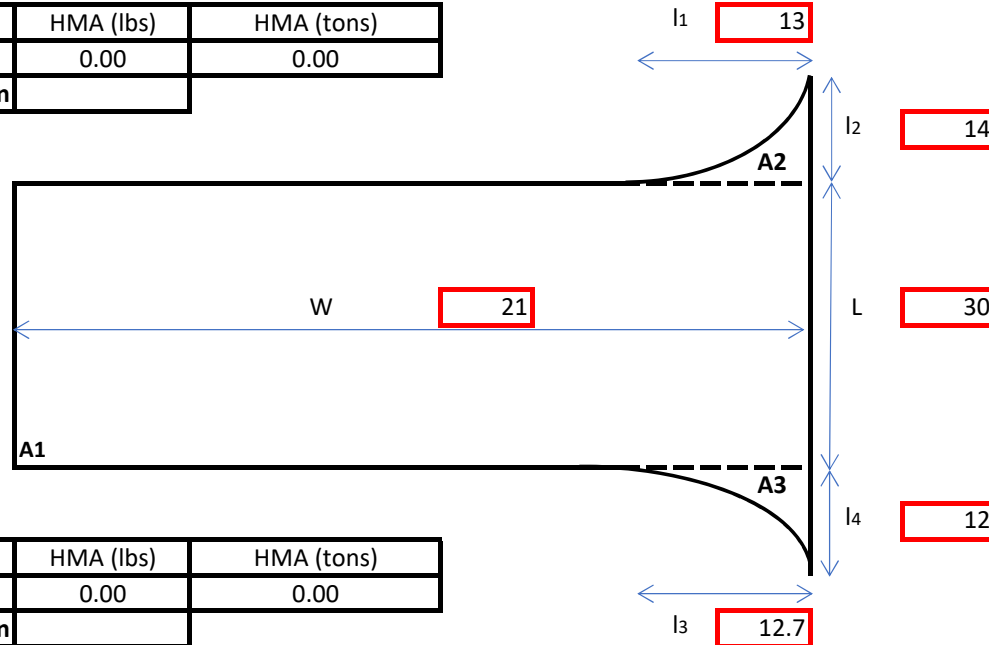

MDOT 5E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

DATE: 8/4/2020

REVIEWED BY: _____

DATE: _____



Somat Engineering
INCORPORATED



Cold Milling HMA Surface, Modified & Projected HMA Quantities

DATE: 8/4/2020

JOB NUMBER: PW-7018

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

LOCATION: Detroit, MI

OWNER: City of Detroit

CONTRACTOR: Ajax Paving Industries

PROJECT ENGINEER: Jim Petronski

SHEETS: 1 OF 1

Main Street		Tireman	Street Width (ft)	Street Length (ft)	Mainline HMA Area (syd)	Mix 4E3 @ 2 inches	Mix 5E3 @ 1.5 inches	PROJECTED HMA (lbs)	PROJECTED 4E3 HMA (tons)	PROJECTED HMA (lbs)	PROJECTED 5E3 HMA (tons)	Date of Completion
No. 1	Start End	Stahelin to Southfield Service Dr.	40.00	2,023.00	8,991.11			0.00	0.00	0.00	0.00	
No.	Start End				0.00			0.00	0.00	0.00	0.00	
No.	Start End				0.00			0.00	0.00	0.00	0.00	
No.	Start End				0.00			0.00	0.00	0.00	0.00	
No.	Start End				0.00			0.00	0.00	0.00	0.00	
No.	Start End				0.00			0.00	0.00	0.00	0.00	
No.	Start End				0.00			0.00	0.00	0.00	0.00	
No.	Start End				0.00			0.00	0.00	0.00	0.00	
Today Total Quantities				2023.00	8,991.11			0.00	0.00	0.00	0.00	

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

REVIEWED BY:

DATE: 8/4/2020

DATE:
