



City of Detroit

Inspector's Daily Report

5/12/2021 3:37 PM

FieldBook 5.3a

Contract: **PW-7018**, City of Detroit Resurfacing 2020

IDR Date 5/12/2021	Day of Week Wednesday	Seq. No. 1	Import Date N/A	Project Engineer Jim Petronski / Ian Duncan - WSP	Construction Engineer Steve Bannasch - City of Detroit
Inspector's Initials-Name LE Lenoris Elliott				Federal Project Number	Elec. Attachments None
Prime Contractor Fort Wayne Contracting / Ajax Paving Industries, a joint ven					
Entered By LE		Revised By		Revision Date	Revision No.
Temperatures ✓ Low: 40 ° F High: 61 ° F		Weather Clear ✓			



Inspector's Daily Report

5/12/2021 3:37 PM

FieldBook 5.3a

Comments

STREET LOCATION: SB JC LODGE SD Vassar to Wyoming

CONTRACTOR ONSITE:

Ajax Paving Industries – Foreman Jason Tapani
Progressive Sweeping

CONTRACTOR ACTIVITIES:

Ajax Paving Industries: (Site Time 6:30AM to 2:30PM)
Progressive Sweeping: (Site Time 6:30AM to 2:30PM)

The contractor's continued the construction activities by power sweeping roadway and applying a total of 113.0 gallons of the Bond Coat – Emulsified Asphalt Product SS-1H on the MDOT 4E3 surface. The application was applied by jet spray. Ajax delivered a total 5 loads at 114.11 tons of MDOT 5E3. The contractor placed 114.11 tons (No Waste) of HMA MDOT 5E3 mix from the Ajax Paving Industries Plant No. 7 (Sherwood) in Warren, Michigan. A Caterpillar Paver AP1055F was utilized to place the HMA in a loose layer ranging from 1.5 to 2.0 inches in thickness for street return approaches from Hubbell to Curtis.

HMA Approach, Mod, Adj, Locations:

Hubbell
Strathmoor St.
Freeland St.
Clarita Ave.
Ardmore St.
Margareta Ave.
Lesure St.
Pickford Ave. / Tracey St.
Curtis St.

During paving operation's, contractor checked the drainage flow by utilizing a 4-foot-long hand level. Random depth checks were performed and HMA temperatures were recorded on each truckload ticket. To achieve the project density requirements, the compaction operation was performed by using a series of steel drum tandem vibratory rollers.

POSTING ITEMS:

Item Code 5017031 HMA Approach, Mod, Adj, at 114.11 tons.
Item Code 5017031 Bond Coat at 113.0 gallons.

TEMPORARY STRIPING: N/A

ATTACHMENTS:

SB JC Lodge SD Daily Summary Report

MATERIAL TESTING:

Certified HMA technicians from Ajax Paving Industries and Somat were onsite to perform QC/QA HMA sampling and in-place density testing. Somat obtained HMA samples designated from the AM & PM and were submitted to Somat laboratory for testing. The certified technicians informed the inspector that the HMA field test results have met the JMF design in-place density requirements as specified in the project contract/plans and specification.

TRAFFIC CONTROL:

Traffic was maintained throughout the project during the time of construction in accordance with 2012 MDOT Standard Specification for Construction, Section 812, and Temporary Traffic Control for Construction Zone Operations and the City of Detroit Special Provision for Maintaining Traffic, which also includes the furnishing and installation of all traffic control devices and signing.

COVID 19 ONSITE TESTING:

Forehead temperature was performed on myself by using an infrared temperature gun. My reading measured at 96.4 Fahrenheit.



City of Detroit

Inspector's Daily Report

5/12/2021 3:37 PM

FieldBook 5.3a

DBE CONTRACTORS: N/A

UTILITIES: N/A

SITE SAFETY: N/A

SOIL EROSION CONTROL: No issues witnessed or reported to me.

TRAFFIC CONTROL: No issues witnessed or reported to me.

PROJECT VISITORS: N/A

MATERIALS: N/A

Need to list
contractors workforce

EXTRA and OVERRUNS: N/A

Item Postings

Item/Material Description	Item Code	Prop. Line	Project	Category	Quantity	Unit	Location	Brkdwn ID	Attn
_ HMA Approach, Modified, Adj	5017031	0975	PW-7018	0000	114.110	Ton	Street return approaches from Hubbell to Curtis.		
Contractor: Ajax Paving Industries, Inc.									
Bond Coat, Emulsified Asphalt SS-1H					113.00	Gal			
HMA, 5E3					114.11	Ton			

Must list source of
materials

Reviewed By: Michael Teachout
(Signature)

Digitally signed by Michael
Teachout
DN: cn=Michael Teachout, c=US,
o=WSP Michigan Inc,
email=Mike.Teachout@WSP.com
Date: 2021.06.02 07:59:40 -04'00'

(Date)

Cold Milling HMA Approach Surface, Butt Joints Rem, Modified & Projected HMA Quantity

DATE: Wednesday, May 12, 2021

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski

LOCATION: Detroit, MI

SHEETS: 1 OF 1

South Bound John C Lodge Service Drive

Item Code 5010005 HMA Surface, Rem	
Surface Area (sft.)	12,045.37
Surface Area (syd.)	1,338.37
A1 (sft.)	11,429.65
A2 (sft.)	210.24
A3 (sft.)	405.48

Item Code 5010008 Pavt for Butt Joints, Rem	
Width (ft.)	0.00
Length (ft.)	0.00
SYD	0.00

Item Code 5017031 HMA Approach, Mod, Adj, 4E3	
HMA (lbs.)	0.00
HMA (tons)	0.00

Item Code 5017031 HMA Approach, Mod, Adj, 5E3	
HMA (lbs.)	220,831.87
HMA (tons)	110.42

Item Code 5017011 _ Cold Milling HMA Surface, Modified			YES		NO	X
Item Code HMA, 4E3			YES		NO	X
Item Code 5017031, HMA Approach, Mod, Adj, 5E3			YES	X	NO	
Main Street	SB John C Lodge SD	Street Width (ft)	Street Length (ft)		Surface Mainline Area (syd)	
No.1 End	Start End	Hubbell Curtis	N/A		0.00	
MDOT MIXES			PROJECTED HMA (lbs)		PROJECTED HMA (tons)	
Mix 4E3 @ 2"		220	0.00		0.00	
Mix 5E3 @ 1.5"		165	0.00		0.00	
Bond Coat – Emulsified Asphalt			Product: SS-1H		Gallons: 113.00	

Item Code _2040055 Sidewalk, Rem		Item Code _8027011 _Sidewalk,Conc, 4", Mod.	Item Code _8027012 _Sidewalk,Conc, 6", Mod.	Item Code _8037010 _Sidewalk,Conc,Tree Roots 4"	Item Code 8037011 _Sidewalk,Conc,Tree Roots 6"
	SYD's	SFT			
Rem.	0.00	0.00			
4 in.	0.00	0.00			
6 in.	0.00	0.00			
4"Root	0.00	0.00			
6"Root	0.00	0.00			

Item Code _2047002 _Curb, Rem,Mod.		Item Code _6037001 _Curb, Detail CD,Mod	Item Code _8030030 _Curb Ramp Open,Conc	Item Code _2047001 _Inter,Curb,Walk,2ft Rem	Item Code _8037001 _Inter.Curb.Walk.2ft Mod
		LFT			
Removal (ft)		0.00			
Curb, Conc, Detail CD (ft)		0.00			
Ramp Opening Curb (ft)		0.00			
2 ft Integral Rem. (ft)		0.00			
2 ft Integral (ft)		0.00			

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

DATE: 5/12/2021

REVIEWED BY:

DATE:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: Wednesday, May 12, 2021

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 1 OF 9

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Hubbell	Lodge	West Side	17	132	0	0	15	13
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
2,285.8 ✓	253.98 ✓	2244.0 ✓	0.0	41.8 ✓				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	0.0
Length (ft.)	0.0
SYD	0.00

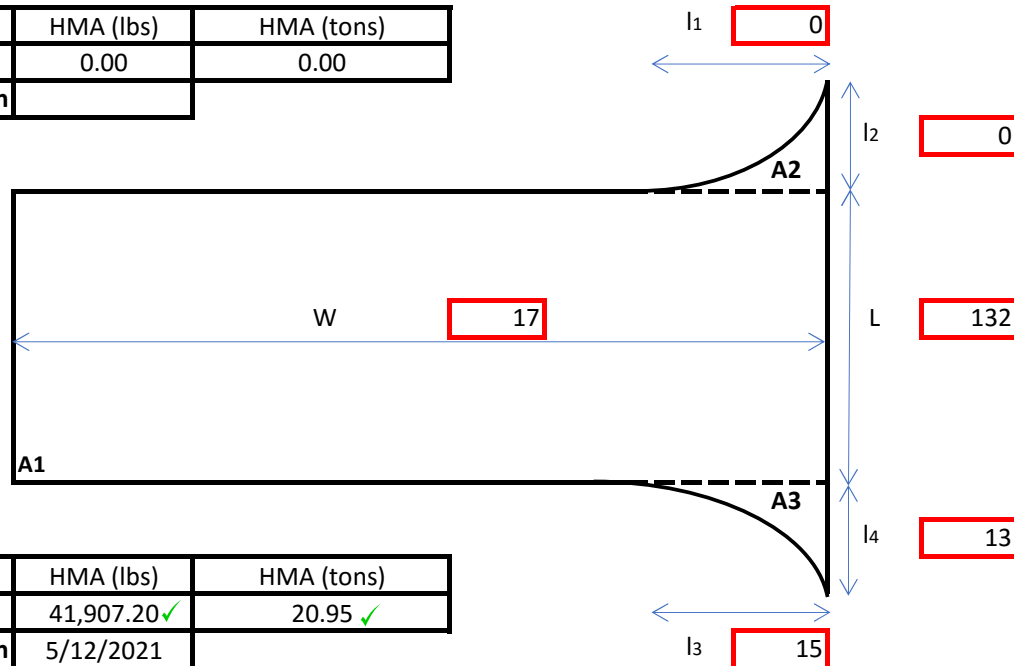

MDOT 5E3	HMA (lbs)	HMA (tons)
165	41,907.20 ✓	20.95 ✓
Date of Completion	5/12/2021	

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

REVIEWED BY: MT (WSP)

DATE: 5/12/2021

DATE: 06/02/2021

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: Wednesday, May 12, 2021

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 2 OF 9

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Strathmoor	Lodge	West Sde	17	83.85	0	0	17	17
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A2			
1,487.5 ✓	165.27 ✓	1425.5 ✓	0.0	62.0 ✓				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	0.0
Length (ft.)	0.00
SYD	0.00

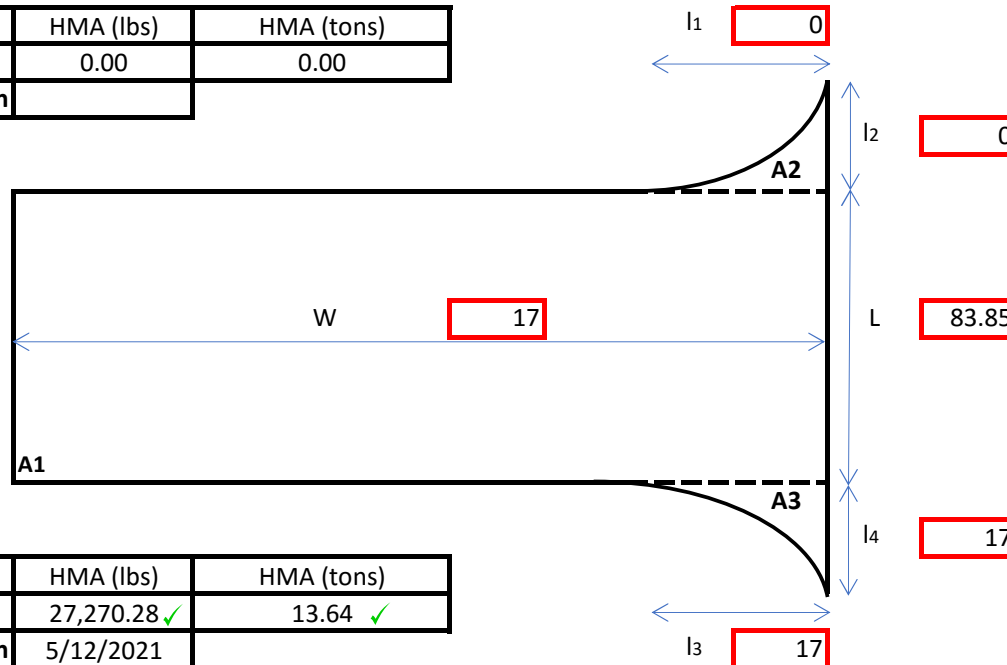

MDOT 5E3	HMA (lbs)	HMA (tons)
165	27,270.28 ✓	13.64 ✓
Date of Completion	5/12/2021	

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

REVIEWED BY: MT (WSP)

DATE: 5/12/2021

DATE: 06/02/2021

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: Wednesday, May 12, 2021

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 3 OF 9

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Freeland	Lodge	West Side	20	40.6	11	9.8	12	12.6
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A3			
867.6 ✓	96.40 ✓	812.0 ✓	23.1 ✓	32.4 ✓				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	0.0
Length (ft.)	0.0
SYD	0.00

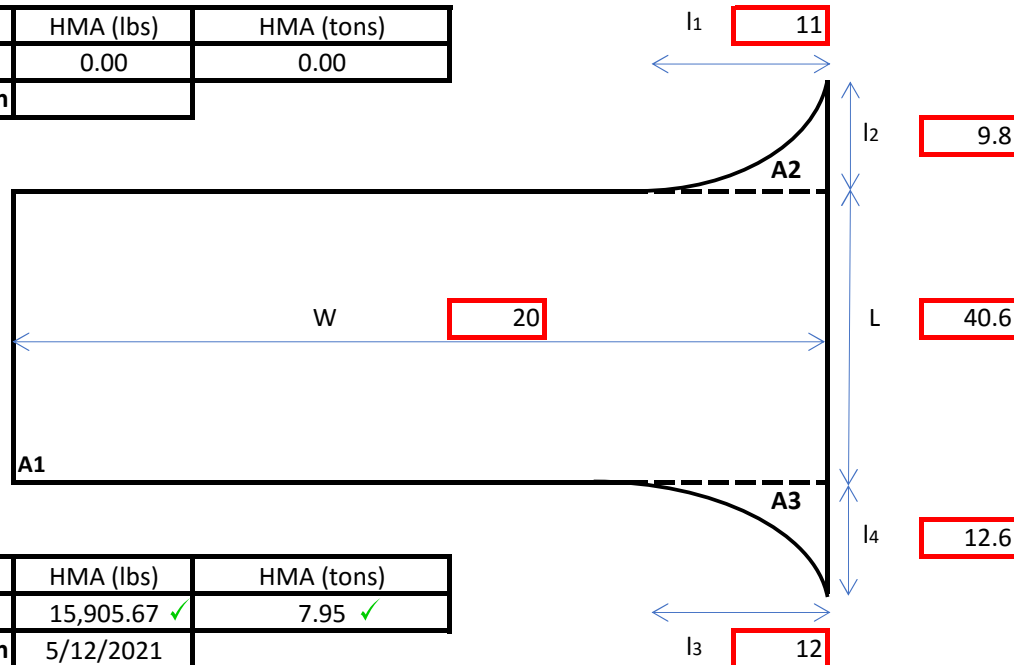

MDOT 5E3	HMA (lbs)	HMA (tons)
165	15,905.67 ✓	7.95 ✓
Date of Completion	5/12/2021	

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

REVIEWED BY: MT (WSP)

DATE: 5/12/2021

DATE: 06/02/2021

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: Wednesday, May 12, 2021

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 4 OF 9

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Clarita	Lodge	West Side	21.5	50	8	7	18.5	19
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A4			
1,162.5 ✓	129.16 ✓	1075.0 ✓	12.0 ✓	75.4 ✓				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	0.0
Length (ft.)	0.0
SYD	0.00

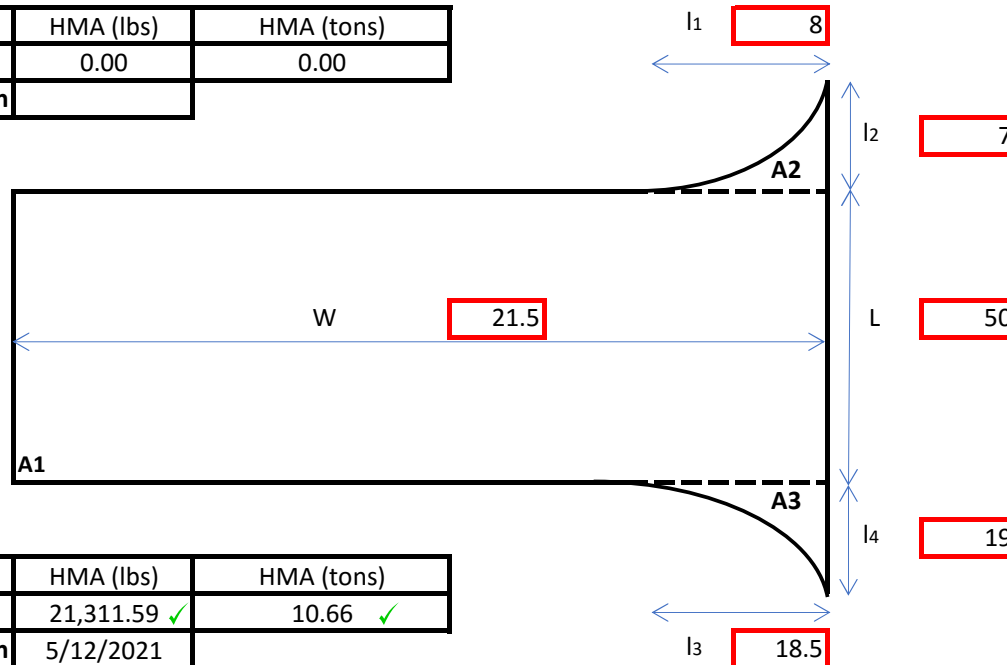

MDOT 5E3	HMA (lbs)	HMA (tons)
165	21,311.59 ✓	10.66 ✓
Date of Completion	5/12/2021	

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

REVIEWED BY: MT (WSP)

DATE: 5/12/2021

DATE: 06/02/2021

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: Wednesday, May 12, 2021

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 5 OF 9

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Ardmore	Lodge	West Side	24	56.5	0	0	16	17
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A5			
1,414.4 ✓	157.15 ✓	1356.0 ✓	0.0	58.4 ✓				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	0.0
Length (ft.)	0.0
SYD	0.00

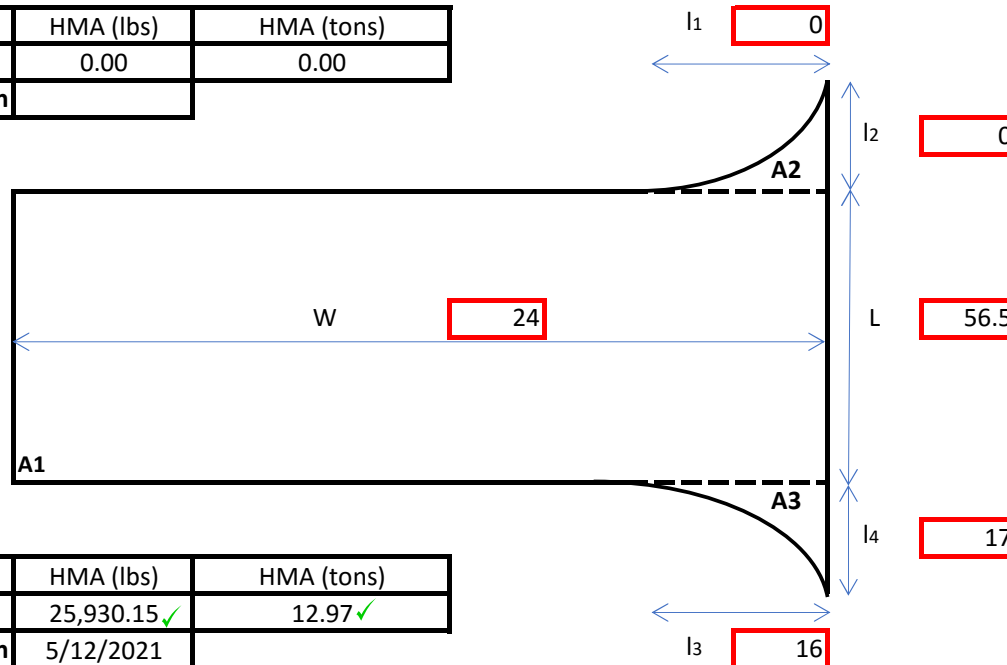

MDOT 5E3	HMA (lbs)	HMA (tons)
165	25,930.15 ✓	12.97 ✓
Date of Completion	5/12/2021	

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

REVIEWED BY: MT (WSP)

DATE: 5/12/2021

DATE: 06/02/2021

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: Wednesday, May 12, 2021

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 6 OF 9

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Margaretta	Lodge	West Side	21.2	53.5	9.5	13.3	0	0
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A6			
1,161.3 ✓	129.03 ✓	1134.2 ✓	27.1 ✓	0.0				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	0.0
Length (ft.)	0.0
SYD	0.00

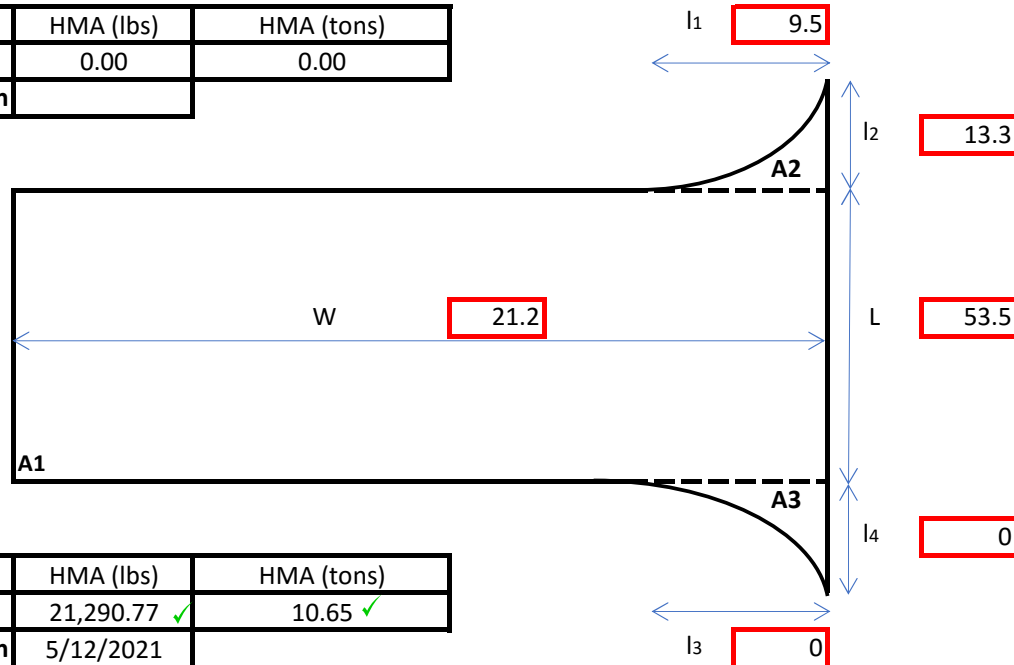

MDOT 5E3	HMA (lbs)	HMA (tons)
165	21,290.77 ✓	10.65 ✓
Date of Completion	5/12/2021	

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

REVIEWED BY: MT (WSP)

DATE: 5/12/2021

DATE: 06/02/2021

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: Wednesday, May 12, 2021

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 7 OF 9

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Lesure	Lodge	West Side	18.5	37	16.9	15.6	17.8	15.4
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A7			
799.9 ✓	88.88 ✓	684.5 ✓	56.6 ✓	58.8 ✓				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	0.0
Length (ft.)	0.0
SYD	0.00

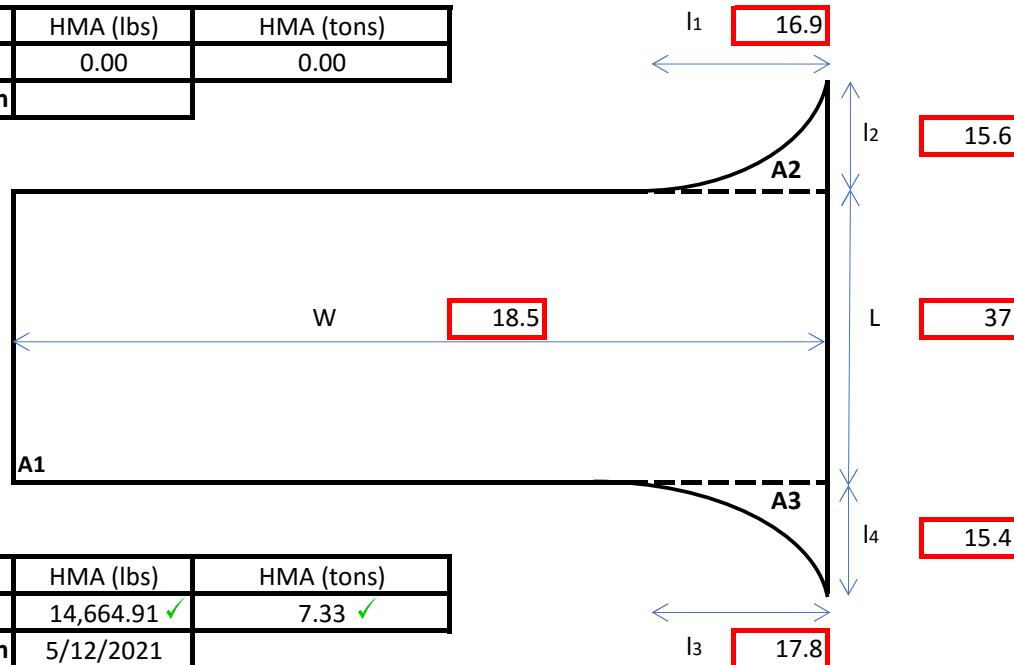

MDOT 5E3	HMA (lbs)	HMA (tons)
165	14,664.91 ✓	7.33 ✓
Date of Completion	5/12/2021	

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

REVIEWED BY: MT (WSP)

DATE: 5/12/2021

DATE: 06/02/2021

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: Wednesday, May 12, 2021

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 8 OF 9

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Pickford / Tracey	Lodge	West Side	19.5	77.8	15.5	18	12	14.9
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A8			
1,615.3 ✓	179.48 ✓	1517.1 ✓	59.9 ✓	38.4 ✓				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	0.0
Length (ft.)	0.0
SYD	0.00

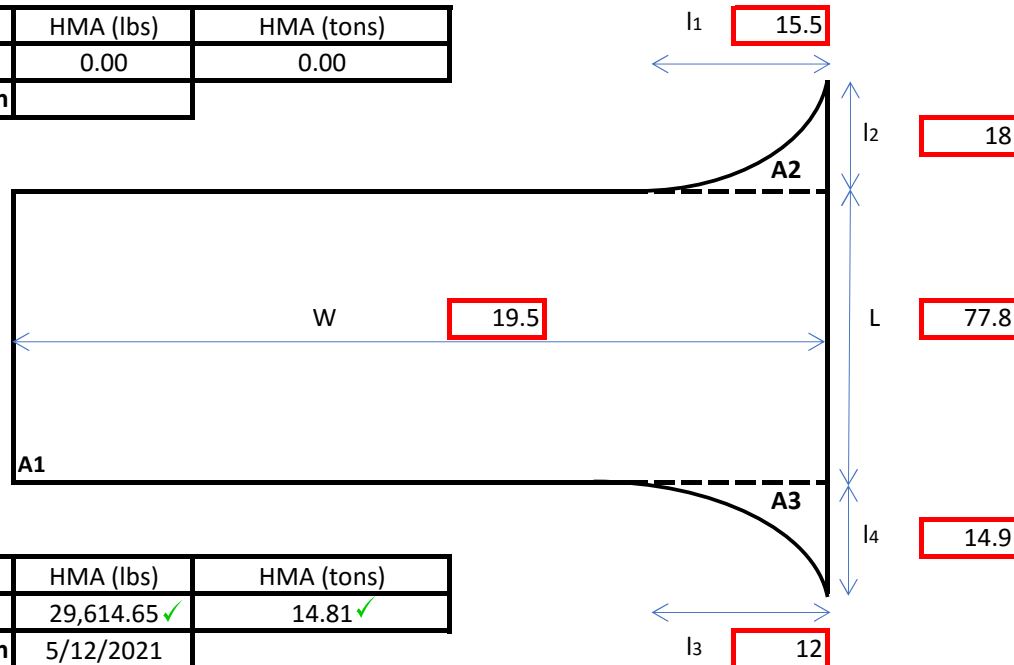

MDOT 5E3	HMA (lbs)	HMA (tons)
165	29,614.65 ✓	14.81 ✓
Date of Completion	5/12/2021	

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

REVIEWED BY: MT (WSP)

DATE: 5/12/2021

DATE: 06/02/2021

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: Wednesday, May 12, 2021

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 9 OF 9

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Curtis	Lodge	West Side	17.9	66	11.3	13	11.4	15.6
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A9			
1,251.1 ✓	139.01 ✓	1181.4 ✓	31.5 ✓	38.2 ✓				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	0.0
Length (ft.)	0.0
SYD	0.00

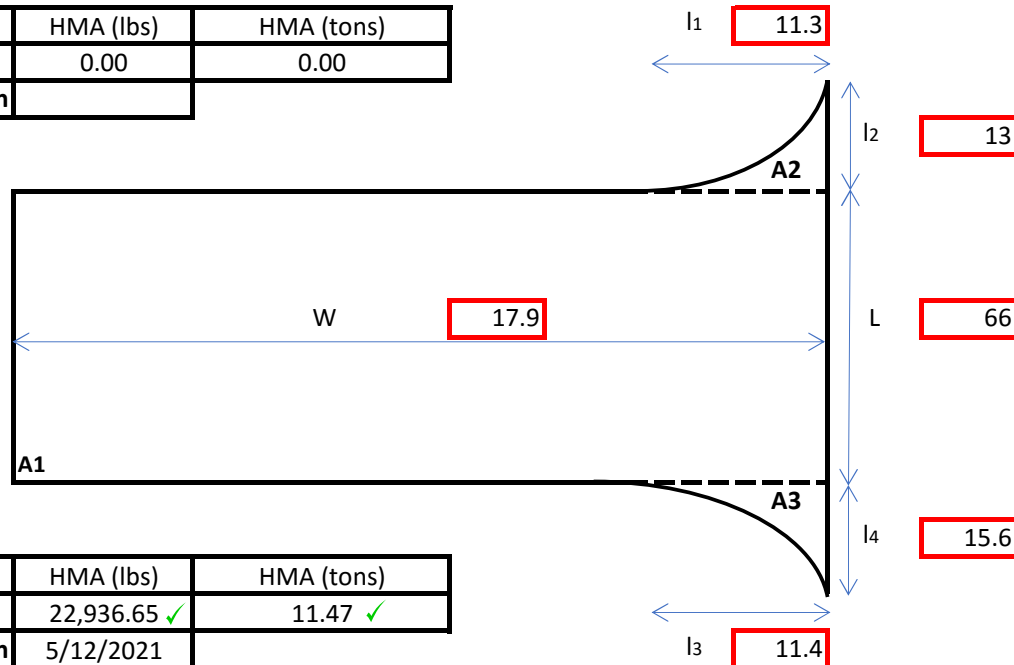

MDOT 5E3	HMA (lbs)	HMA (tons)
165	22,936.65 ✓	11.47 ✓
Date of Completion	5/12/2021	

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

REVIEWED BY: MT (WSP)

DATE: 5/12/2021

DATE: 06/02/2021
