



City of Detroit

Inspector's Daily Report

5/14/2021 3:27 PM

FieldBook 5.3a

Contract: **PW-7018**, City of Detroit Resurfacing 2020

IDR Date 5/14/2021	Day of Week Friday	Seq. No. 1	Import Date N/A	Project Engineer Jim Petronski / Ian Duncan - WSP	Construction Engineer Steve Bannasch - City of Detroit
Inspector's Initials-Name LE Lenoris Elliott				Federal Project Number	Elec. Attachments None
Prime Contractor Fort Wayne Contracting / Ajax Paving Industries, a joint ven					
Entered By LE		Revised By		Revision Date	Revision No.
Temperatures ✓ Low: 47 ° F High: 70 ° F		Weather ✓ Partly Sunny			



Inspector's Daily Report

5/14/2021 3:27 PM

FieldBook 5.3a

Comments

STREET LOCATION: SB JC LODGE SD Vassar to Wyoming

CONTRACTOR ONSITE:

Ajax Paving Industries – Foreman Jason Tapani
Progressive Sweeping

CONTRACTOR ACTIVITIES:

Ajax Paving Industries: (Site Time 6:30AM to 2:30PM)
Progressive Sweeping: (Site Time 6:30AM to 2:30PM)

HMA APPROACH, MOD, ADJ:

The contractor's continued the construction activities by power sweeping roadway and applying a total of 55.0 gallons of the Bond Coat – Emulsified Asphalt Product SS-1H on the MDOT 4E3 surface. The application was applied by jet spray. Ajax delivered a total 4 loads at 98.20 tons of MDOT 5E3. The contractor placed 90.20 tons (8.0 tons of Waste) of HMA MDOT 5E3 mix from the Ajax Paving Industries Plant No. 7 (Sherwood) in Warren, Michigan. A Caterpillar Paver AP1055F was utilized to place the HMA in a loose layer ranging from 1.75 to 2.0 inches in thickness for street return approaches from Manor to Wyoming.

HMA Approach, Mod, Adj, Locations:

Manor.
Florence.
Monte Vista St.
Pinehurst St.
Wyoming SB Off Ramp.
Pilgrim.
Griggs Ave.
Midland St.
Ilene.
Keeler.

During paving operation's, contractor checked the drainage flow by utilizing a 4-foot-long hand level. Random depth checks were performed and HMA temperatures were recorded on each truckload ticket. To achieve the project density requirements, the compaction operation was performed by using a series of steel drum tandem vibratory rollers.

POSTING ITEMS:

Item Code 5017031 HMA Approach, Mod, at 90.20 tons.
Item Code 5017031 Bond Coat at 55.0 gallons.

TEMPORARY STRIPING: N/A

ATTACHMENTS:

SB JC Lodge SD Daily Summary Report

MATERIAL TESTING:

Certified HMA technicians from Ajax Paving Industries and Somat were onsite to perform QC/QA HMA sampling and in-place density testing. Somat obtained HMA samples designated from the AM & PM and were submitted to Somat laboratory for testing. The certified technicians informed the inspector that the HMA field test results have met the JMF design in-place density requirements as specified in the project contract/plans and specification.

TRAFFIC CONTROL:

Traffic was maintained throughout the project during the time of construction in accordance with 2012 MDOT Standard Specification for Construction, Section 812, and Temporary Traffic Control for Construction Zone Operations and the City of Detroit Special Provision for Maintaining Traffic, which also includes the furnishing and installation of all traffic control devices and signing.

COVID 19 ONSITE TESTING:



City of Detroit

Inspector's Daily Report

5/14/2021 3:27 PM

FieldBook 5.3a

Forehead temperature was performed on myself by using an infrared temperature gun. My reading measured at 96.9 Fahrenheit.

DBE CONTRACTORS: N/A

UTILITIES: N/A

SITE SAFETY: N/A

SOIL EROSION CONTROL: No issues witnessed or reported to me.

TRAFFIC CONTROL: No issues witnessed or reported to me.

PROJECT VISITORS: N/A

MATERIALS: N/A

EXTRA and OVERRUNS: N/A

Need to list
contractors
manpower/equipment

Item Postings

Item/Material Description	Item Code	Prop. Line	Project	Category	Quantity	Unit	Location	Brkdwn ID	Attn
_ HMA Approach, Modified, Adj	5017031	0975	PW-7018	0000	90.200	Ton	Street return approaches from Manor to Wyoming.		
Contractor: Ajax Paving Industries, Inc.									
Bond Coat, Emulsified Asphalt SS-1H							55.00 Gal		
HMA, 5E3							90.20 Ton		

Must list source of
materials

Reviewed By: **Michael Teachout**
Digitally signed by Michael Teachout
 DN: cn=Michael Teachout, c=US,
 o=WSP Michigan Inc,
 email=Mike.Teachout@WSP.com
 Date: 2021.06.02 08:52:22 -0400
 (Signature)

(Date)

Cold Milling HMA Approach Surface, Butt Joints Rem, Modified & Projected HMA Quantity

DATE: Friday, May 14, 2021

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski

LOCATION: Detroit, MI

SHEETS: 1 OF 1

SB JC LODGE SD Vassar to Wyoming

Item Code 5010005 HMA Surface, Rem	
Surface Area (sft.)	10,195.28
Surface Area (syd.)	1,132.81
A1 (sft.)	9,440.46
A2 (sft.)	298.94
A3 (sft.)	455.88

Item Code 5010008 Pavt for Butt Joints, Rem	
Width (ft.)	0.00
Length (ft.)	0.00
SYD	0.00

Approaches Projected HMA 4E3	
HMA (lbs.)	0.00
HMA (tons)	0.00

Approaches Projected HMA 5E3	
HMA (lbs.)	186,913.41
HMA (tons)	93.46

Item Code 5017011 _ Cold Milling HMA Surface, Modified			YES		NO	X
Item Code HMA, 4E3			YES		NO	X
Item Code 5017031, HMA Approach, Mod, Adj, 5E3			YES	X	NO	
Main Street	John C Lodge	Street Width (ft)	Street Length (ft)		Surface Mainline Area (syd)	
No.1 End	Start End	Manor Wyoming	N/A		0.00	
MDOT MIXES			PROJECTED HMA (lbs)		PROJECTED HMA (tons)	
Mix 4E3 @ 2"			220		0.00	
Mix 5E3 @ 1.5"			165		0.00	
Bond Coat – Emulsified Asphalt			Product: SS-1H		Gallons: 55.00	

Item Code _2040055 Sidewalk, Rem	Item Code _8027011 _Sidewalk,Conc, 4", Mod.	Item Code _8027012 _Sidewalk,Conc, 6", Mod.	Item Code _8037010 _Sidewalk,Conc,Tree Roots 4"	Item Code 8037011 _Sidewalk,Conc,Tree Roots 6"
	SYD's	SFT		
Rem.	0.00	0.00		
4 in.	0.00	0.00		
6 in.	0.00	0.00		
4"Root	0.00	0.00		
6"Root	0.00	0.00		

Item Code _2047002 _Curb, Rem,Mod.	Item Code _6037001 _Curb, Detail CD,Mod	Item Code _8030030 _Curb Ramp Open,Conc	Item Code _2047001 _Inter,Curb,Walk,2ft Rem	Item Code _8037001 _Inter.Curb.Walk.2ft Mod
				LFT
	Removal (ft)			0.00
	Curb, Conc, Detail CD (ft)			0.00
	Ramp Opening Curb (ft)			0.00
	2 ft Integral Rem. (ft)			0.00
	2 ft Integral (ft)			0.00

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

DATE: 5/14/2021

REVIEWED BY:

DATE:

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: Friday, May 14, 2021

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 1 OF 10

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	l1 (ft)	l2 (ft)	l3 (ft)	l4 (ft)
Manor	Lodge	West Side	21	32.6	13.4	15.2	17	15.7
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A1			
785.6 ✓	87.29 ✓	684.6 ✓	43.7 ✓	57.3 ✓				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	0.0
Length (ft.)	0.0
SYD	0.00

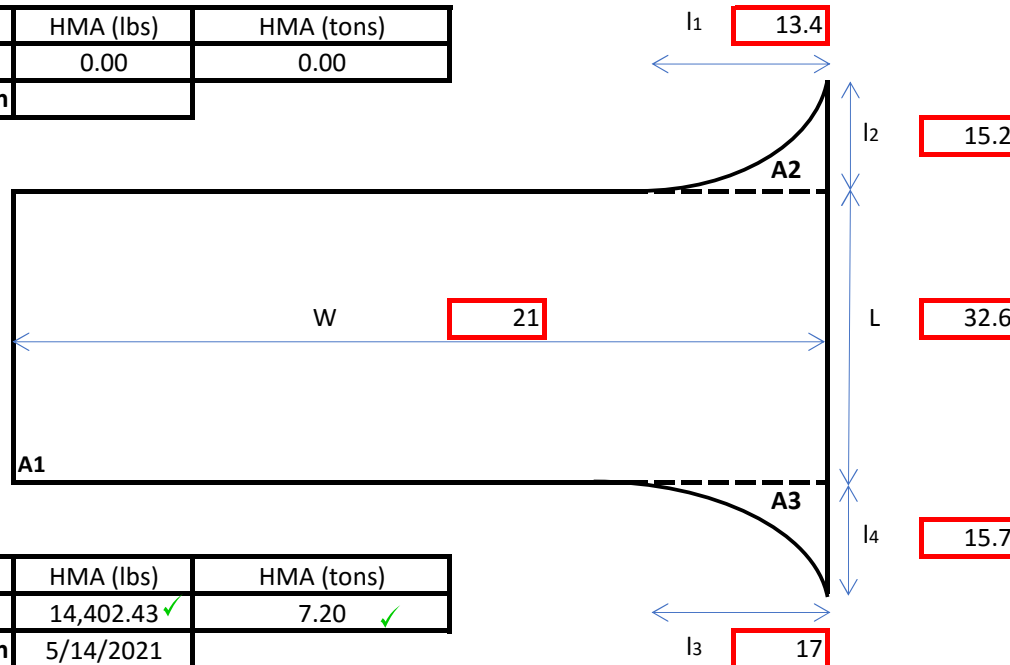

MDOT 5E3	HMA (lbs)	HMA (tons)
165	14,402.43 ✓	7.20 ✓
Date of Completion	5/14/2021	

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

REVIEWED BY: MT (WSP)

DATE: 5/14/2021

DATE: 06/02/2021

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: Friday, May 14, 2021

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 2 OF 10

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Florence	Lodge	West Side	19.8	43	12.4	12.4	19.4	20
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A2			
967.7 ✓	107.52 ✓	851.4 ✓	33.0 ✓	83.3 ✓				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	0.0
Length (ft.)	0.0
SYD	0.00

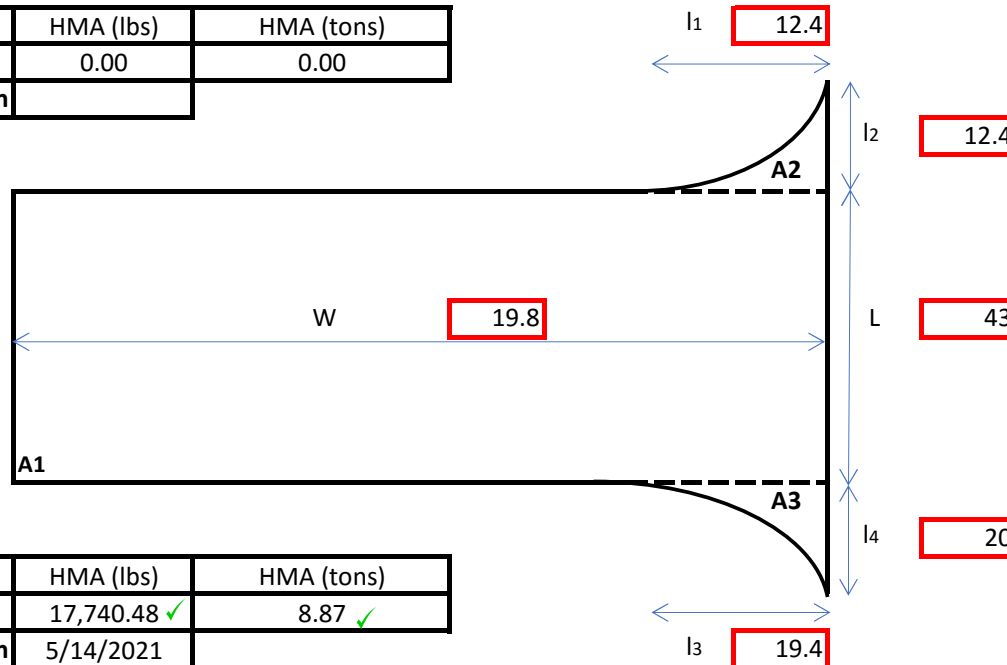

MDOT 5E3	HMA (lbs)	HMA (tons)
165	17,740.48 ✓	8.87 ✓
Date of Completion	5/14/2021	

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

REVIEWED BY: MT (WSP)

DATE: 5/14/2021

DATE: 06/02/2021

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: Friday, May 14, 2021

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 3 OF 10

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Monte Vista	Lodge	West Side	22.7	33	11.3	15	16.6	16.6
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A3			
844.6 ✓	93.85 ✓	749.1 ✓	36.4 ✓	59.1 ✓				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	0.0
Length (ft.)	0.0
SYD	0.00

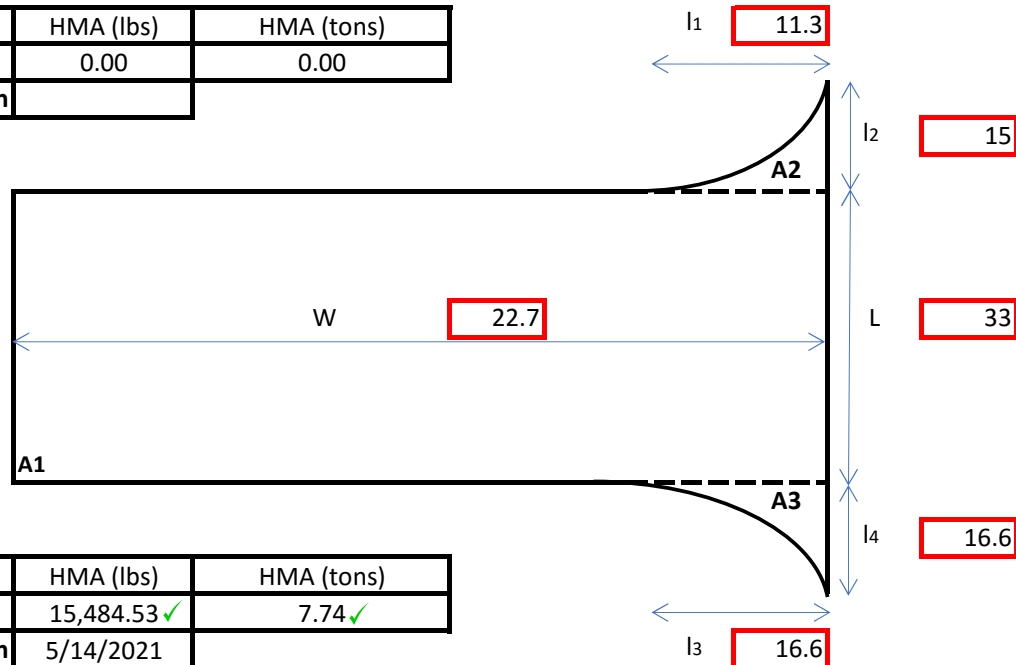

MDOT 5E3	HMA (lbs)	HMA (tons)
165	15,484.53 ✓	7.74 ✓
Date of Completion	5/14/2021	

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

REVIEWED BY: MT (WSP)

DATE: 5/14/2021

DATE: 06/02/2021

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: Friday, May 14, 2021

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 4 OF 10

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Pinehurst	Lodge	West Side	19.6	31.5	17.3	16.4	18	18
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A4			
747.8 ✓	83.09 ✓	617.4 ✓	60.9 ✓	69.5 ✓				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	0.0
Length (ft.)	0.0
SYD	0.00

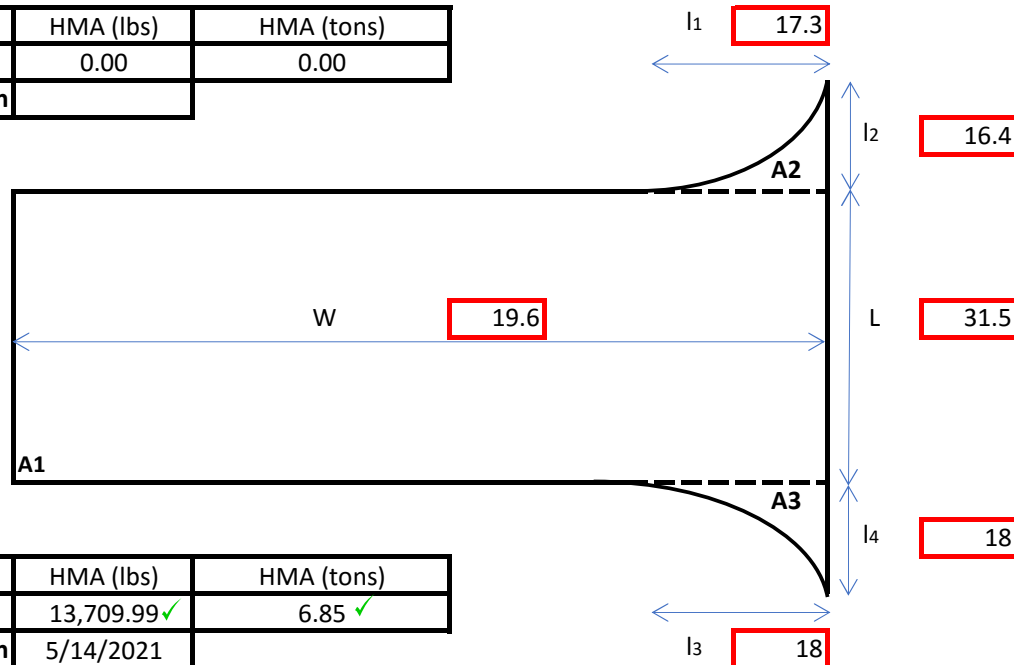

MDOT 5E3	HMA (lbs)	HMA (tons)
165	13,709.99 ✓	6.85 ✓
Date of Completion	5/14/2021	

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

REVIEWED BY: MT (WSP)

DATE: 5/14/2021

DATE: 06/02/2021

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: Friday, May 14, 2021

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 5 OF 10

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Pilgrim	Lodge	West Side	16.6	53.3	16	16	13.3	15.9
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A5			
985.1 ✓	109.46 ✓	884.8 ✓	54.9 ✓	45.4 ✓				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	0.0
Length (ft.)	0.0
SYD	0.00

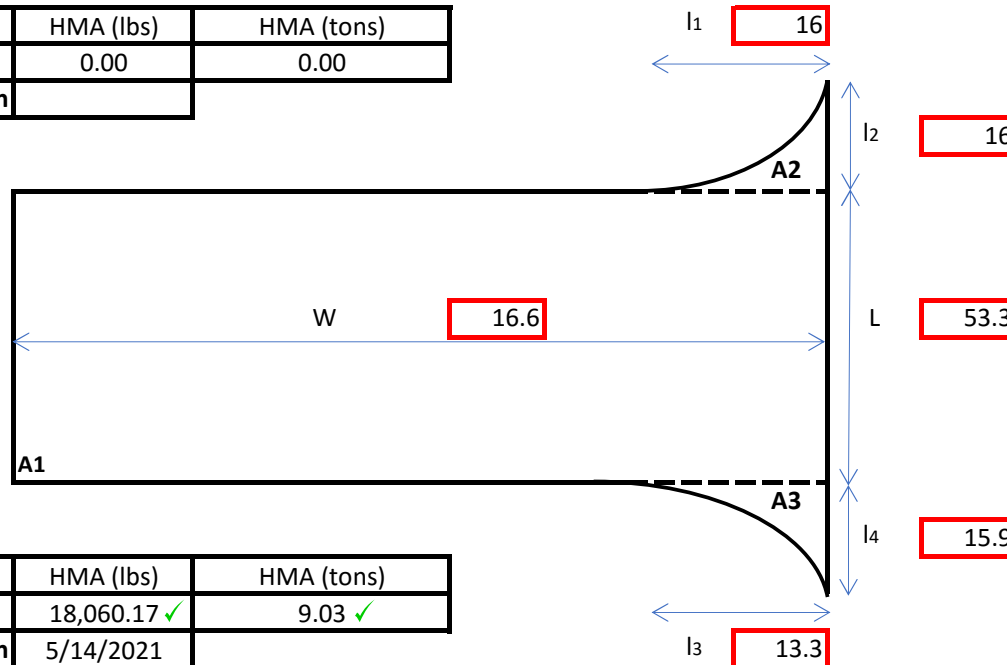

MDOT 5E3	HMA (lbs)	HMA (tons)
165	18,060.17 ✓	9.03 ✓
Date of Completion	5/14/2021	

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

REVIEWED BY: MT (WSP)

DATE: 5/14/2021

DATE: 06/02/2021

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: Friday, May 14, 2021

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 6 OF 10

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Griggs	Lodge	West Side	16	31.6	13.2	12.8	15.3	15
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A6			
591.1 ✓	65.68 ✓	505.6 ✓	36.3 ✓	49.3 ✓				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	0.0
Length (ft.)	0.0
SYD	0.00

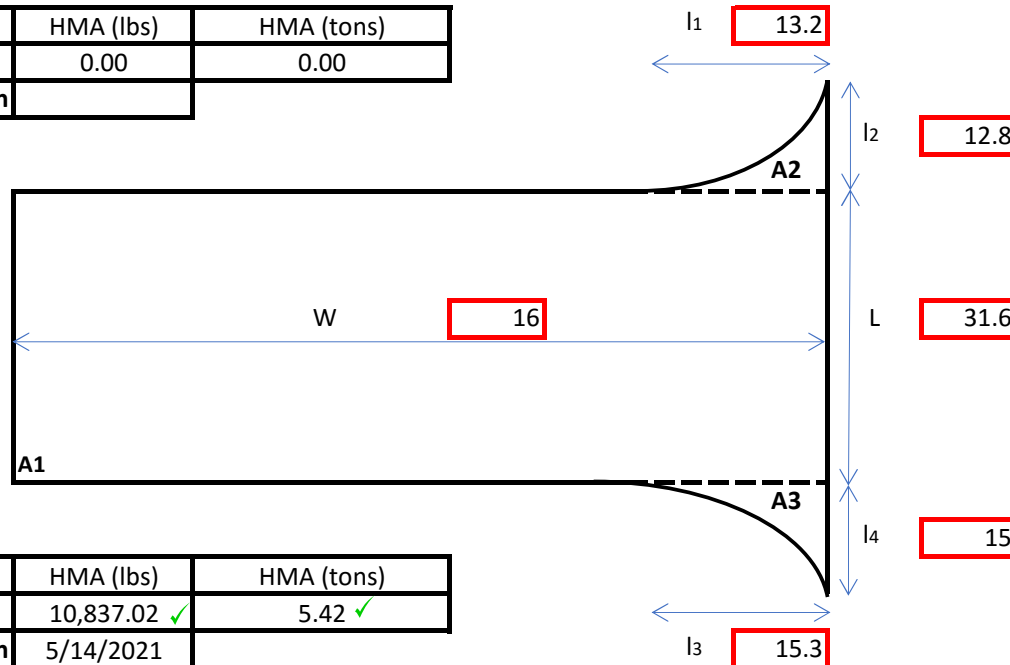

MDOT 5E3	HMA (lbs)	HMA (tons)
165	10,837.02 ✓	5.42 ✓
Date of Completion	5/14/2021	

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

REVIEWED BY: MT (WSP)

DATE: 5/14/2021

DATE: 06/02/2021

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: Friday, May 14, 2021

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 7 OF 10

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Midland	Lodge	West Side	20	39.4	12.2	12.9	17.7	12
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A7			
867.4 ✓	96.37 ✓	788.0 ✓	33.8 ✓	45.6 ✓				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	0.0
Length (ft.)	0.0
SYD	0.00

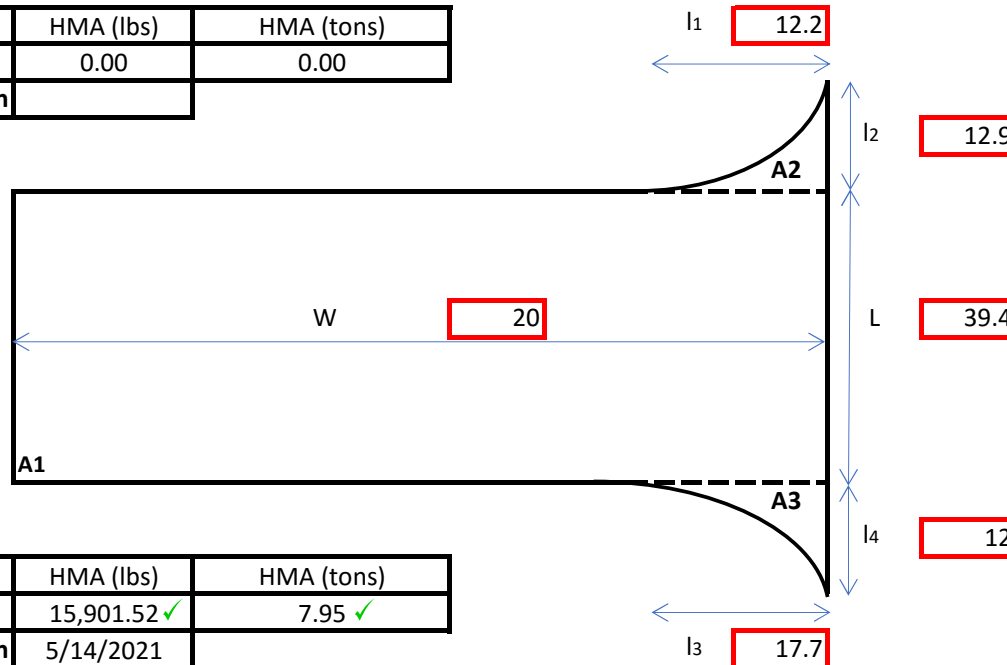

MDOT 5E3	HMA (lbs)	HMA (tons)
165	15,901.52 ✓	7.95 ✓
Date of Completion	5/14/2021	

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

REVIEWED BY: MT (WSP)

DATE: 5/14/2021

DATE: 06/02/2021

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: Friday, May 14, 2021

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 8 OF 10

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Ilene	Lodge	West Side	14.8	53.35	0	0	15.8	13.7
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A8			
836.0 ✓	92.89 ✓	789.6 ✓	0.0	46.5 ✓				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	0.0
Length (ft.)	0.00
SYD	0.00

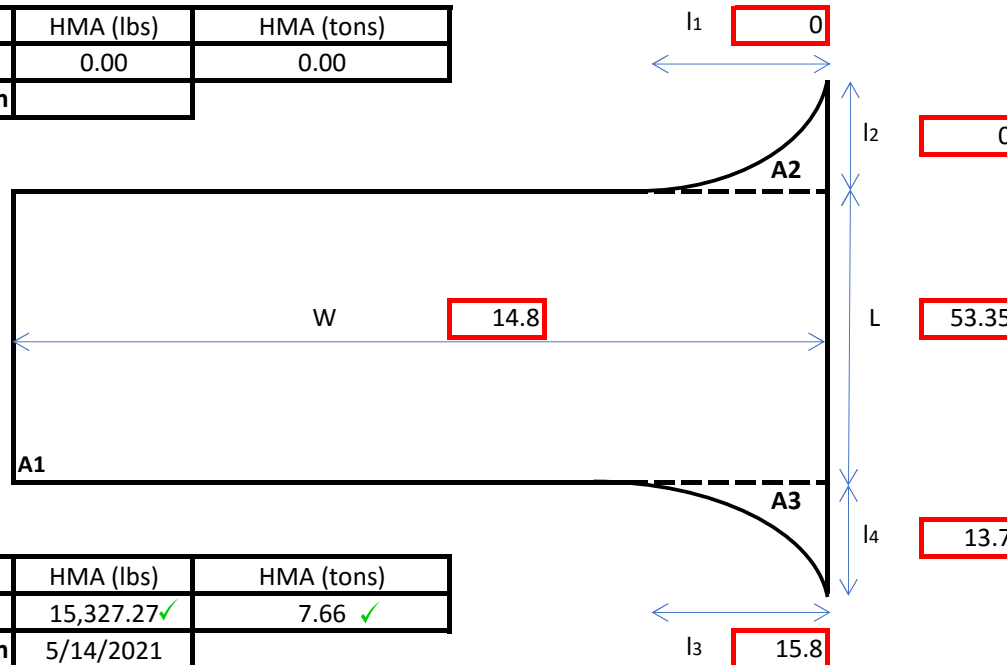

MDOT 5E3	HMA (lbs)	HMA (tons)
165	15,327.27 ✓	7.66 ✓
Date of Completion	5/14/2021	

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

REVIEWED BY: MT (WSP)

DATE: 5/14/2021

DATE: 06/02/2021

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: Friday, May 14, 2021

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 9 OF 10

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Wyoming SB Off Ramp	SB Lodge SD	South Side	89	30	0	0	0	0
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A9			
2,670.0 ✓	296.67 ✓	2670.0 ✓	0.0	0.0				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	0.0
Length (ft.)	0.0
SYD	0.00

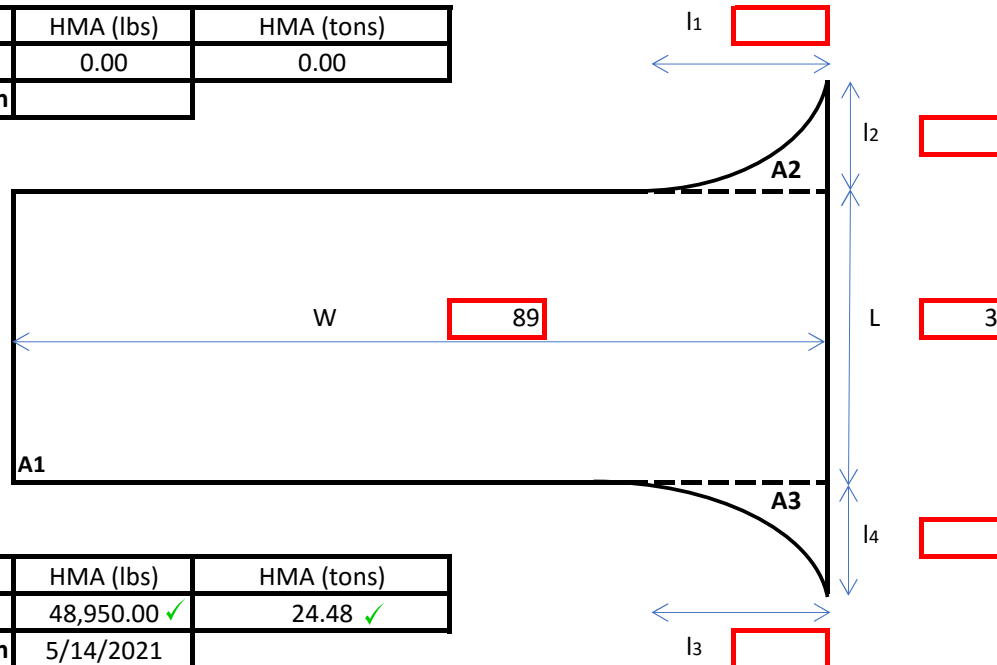

MDOT 5E3	HMA (lbs)	HMA (tons)
165	48,950.00 ✓	24.48 ✓
Date of Completion	5/14/2021	

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

REVIEWED BY: MT (WSP)

DATE: 5/14/2021

DATE: 06/02/2021

Cold Milling HMA Approach Surface, Modified & Projected HMA Quantity

DATE: Friday, May 14, 2021

OWNER: City of Detroit

JOB NUMBER: PW-7018

CONTRACTOR: Ajax Paving Industries

PROJECT NAME: PW-7018 City of Detroit Resurfacing 2020

PROJECT ENGINEER: Jim Petronski


LOCATION: Detroit, MI

SHEETS: 10 OF 10

Main Street	Cross Street	Side of Road	Width (ft)	Length (ft)	I1 (ft)	I2 (ft)	I3 (ft)	I4 (ft)
Keeler	Lodge	West Side	72	12.5	0	0	0	0
Surface Area (sft)	Surface Area (syd)	A1 (sft)	A2 (sft)	A3 (sft)	Location No.: A10			
900.0 ✓	100.00 ✓	900.0 ✓	0.0	0.0				

MDOT 4E3	HMA (lbs)	HMA (tons)
	0.00	0.00
Date of Completion		

BUTT JOINT	
Width (ft.)	0.0
Length (ft.)	0.0
SYD	0.00

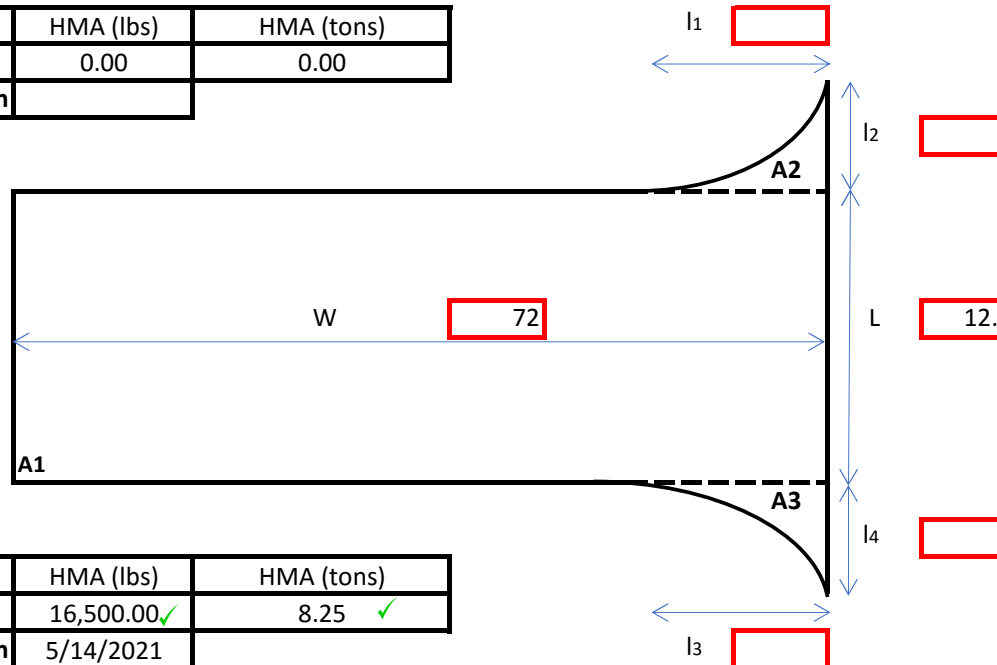

MDOT 5E3	HMA (lbs)	HMA (tons)
165	16,500.00 ✓	8.25 ✓
Date of Completion	5/14/2021	

FIELD INSPECTOR: Lenoris Elliott (SOMAT)

REVIEWED BY: MT (WSP)

DATE: 5/14/2021

DATE: 06/02/2021
