

Wednesday, January 22, 2020

Merlo Const. Co. Inc.
4964 Technical Dr.
Milford, Mi. 48381



Administrative Office
30701 West 10 Mile Rd.
Suite 500
Farmington Hills, MI 48336

RE: Concrete submittal for MDOT 82000-205935 Various Locations in Detroit.

**** Resubmittal due to fine aggregate change ****

Superior Materials, LLC submits the following concrete mixture(s) and documents for review.
Immediately below is a summary of this submittal.

SUPERIOR MATERIALS WARRANTS CONCRETE PLASTIC MEASURES WHEN TESTED AT THE DELIVERY UNIT DISCHARGE CHUTE UPON ARRIVAL ON SITE. WE WILL NOT BE RESPONSIBLE FOR PWL OR NON-PWL NEGATIVE ADJUSTMENTS AFTER OTHER TRANSPORT AND CONSOLIDATION METHODS ARE UTILIZED SUCH AS PUMPING, PAVING EQUIPMENT, VIBRATION, CONVEYORS, DROPPING, ... ETC., AS THESE HANDLING PROCEDURES ARE KNOWN TO ALTER PLASTIC MEASURES. IF A PLASTIC MEASURE(S), WHEN TESTED AT THE DELIVERY UNIT, IS FOUND TO BE OUTSIDE OF SPECIFICATION LIMITS (INCLUDING TOTAL AIR CONTENT BELOW 5.5% OR HIGHER THAN 8.5%), THE CONCRETE MUST EITHER BE REJECTED OR BROUGHT INTO SPECIFICATION LIMITS BEFORE PLACEMENT. ALL PLASTIC MEASURES RESULTS FOUND OUTSIDE OF QC PLAN ACTION LIMITS MUST BE CALLED INTO SUPERIOR MATERIALS QC DEPARTMENT AT ANY ONE OF THE NUMBERS: 810-240-9286 / 248-361-0958 / 248-875-3640 / 586-531-0004.

- 1.) Mix ID # HE75E7CNA032-Grade PNC Concrete, 3 inch slump.
 - a. JMF and Verification Forms.
- 2.) Mix ID # HE75E8CNA032-Grade PNC Concrete, 5 inch slump.
 - a. JMF and Verification Forms.
- 3.) Mix ID # P155E7CNA032-Grade P1 Concrete, 3 inch slump.
 - a. JMF and Verification Forms.
- 4.) Mix ID # P155ERCNA032-Grade P1 Concrete, 5 inch slump.
 - a. JMF and Verification Forms.
- 5.) Mix ID # S1H5ERCNA032-Grade S1 Concrete, 5 inch slump.
 - a. JMF and Verification Forms.
- 6.) Stockpile Management SOP
- 7.) Certifications
 - a. NRMCA certification
 - b. Scale Calibration Certification
 - c. Admix Certification Letter
 - d. Admix Calibration Certification
- 8.) ASR documentation
 - a. ASTM C-1293
- 9.) Materials:
 - a. Cement Mill Report
 - b. Slag Mill Report
 - c. Aggregates
 - d. Admixtures

Please provide approval status when available.

Sincerely,

Nancy Donahue
Technical Service
Superior Materials, LLC
(248) 640-2380 Cell
nxdonahue@superiormaterials.net

Serving All of Southeastern Michigan

Toll Free Order desk: (888) 988-4400 * Office: (248) 788-8000 * Fax: (248) 592-9074

JOB MIX FORMULA (JMF) CONCRETE FIELD COMMUNICATION

This form applies only to the project listed below and is not transferable to other projects
DISTRIBUTION: ORIGINAL - Project Engineer COPIES - Contractor, Lansing CFS, Region, Inspector

CONTROL SECTION 82000	JOB NUMBER 205935	PROJECT LOCATION VARIOUS LOCATIONS	PROJECT ENGINEER JOHN J QUALEY III
CONCRETE SUPPLIER Superior Materials		PLANT LOCATION 8911 W. Jefferson, Detroit, MI 48209	PLANT NUMBER Plant 32 (M-02)
GRADE OF CONCRETE PNC	PSI REQUIREMENT 3500	MIX DESIGN NUMBER HE75E7CNA032	INTENDED USE (S) STRUCTURE ADJUSTMENTS
PRIME / SUBCONTRACTOR (S)		CONTRACTOR OC PLAN SUBMITTED? (MDOT use only) Y ☐ N ☐	
MERLO CONSTRUCTION CO INC			
STANDARD SPEC DATE 2012	QC/QA SPECIAL PROVISION 12SP-604A-09	DATE 6/11/2018	JMF EFFECTIVE DATE 1/22/2020
		AGG. CORRECTION 0.2	

MATERIALS DESIGN SOURCES AND PROPERTIES					
COARSE AGGREGATE		INTERMEDIATE AGGREGATE		FINE AGGREGATE	
Aggregate Type	limestone	Aggregate Type	NA	Aggregate Type	NA
Source Name	Presque Isle	Source Name	NA	Source Name	Levy - Ray Road
MDOT Source Number	71-47	MDOT Source Number	NA	MDOT Source Number	63-115
MDOT Series Class	6AA	MDOT Series Class	NA	MDOT Series Class	2NS
Specific Gravity (Bulk Dry)*	2.56	Specific Gravity (Bulk Dry)*	NA	Specific Gravity (Bulk Dry)	2.62
Specific Gravity (Bulk SSD) optional		Specific Gravity (Bulk SSD) optional		Specific Gravity (Bulk SSD) optional	
Absorption	1.3	Absorption	0	Absorption	1.1
Unit Weight (Dry Rodded) DR or	98	Unit Weight (Dry Rodded) DR or	0	Unit Weight (Dry Rodded) DR or	
Unit Weight (Dry Loose) DL		Unit Weight (Dry Loose) DL		Unit Weight (Dry Loose) DL	
Percent Crushed	100	Percent Crushed	100	Percent Crushed	
MDOT Freeze-Thaw (F-T) Dilation	0.016	MDOT Freeze-Thaw (F-T) Dilation	NA	MDOT Freeze-Thaw (F-T) Dilation	
Specific Gravity (Bulk Dry) of F-T Sample *	2.56	Specific Gravity (Bulk Dry) of F-T Sample *	NA	Specific Gravity (Bulk Dry) of F-T Sample *	
Date of MDOT Freeze-Thaw Report	5/8/2014	Date of MDOT Freeze-Thaw Report	NA	Date of MDOT Freeze-Thaw Report	

* If the bulk specific gravity is more than 0.04 less than the bulk dry specific gravity of the most recently tested freeze-thaw sample, the aggregate will be considered to have changed characteristics and be required to have a new freeze-thaw test conducted prior to use on Department projects.

CEMENTITIOUS		ADMIXTURES		Manufacturer/Product Name	Type	Supplier Code
Cement Source / Plant	St. Marys Detroit	Air Entrainer* (Source/Prod/Type) w/ticket code		BASF MasterAir AE 200	AE	XUE12
Cement Type	I	WR** (Source/Prod/Type) w/ticket code		BASF MasterPozzolith 200	D	XUN12
Cement Specific Gravity	3.15	MR*** (Source/Prod/Type) w/ticket code		NA	NA	NA
Fly Ash Source (distributor & plant)	NA	HR**** (Source/Prod/Type) w/ticket code		NA	NA	NA
Fly Ash Class	NA	Accelerator (Source/Prod/Type) w/ticket code		NA	NA	NA
Fly Ash Specific Gravity	NA	Other (Source/Prod/Type) w/ ticket code		NA	NA	NA
Slag Cement Source	St. Marys					
Slag Cement Grade	100					
Slag Cement Specific Gravity	2.9					
Other	NA					

TYPE OF MIX WINTER / SUMMER

* If AE dosage is less than 1.0 oz/cwt DO NOT REJECT refer to notes at end of QPL Admix Listings.

Water Reducer / *Mid-Range Water Reducer / ****High-Range Water Reducer

MIX PROPORTIONS					
Bulk Volume of Coarse Aggregate (DR)	0.66	Design Slump* (in)	3.0	Slump Range	(1.5-3)
Coarse Aggregate Weight (Dry)	1744	Specified Slump (in)	0 - 3		
Intermediate Aggregate Weight (Dry)	0	Design Air %	6.5%		
Fine Aggregate Weight (Dry)	1156	Specified Air %	5.5% - 8.5%		
Portland Cement Weight	493	PSI minimum required	3500		
Fly Ash Weight	0				
Fly Ash Percent of Cementitious	0	Total Cementitious	658		
Slag Cement Weight	165				
Slag Cement Percent of Cementitious	25	Yield cu/ft	27		
Total Water Weight	294				
Net Water Weight	258				
W/C (as designed)	0.39				
Air Entrainer* (dosage)	1.0 oz/cwt	HR (dosage)	NA	NA	
WR (dosage)	4.0 oz/cwt	Accelerator (dosage)	NA	NA	
MR (dosage)	NA	Other (dosage)	NA	NA	

I certify that all applicable standard test methods have been followed verifying the mix design and JMF:

Signature NXDonahue Digitally signed by NXDonahue
Date: 2020.01.22 12:29:40 -05'00'

MCA Level II Expiration Date: 4/15/2021

Date: 1/22/2020

Remarks:

Portland Cement Concrete (PCC) Mixture Design Verification:For PCC Grade: PNC**Mix Verification:** For Mix Number: HE75E7CNA032**Mix Verification Method:** 2Mix Verification tests conducted by: Superior Materials, LLC LaboratoryProject Number: 82000 Address: 10147 Grand RiverJob Number: 205935 City / State / Zip Brighton, MI 48116Telephone: 248-788-8000**Verification Mix Proportions***

Workability Factor, b/bo	0.66	
b/bo, Based on Unit Weight (DL) or (DR)	DR	
Coarse Aggregate Weight (Dry)	1744	
Intermediate Aggregate Weight (Dry)	0	
Fine Aggregate Weight (Dry)	1156	
Portland Cement Weight	493	
Fly Ash Weight	0	
Fly Ash Percent of Cementitious	0	
GGBFS Weight	165	
GGBFS Percent of Cementitious	25	
Total Water Weight	294	
Net Water Weight	258	
W/C (as designed)	0.39	
Air Entrainment (dosage)	1.0	oz/cwt
Water Reducer (dosage)	4.0	oz/cwt
Mid Range Water Reducer (dosage)	NA	NA
High Range Water Reducer (dosage)	NA	NA
Accelerator (dosage)	NA	NA
Other (dosage)	NA	NA

*Refer to accompanying JMF Form for specifics on materials used in concrete mix design.

Verification Mix Properties

Batch			
	1	2	3
Date of Batch	6/9/2018	11/6/2018	5/20/2019
Air Content	7.6	7	8
Slump	2.5	2.75	3
Temperature	75	67	66
Density (pcf)	144.2	142.6	144.2
Strength at	Days Old		
Cylinder 1			
Cylinder 2			
Average			
Strength at	7 Days Old		
Cylinder 1	0	3440	390
Cylinder 2			
Average	0	3440	390
Strength at	28 Days Old		
Cylinder 1	4370	4640	5940
Cylinder 2	6070	4910	5810
Average	5220	4775	5875

Statement of Verification

All applicable ACI and ASTM methods have been followed in verifying this mix design.

Signed: NANCY DONAHUEDate: 1/22/20Title: Technical Service / MCA-ACI Level II Certified Technician

JOB MIX FORMULA (JMF) CONCRETE FIELD COMMUNICATION

This form applies only to the project listed below and is not transferable to other projects
DISTRIBUTION: ORIGINAL - Project Engineer COPIES - Contractor, Lansing CFS, Region, Inspector

CONTROL SECTION 82000	JOB NUMBER 205935	PROJECT LOCATION VARIOUS LOCATIONS	PROJECT ENGINEER JOHN J QUALEY III
CONCRETE SUPPLIER Superior Materials		PLANT LOCATION 8911 W. Jefferson, Detroit, MI 48209	PLANT NUMBER Plant 32 (M-02)
GRADE OF CONCRETE PNC	PSI REQUIREMENT 3500	MIX DESIGN NUMBER HE75E8CNA032	INTENDED USE (S) STRUCTURE ADJUSTMENTS
PRIME / SUBCONTRACTOR (S)		CONTRACTOR OC PLAN SUBMITTED? (MDOT use only) Y ☐ N ☐	
MERLO CONSTRUCTION CO. INC.			
STANDARD SPEC DATE 2012	QC/QA SPECIAL PROVISION 12SP-604A-09	DATE 6/11/2018	JMF EFFECTIVE DATE 1/22/2020
		AGG. CORRECTION 0.2	

MATERIALS DESIGN SOURCES AND PROPERTIES

COARSE AGGREGATE		INTERMEDIATE AGGREGATE		FINE AGGREGATE	
Aggregate Type	limestone	Aggregate Type	NA	Source Name	Levy - Ray Road
Source Name	Presque Isle	Source Name	NA	MDOT Source Number	63-115
MDOT Source Number	71-47	MDOT Source Number	NA	MDOT Series Class	2NS
MDOT Series Class	6AA	MDOT Series Class	NA	Specific Gravity (Bulk Dry)*	2.62
Specific Gravity (Bulk Dry)*	2.56	Specific Gravity (Bulk Dry)*	NA	Specific Gravity (Bulk SSD) optional	
Specific Gravity (Bulk SSD) optional		Specific Gravity (Bulk SSD) optional		Absorption	1.1
Absorption	1.3	Absorption	0	Fineness Modulus (FM)	2.86
Unit Weight (Dry Rodded) DR or	98	Unit Weight (Dry Rodded) DR or	0		
Unit Weight (Dry Loose) DL		Unit Weight (Dry Loose) DL			
Percent Crushed	100	Percent Crushed	100		
MDOT Freeze-Thaw (F-T) Dilation	0.016	MDOT Freeze-Thaw (F-T) Dilation	NA		
Specific Gravity (Bulk Dry) of F-T Sample *	2.56	Specific Gravity (Bulk Dry) of F-T Sample *	NA		
Date of MDOT Freeze-Thaw Report	5/8/2014	Date of MDOT Freeze-Thaw Report	NA		

* If the bulk specific gravity is more than 0.04 less than the bulk dry specific gravity of the most recently tested freeze-thaw sample, the aggregate will be considered to have changed characteristics and be required to have a new freeze-thaw test conducted prior to use on Department projects.

CEMENTITIOUS		ADMIXTURES		Manufacturer/Product Name	Type	Supplier Code
Cement Source / Plant	St. Marys Detroit	Air Entrainer* (Source/Prod/Type) w/ticket code		BASF MasterAir AE 200	AE	XUE12
Cement Type	I	WR** (Source/Prod/Type) w/ticket code		BASF MasterPozzolith 200	D	XUN12
Cement Specific Gravity	3.15	MR*** (Source/Prod/Type) w/ticket code		BASF MasterPolyheed 997	MR	XUM11
Fly Ash Source (distributor & plant)	NA	HR**** (Source/Prod/Type) w/ticket code		NA	NA	NA
Fly Ash Class	NA	Accelerator (Source/Prod/Type) w/ticket code		NA	NA	NA
Fly Ash Specific Gravity	NA	Other (Source/Prod/Type) w/ ticket code		NA	NA	NA
Slag Cement Source	St. Marys					
Slag Cement Grade	100					
Slag Cement Specific Gravity	2.9					
Other	NA					

TYPE OF MIX WINTER / SUMMER

* If AE dosage is less than 1.0 oz/cwt DO NOT REJECT refer to notes at end of QPL Admix Listings.

Water Reducer / *Mid-Range Water Reducer / ****High-Range Water Reducer

MIX PROPORTIONS

Bulk Volume of Coarse Aggregate (DR)	0.66	Design Slump* (in)	5.0 (3.5-6)
Coarse Aggregate Weight (Dry)	1744	Specified Slump (in)	0 - 6
Intermediate Aggregate Weight (Dry)	0	Design Air %	6.5%
Fine Aggregate Weight (Dry)	1156	Specified Air %	5.5% - 8.5%
Portland Cement Weight	493	PSI minimum required	3500
Fly Ash Weight	0		
Fly Ash Percent of Cementitious	0	Total Cementitious	658
Slag Cement Weight	165		
Slag Cement Percent of Cementitious	25	Yield cu/ft	27
Total Water Weight	294		
Net Water Weight	258		
W/C (as designed)	0.39		
Air Entrainer* (dosage)	1.0 oz/cwt	HR (dosage)	NA NA
WR (dosage)	4.0 oz/cwt	Accelerator (dosage)	NA NA
MR (dosage)	8.0 oz/cwt	Other (dosage)	NA NA

I certify that all applicable standard test methods have been followed verifying the mix design and JMF:

Signature **NXDonahue** Digitally signed by NXDonahue
Date: 2020.01.22 12:29:58 -05'00'

MCA Level II Expiration Date: 4/15/2021

Date: 1/22/2020

Remarks:

Portland Cement Concrete (PCC) Mixture Design Verification:For PCC Grade: PNC**Mix Verification:** For Mix Number: HE75E8CNA032**Mix Verification Method:** 2Mix Verification tests conducted by: Superior Materials, LLC LaboratoryProject Number: 82000 Address: 10147 Grand RiverJob Number: 205935 City / State / Zip Brighton, MI 48116Telephone: 248-788-8000**Verification Mix Proportions***

Workability Factor, b/bo	0.66	
b/bo, Based on Unit Weight (DL) or (DR)	DR	
Coarse Aggregate Weight (Dry)	1744	
Intermediate Aggregate Weight (Dry)	0	
Fine Aggregate Weight (Dry)	1156	
Portland Cement Weight	493	
Fly Ash Weight	0	
Fly Ash Percent of Cementitious	0	
GGBFS Weight	165	
GGBFS Percent of Cementitious	25	
Total Water Weight	294	
Net Water Weight	258	
W/C (as designed)	0.39	
Air Entrainment (dosage)	1.0	oz/cwt
Water Reducer (dosage)	4.0	oz/cwt
Mid Range Water Reducer (dosage)	8.0	oz/cwt
High Range Water Reducer (dosage)	NA	NA
Accelerator (dosage)	NA	NA
Other (dosage)	NA	NA

*Refer to accompanying JMF Form for specifics on materials used in concrete mix design.

Verification Mix Properties

Batch			
	1	2	3
Date of Batch	8/22/2019	9/13/2019	10/23/2019
Air Content	7.2	6.5	6.8
Slump	6	5	5.75
Temperature	80	81	65
Density (pcf)	141.2	141.8	141.5
Strength at	Days Old		
Cylinder 1			
Cylinder 2			
Average			
Strength at	7 Days Old		
Cylinder 1	3730	3910	4810
Cylinder 2			
Average	3730	3910	4810
Strength at	28 Days Old		
Cylinder 1	6190	5490	6070
Cylinder 2	6210	5520	6130
Average	6200	5505	6100

Statement of Verification

All applicable ACI and ASTM methods have been followed in verifying this mix design.

Signed: NANCY DONAHUEDate: 1/22/20Title: Technical Service / MCA-ACI Level II Certified Technician

JOB MIX FORMULA (JMF) CONCRETE FIELD COMMUNICATION

This form applies only to the project listed below and is not transferable to other projects
DISTRIBUTION: ORIGINAL - Project Engineer COPIES - Contractor, Lansing CFS, Region, Inspector

CONTROL SECTION 82000	JOB NUMBER 205935	PROJECT LOCATION VARIOUS LOCATIONS	PROJECT ENGINEER JOHN J QUALEY III
CONCRETE SUPPLIER Superior Materials		PLANT LOCATION 8911 W. Jefferson, Detroit, MI 48209	PLANT NUMBER Plant 32 (M-02)
GRADE OF CONCRETE P1	PSI REQUIREMENT 3500	MIX DESIGN NUMBER P155E7CNA032	INTENDED USE (S) STRUCTURE ADJUSTMENTS
PRIME / SUBCONTRACTOR (S) MERLO CONSTRUCTION CO. INC.		CONTRACTOR OC PLAN SUBMITTED? (MDOT use only) Y ☐ N ☐	
STANDARD SPEC DATE 2012	QC/QA SPECIAL PROVISION 12SP-604A-09	DATE 6/11/2018	JMF EFFECTIVE DATE 1/22/2020
		AGG. CORRECTION 0.2	

MATERIALS DESIGN SOURCES AND PROPERTIES					
COARSE AGGREGATE		INTERMEDIATE AGGREGATE		FINE AGGREGATE	
Aggregate Type	limestone	Aggregate Type	NA	Aggregate Type	Levy - Ray Road
Source Name	Presque Isle	Source Name	NA	Source Name	
MDOT Source Number	71-47	MDOT Source Number	NA	MDOT Source Number	63-115
MDOT Series Class	6AA	MDOT Series Class	NA	MDOT Series Class	2NS
Specific Gravity (Bulk Dry)*	2.56	Specific Gravity (Bulk Dry)*	NA	Specific Gravity (Bulk Dry)	2.62
Specific Gravity (Bulk SSD) optional		Specific Gravity (Bulk SSD) optional		Specific Gravity (Bulk SSD) optional	
Absorption	1.3	Absorption	0	Absorption	1.1
Unit Weight (Dry Rodded) DR or	98	Unit Weight (Dry Rodded) DR or	0	Fineness Modulus (FM)	2.86
Unit Weight (Dry Loose) DL		Unit Weight (Dry Loose) DL			
Percent Crushed	100	Percent Crushed	100		
MDOT Freeze-Thaw (F-T) Dilation	0.016	MDOT Freeze-Thaw (F-T) Dilation	NA		
Specific Gravity (Bulk Dry) of F-T Sample *	2.56	Specific Gravity (Bulk Dry) of F-T Sample *	NA		
Date of MDOT Freeze-Thaw Report	5/8/2014	Date of MDOT Freeze-Thaw Report	NA		

* If the bulk specific gravity is more than 0.04 less than the bulk dry specific gravity of the most recently tested freeze-thaw sample, the aggregate will be considered to have changed characteristics and be required to have a new freeze-thaw test conducted prior to use on Department projects.

CEMENTITIOUS		ADMIXTURES		Manufacturer/Product Name	Type	Supplier Code
Cement Source / Plant	St. Marys Detroit	Air Entrainer* (Source/Prod/Type) w/ticket code		BASF MasterAir AE 200	AE	XUE12
Cement Type	I	WR** (Source/Prod/Type) w/ticket code		BASF MasterPozzolith 200	D	XUN12
Cement Specific Gravity	3.15	MR*** (Source/Prod/Type) w/ticket code		NA	NA	NA
Fly Ash Source (distributor & plant)	NA	HR**** (Source/Prod/Type) w/ticket code		NA	NA	NA
Fly Ash Class	NA	Accelerator (Source/Prod/Type) w/ticket code		NA	NA	NA
Fly Ash Specific Gravity	NA	Other (Source/Prod/Type) w/ ticket code		NA	NA	NA
Slag Cement Source	St. Marys					
Slag Cement Grade	100					
Slag Cement Specific Gravity	2.9					
Other	NA					

TYPE OF MIX WINTER / SUMMER

* If AE dosage is less than 1.0 oz/cwt DO NOT REJECT refer to notes at end of QPL Admix Listings.

Water Reducer / *Mid-Range Water Reducer / ****High-Range Water Reducer

MIX PROPORTIONS					
Bulk Volume of Coarse Aggregate (DR)	0.65	Design Slump* (in)	3.0	Slump Range	(1.5-3)
Coarse Aggregate Weight (Dry)	1724	Specified Slump (in)	0 - 3		
Intermediate Aggregate Weight (Dry)	0	Design Air %	6.5%		
Fine Aggregate Weight (Dry)	1338	Specified Air %	5.5% - 8.5%		
Portland Cement Weight	394	PSI minimum required	3500		
Fly Ash Weight	0				
Fly Ash Percent of Cementitious	0	Total Cementitious	526		
Slag Cement Weight	132				
Slag Cement Percent of Cementitious	25	Yield cu/ft	27		
Total Water Weight	277				
Net Water Weight	239				
W/C (as designed)	0.45				
Air Entrainer* (dosage)	1.0 oz/cwt	HR (dosage)	NA	NA	
WR (dosage)	4.0 oz/cwt	Accelerator (dosage)	NA	NA	
MR (dosage)	NA	Other (dosage)	NA	NA	

I certify that all applicable standard test methods have been followed verifying the mix design and JMF:

Signature **NXDonahue** Digitally signed by NXDonahue
Date: 2020.01.22 12:30:10 -0500
MCA Level II Expiration Date: 4/15/2021
Date: 1/22/2020

Remarks:

Portland Cement Concrete (PCC) Mixture Design Verification:For PCC Grade: P1**Mix Verification:** For Mix Number: P155E7CNA032**Mix Verification Method:** 2Mix Verification tests conducted by: Superior Materials, LLC LaboratoryProject Number: 82000 Address: 10147 Grand RiverJob Number: 205935 City / State / Zip Brighton, MI 48116Telephone: 248-788-8000**Verification Mix Proportions***

Workability Factor, b/bo	0.65	
b/bo, Based on Unit Weight (DL) or (DR)	DR	
Coarse Aggregate Weight (Dry)	1724	
Intermediate Aggregate Weight (Dry)	0	
Fine Aggregate Weight (Dry)	1338	
Portland Cement Weight	394	
Fly Ash Weight	0	
Fly Ash Percent of Cementitious	0	
GGBFS Weight	132	
GGBFS Percent of Cementitious	25	
Total Water Weight	277	
Net Water Weight	239	
W/C (as designed)	0.45	
Air Entrainment (dosage)	1.0	oz/cwt
Water Reducer (dosage)	4.0	oz/cwt
Mid Range Water Reducer (dosage)	NA	NA
High Range Water Reducer (dosage)	NA	NA
Accelerator (dosage)	NA	NA
Other (dosage)	NA	NA

*Refer to accompanying JMF Form for specifics on materials used in concrete mix design.

Verification Mix Properties

Batch			
	1	2	3
Date of Batch	8/20/2019	8/21/2019	9/10/2019
Air Content	6.4	7	5.8
Slump	2.5	3	3
Temperature	81	78	74
Density (pcf)	141	140.5	141.5
Strength at	Days Old		
Cylinder 1			
Cylinder 2			
Average			
Strength at	7 Days Old		
Cylinder 1	5380	3820	0
Cylinder 2			
Average	5380	3820	0
Strength at	28 Days Old		
Cylinder 1	6970	4510	5970
Cylinder 2	6910	5180	5840
Average	6940	4845	5905

Statement of Verification

All applicable ACI and ASTM methods have been followed in verifying this mix design.

Signed: NANCY DONAHUEDate: 1/22/20Title: Technical Service / MCA-ACI Level II Certified Technician

JOB MIX FORMULA (JMF) CONCRETE FIELD COMMUNICATION

This form applies only to the project listed below and is not transferable to other projects
DISTRIBUTION: ORIGINAL - Project Engineer COPIES - Contractor, Lansing CFS, Region, Inspector

CONTROL SECTION 82000	JOB NUMBER 205935	PROJECT LOCATION VARIOUS LOCATIONS	PROJECT ENGINEER JOHN J QUALEY III
CONCRETE SUPPLIER Superior Materials		PLANT LOCATION 8911 W. Jefferson, Detroit, MI 48209	PLANT NUMBER Plant 32 (M-02)
GRADE OF CONCRETE P1	PSI REQUIREMENT 3500	MIX DESIGN NUMBER P155ERCNA032	INTENDED USE (S) STRUCTURE ADJUSTMENTS
PRIME / SUBCONTRACTOR (S) MERLO CONSTRUCTION CO. INC.		CONTRACTOR OC PLAN SUBMITTED? (MDOT use only) Y ☐ N ☐	
STANDARD SPEC DATE 2012	QC/QA SPECIAL PROVISION 12SP-604A-09	DATE 6/11/2018	JMF EFFECTIVE DATE 1/22/2020
		AGG. CORRECTION 0.2	

MATERIALS DESIGN SOURCES AND PROPERTIES					
COARSE AGGREGATE		INTERMEDIATE AGGREGATE		FINE AGGREGATE	
Aggregate Type	limestone	Aggregate Type	NA	Aggregate Type	Levy - Ray Road
Source Name	Presque Isle	Source Name	NA	Source Name	
MDOT Source Number	71-47	MDOT Source Number	NA	MDOT Source Number	63-115
MDOT Series Class	6AA	MDOT Series Class	NA	MDOT Series Class	2NS
Specific Gravity (Bulk Dry)*	2.56	Specific Gravity (Bulk Dry)*	NA	Specific Gravity (Bulk Dry)	2.62
Specific Gravity (Bulk SSD) optional		Specific Gravity (Bulk SSD) optional		Specific Gravity (Bulk SSD) optional	
Absorption	1.3	Absorption	0	Absorption	1.1
Unit Weight (Dry Rodded) DR or	98	Unit Weight (Dry Rodded) DR or	0	Fineness Modulus (FM)	2.86
Unit Weight (Dry Loose) DL		Unit Weight (Dry Loose) DL			
Percent Crushed	100	Percent Crushed	100		
MDOT Freeze-Thaw (F-T) Dilation	0.016	MDOT Freeze-Thaw (F-T) Dilation	NA		
Specific Gravity (Bulk Dry) of F-T Sample *	2.56	Specific Gravity (Bulk Dry) of F-T Sample *	NA		
Date of MDOT Freeze-Thaw Report	5/8/2014	Date of MDOT Freeze-Thaw Report	NA		

* If the bulk specific gravity is more than 0.04 less than the bulk dry specific gravity of the most recently tested freeze-thaw sample, the aggregate will be considered to have changed characteristics and be required to have a new freeze-thaw test conducted prior to use on Department projects.

CEMENTITIOUS		ADMIXTURES		Manufacturer/Product Name	Type	Supplier Code
Cement Source / Plant	St. Marys Detroit	Air Entrainer* (Source/Prod/Type) w/ticket code		BASF MasterAir AE 200	AE	XUE12
Cement Type	I	WR** (Source/Prod/Type) w/ticket code		BASF MasterPozzolith 200	D	XUN12
Cement Specific Gravity	3.15	MR*** (Source/Prod/Type) w/ticket code		BASF MasterPolyheed 997	MR	XUM11
Fly Ash Source (distributor & plant)	NA	HR**** (Source/Prod/Type) w/ticket code		NA	NA	NA
Fly Ash Class	NA	Accelerator (Source/Prod/Type) w/ticket code		NA	NA	NA
Fly Ash Specific Gravity	NA	Other (Source/Prod/Type) w/ ticket code		NA	NA	NA
Slag Cement Source	St. Marys					
Slag Cement Grade	100					
Slag Cement Specific Gravity	2.9					
Other	NA					

TYPE OF MIX WINTER / SUMMER

* If AE dosage is less than 1.0 oz/cwt DO NOT REJECT refer to notes at end of QPL Admix Listings.
Water Reducer / *Mid-Range Water Reducer / ****High-Range Water Reducer

MIX PROPORTIONS					
Bulk Volume of Coarse Aggregate (DR)	0.65	Design Slump* (in)	5.0	Slump Range	(3.5-6)
Coarse Aggregate Weight (Dry)	1724	Specified Slump (in)	0 - 6		
Intermediate Aggregate Weight (Dry)	0	Design Air %	6.5%		
Fine Aggregate Weight (Dry)	1338	Specified Air %	5.5% - 8.5%		
Portland Cement Weight	394	PSI minimum required	3500		
Fly Ash Weight	0				
Fly Ash Percent of Cementitious	0	Total Cementitious	526		
Slag Cement Weight	132				
Slag Cement Percent of Cementitious	25	Yield cu/ft	27		
Total Water Weight	277				
Net Water Weight	239				
W/C (as designed)	0.45				
Air Entrainer* (dosage)	1.0 oz/cwt	HR (dosage)	NA	NA	
WR (dosage)	4.0 oz/cwt	Accelerator (dosage)	NA	NA	
MR (dosage)	8.0 oz/cwt	Other (dosage)	NA	NA	

I certify that all applicable standard test methods have been followed verifying the mix design and JMF:

Signature **NXDonahue** Digitally signed by NXDonahue
Date: 2020.01.22 12:30:20 -05'00'

MCA Level II Expiration Date: 4/15/2021

Date: 1/22/2020

Remarks:

Portland Cement Concrete (PCC) Mixture Design Verification:For PCC Grade: P1**Mix Verification:** For Mix Number: P155ERCNA032**Mix Verification Method:** 2Mix Verification tests conducted by: Superior Materials, LLC LaboratoryProject Number: 82000 Address: 10147 Grand RiverJob Number: 205935 City / State / Zip Brighton, MI 48116Telephone: 248-788-8000**Verification Mix Proportions***

Workability Factor, b/bo	0.65	
b/bo, Based on Unit Weight (DL) or (DR)	DR	
Coarse Aggregate Weight (Dry)	1724	
Intermediate Aggregate Weight (Dry)	0	
Fine Aggregate Weight (Dry)	1338	
Portland Cement Weight	394	
Fly Ash Weight	0	
Fly Ash Percent of Cementitious	0	
GGBFS Weight	132	
GGBFS Percent of Cementitious	25	
Total Water Weight	277	
Net Water Weight	239	
W/C (as designed)	0.45	
Air Entrainment (dosage)	1.0	oz/cwt
Water Reducer (dosage)	4.0	oz/cwt
Mid Range Water Reducer (dosage)	8.0	oz/cwt
High Range Water Reducer (dosage)	NA	NA
Accelerator (dosage)	NA	NA
Other (dosage)	NA	NA

*Refer to accompanying JMF Form for specifics on materials used in concrete mix design.

Verification Mix Properties

Batch			
	1	2	3
Date of Batch	9/24/2019	9/26/2019	10/1/2019
Air Content	6.2	7.1	7
Slump	5.5	5.25	5
Temperature	76	68	76
Density (pcf)	141	140.4	140.5
Strength at	Days Old		
Cylinder 1			
Cylinder 2			
Average			
Strength at	7 Days Old		
Cylinder 1	0	0	0
Cylinder 2			
Average	0	0	0
Strength at	28 Days Old		
Cylinder 1	6290	5830	5490
Cylinder 2	5890	5290	5300
Average	6090	5560	5395

Statement of Verification

All applicable ACI and ASTM methods have been followed in verifying this mix design.

Signed: NANCY DONAHUEDate: 1/22/20Title: Technical Service / MCA-ACI Level II Certified Technician

JOB MIX FORMULA (JMF) CONCRETE FIELD COMMUNICATION

This form applies only to the project listed below and is not transferable to other projects
DISTRIBUTION: ORIGINAL - Project Engineer COPIES - Contractor, Lansing CFS, Region, Inspector

CONTROL SECTION 82000	JOB NUMBER 205935	PROJECT LOCATION VARIOUS LOCATIONS	PROJECT ENGINEER JOHN J QUALEY III
CONCRETE SUPPLIER Superior Materials		PLANT LOCATION 8911 W. Jefferson, Detroit, MI 48209	PLANT NUMBER Plant 32 (M-02)
GRADE OF CONCRETE S1	PSI REQUIREMENT 4000	MIX DESIGN NUMBER S1H5ERCQA032	INTENDED USE (S) FOUNDATIONS
PRIME / SUBCONTRACTOR (S)		CONTRACTOR OC PLAN SUBMITTED? (MDOT use only) Y ☐ N ☐	
MERLO CONSTRUCTION CO. INC.			
STANDARD SPEC DATE 2012	QC/QA SPECIAL PROVISION 12SP-604A-09	DATE 6/11/2018	JMF EFFECTIVE DATE 11/25/2019
		AGG. CORRECTION 0.2	

MATERIALS DESIGN SOURCES AND PROPERTIES					
COARSE AGGREGATE		INTERMEDIATE AGGREGATE		FINE AGGREGATE	
Aggregate Type	limestone	Aggregate Type	NA	Source Name	Smelter Bay - Maple Ridge
Source Name	Presque Isle	Source Name	NA	MDOT Source Number	95-013
MDOT Source Number	71-47	MDOT Source Number	NA	MDOT Series Class	2NS
MDOT Series Class	6AA	MDOT Series Class	NA	Specific Gravity (Bulk Dry)*	2.62
Specific Gravity (Bulk Dry)*	2.56	Specific Gravity (Bulk Dry)*	NA	Specific Gravity (Bulk SSD) optional	
Specific Gravity (Bulk SSD) optional		Specific Gravity (Bulk SSD) optional		Absorption	0.68
Absorption	1.3	Absorption	0	Fineness Modulus (FM)	2.72
Unit Weight (Dry Rodded) DR or	98	Unit Weight (Dry Rodded) DR or	0		
Unit Weight (Dry Loose) DL		Unit Weight (Dry Loose) DL			
Percent Crushed	100	Percent Crushed	100		
MDOT Freeze-Thaw (F-T) Dilatation	0.016	MDOT Freeze-Thaw (F-T) Dilatation	NA		
Specific Gravity (Bulk Dry) of F-T Sample *	2.56	Specific Gravity (Bulk Dry) of F-T Sample *	NA		
Date of MDOT Freeze-Thaw Report	5/8/2014	Date of MDOT Freeze-Thaw Report	NA		

* If the bulk specific gravity is more than 0.04 less than the bulk dry specific gravity of the most recently tested freeze-thaw sample, the aggregate will be considered to have changed characteristics and be required to have a new freeze-thaw test conducted prior to use on Department projects.

CEMENTITIOUS		ADMIXTURES		Manufacturer/Product Name	Type	Supplier Code
Cement Source / Plant	St. Marys Detroit	Air Entrainer* (Source/Prod/Type) w/ticket code		BASF MasterAir AE 200	AE	XUE12
Cement Type	I	WR** (Source/Prod/Type) w/ticket code		BASF MasterPozzolith 200	D	XUN12
Cement Specific Gravity	3.15	MR*** (Source/Prod/Type) w/ticket code		BASF MasterPolyheed 997	MR	XUM11
Fly Ash Source (distributor & plant)	NA	HR**** (Source/Prod/Type) w/ticket code		NA	NA	NA
Fly Ash Class	NA	Accelerator (Source/Prod/Type) w/ticket code		NA	NA	NA
Fly Ash Specific Gravity	NA	Other (Source/Prod/Type) w/ ticket code		NA	NA	NA
Slag Cement Source	St. Marys					
Slag Cement Grade	100					
Slag Cement Specific Gravity	2.9					
Other	NA					

TYPE OF MIX WINTER / SUMMER

* If AE dosage is less than 1.0 oz/cwt DO NOT REJECT refer to notes at end of QPL Admix Listings.

Water Reducer / *Mid-Range Water Reducer / ****High-Range Water Reducer

MIX PROPORTIONS					
Bulk Volume of Coarse Aggregate (DR)	0.65	Design Slump* (in)	5.0	Slump Range	(3.5-6)
Coarse Aggregate Weight (Dry)	1708	Specified Slump (in)	0 - 6		
Intermediate Aggregate Weight (Dry)	0	Design Air %	6.5%		
Fine Aggregate Weight (Dry)	1220	Specified Air %	5.5% - 8.5%		
Portland Cement Weight	458	PSI minimum required	3500		
Fly Ash Weight	0				
Fly Ash Percent of Cementitious	0	Total Cementitious	611		
Slag Cement Weight	153				
Slag Cement Percent of Cementitious	25	Yield cu/ft	27		
Total Water Weight	296				
Net Water Weight	265				
W/C (as designed)	0.43				
Air Entrainer* (dosage)	1.0 oz/cwt	HR (dosage)	NA	NA	
WR (dosage)	4.0 oz/cwt	Accelerator (dosage)	NA	NA	
MR (dosage)	8.0 oz/cwt	Other (dosage)	NA	NA	

I certify that all applicable standard test methods have been followed verifying the mix design and JMF:

Signature **NXDonahue** Digitally signed by NXDonahue
Date: 2020.01.22 12:30:41 -05'00'

MCA Level II Expiration Date: 4/15/2021

Date: 11/25/2019

Remarks:

Portland Cement Concrete (PCC) Mixture Design Verification:For PCC Grade: S1**Mix Verification:** For Mix Number: S1H5ERCQA032**Mix Verification Method:** 2Mix Verification tests conducted by: Superior Materials, LLC LaboratoryProject Number: 82000 Address: 10147 Grand RiverJob Number: 205935 City / State / Zip Brighton, MI 48116Telephone: 248-788-8000**Verification Mix Proportions***

Workability Factor, b/bo	0.65	
b/bo, Based on Unit Weight (DL) or (DR)	DR	
Coarse Aggregate Weight (Dry)	1708	
Intermediate Aggregate Weight (Dry)	0	
Fine Aggregate Weight (Dry)	1220	
Portland Cement Weight	458	
Fly Ash Weight	0	
Fly Ash Percent of Cementitious	0	
GGBFS Weight	153	
GGBFS Percent of Cementitious	25	
Total Water Weight	296	
Net Water Weight	265	
W/C (as designed)	0.43	
Air Entrainment (dosage)	1.0	oz/cwt
Water Reducer (dosage)	4.0	oz/cwt
Mid Range Water Reducer (dosage)	8.0	oz/cwt
High Range Water Reducer (dosage)	NA	NA
Accelerator (dosage)	NA	NA
Other (dosage)	NA	NA

*Refer to accompanying JMF Form for specifics on materials used in concrete mix design.

Verification Mix Properties

Batch			
	1	2	3
Date of Batch	8/22/2018	9/6/2018	6/8/2019
Air Content	7.6	8	7
Slump	5.25	5.75	5.5
Temperature	79	82	75
Density (pcf)	140.5	140.1	141
Strength at	Days Old		
Cylinder 1			
Cylinder 2			
Average			
Strength at	7 Days Old		
Cylinder 1	4860	4060	3550
Cylinder 2			
Average	4860	4060	3550
Strength at	28 Days Old		
Cylinder 1	6000	5270	5290
Cylinder 2	5910	5490	5020
Average	5955	5380	5155

Statement of Verification

All applicable ACI and ASTM methods have been followed in verifying this mix design.

Signed: NANCY DONAHUEDate: 11/25/19Title: Technical Service / MCA-ACI Level II Certified Technician

SOP Ops82

Effective Date 1-5-03

SUPERIOR MATERIALS, INC STANDARD OPERATING PROCEDURE

FUNCTION	OPERATIONS	TOPIC	AGGREGATE STOCK PILE MANAGEMENT & USE
----------	------------	-------	--

OBJECTIVE (S): Standardized procedure for aggregates inventory and use during concrete production.

RESPONSIBILITY: Plant operators, yardmen, area managers.

(1) STATEMENT OF POLICY

- a. Proper aggregate inventory/use procedures are mandatory to eliminate material cross contamination and segregation issues as well as inventory balancing/control.
- b. The required procedures apply for all concrete production facilities – including both wet and dry batched plants, and the block plant.

(2) REQUIRED PROCEDURES

- a. Before any aggregate(s) are received in the yards:
 - Appropriately sized storage bins (as determined by the applicable area manager) must be constructed.
 - i. The area selected must be pitched to prevent rain-water or rain-bird collection/ponding.
 - ii. The area selected must be not impede gravel train or front loader traffic.
 1. Do not allow mixer traffic and aggregate traffic to cross.
 - iii. Use interlocking concrete blocks erected to an elevation of 8'.
 1. The block storage bin must have three sides and an open face.
 - iv. Label each yard storage bin with lettering at least 12" in height. Use the following designations for labeling:

1. 6AA, 6A, 2NS, 467, 29A, 26A, HAYDITE C, HAYDITE B, 17A, PEASTONE, 31A, 6AASLAG

- b. When receiving raw materials into the yard:
 - All delivery tickets must be signed by the plant operator, before dumping.
 - The plant operator will retain a copy of the delivery.
 - The plant operator will maintain inventory in Oracle PPM and the Spectrum/Eagle batch computer.
 - The plant operator will inter-office mail these tickets to Farmington Hills office at the end of each day.
- c. Maintaining aggregate stock piles:
 - The yardman will keep the stock pile levels so that the do not extend beyond, or outside of the concrete block yard storage bins.
 - For aggregate sizes of 1.5" or larger, the stone must be remixed with the loader during stock pile maintenance.
 - The yardman will operate the rain-birds (aggregate stock pile water sprinklers) from 5/1 to 9/1.
- d. Using aggregates:
 - When loading the plant(s) with aggregates from stockpiles, work across the entire face of the stock pile to prevent segregation.
 - To prevent segregation, keep the plant aggregate bins full at all times.

(3) RESPONSIBILITIES

- a. Plant operators and area managers are responsible for training of gravel train drivers and yardmen on procedure execution.
- b. Plant operators and yardmen are responsible for procedure execution.

Approved By: _____

Date: _____

National Ready Mixed Concrete Association



Certificate of Conformance For Concrete Production Facilities

THIS IS TO CERTIFY THAT

Jefferson Avenue Plant 32, Detroit, MI

Superior Materials, LLC

has been inspected by the undersigned licensed professional engineer for conformance with the requirements of the *Check List for Ready Mixed Concrete Production Facilities*. As of the inspection date, the facilities met the requirements for production by

*Truck Mixing with Automatic Batching and Recordings of
Cementitious Materials, Aggregate, Water, and Chemical Admixtures*



Signature of Licensed Professional Engineer

January 18, 2018

Inspection Date

January 28, 2020

Certification Expiration Date

This company will maintain these facilities in compliance with the *Check List* requirements and will correct promptly any deficiencies which develop.

Signature of Company Official

Operations Manager

Title of Company Official

NOTICE: The Check List indicates only that plant facilities are satisfactory for the production of concrete when properly operated. Conformance of the concrete itself with specification requirements must be verified by usual inspection methods in accordance with sales agreements.

This certificate is issued by the National Ready Mixed Concrete Association on verification that the production facility conforms to the requirements of the NRMCA Certification of Ready Mixed Concrete Production Facilities, QCS. Unauthorized reproduction or misuse of this certificate may result in legal action.

Plant ID #: 800340

Certification ID #: 22464

© 1965, 1992, 2001, 2002, 2006, 2007, 2012

National Ready Mixed Concrete Association 900 Spring Street • Silver Spring • Maryland 20910



WORK ORDER

Great Lakes Scale

35380 UNION LAKE RD
HARRISON TOWNSHIP, MI 48045
Phone: (586) 776-0517
Fax: (586) 776-3169
Fed Tax ID: 38-3206325

Work Order# 0027354-1

Request Date 11/1/2019 2:08:00 PM

Schedule Date 11/4/2019 9:00:00 AM

Bill To SUP0896

SUP0896
SUPERIOR MATERIALS HOLDINGS LLC
PO BOX 2900
FARMINGTON HILLS, MI, 48336
(248) 788-8000

Ship To SUP1173

SUP1173
SUPERIOR MATERIALS 32
8911 WEST JEFFERSON
DETROIT, MI,
(248) 788-8000

Customer P.O

Requester DAN THOMAS

Phone (248) 788-8048

Email delthomas@superiormaterials.net

CONTRACT TYPE: No Contract

DESCRIPTION:

TASK DESCRIPTION

SERVICE TYPE: CAL

SCALE CHECK WAYNE COUNTY 9 AM

Service Date 11/4/2019

2 hours minimum portal to portal

WORK PERFORMED

CALL COMPLETE

CALIBRATIONS COMPLETE. Test scales with county inspector. Couldn't start right away due to customer loading trucks. Then Hilo ran out of gas. Floors had to clean to move weights around. Agg was bad. Maint helped clean floor for agg. Setup on cement scale to check scale and belt guard was in way to drop chains. Customer told us to move to water so they could remove guard. Moved all equipment to water. Customer loaded trucks between scale checks. Had to wait to remove and install equipment. Cement was heavy customer recalibrated scale.

TECHNICIAN(S)


JOE BIELARZ, RAY MCCREARY

EQUIPMENT SERVICED	ASSET/UNIT #	SERIAL #	MODEL	LOCATION
10,000 x 5 lb	62821 CEMENT	62821 CEMENT	ALCON SCALE/INDICATOR / COMMAND	
6000 x 1	662821 WATER	662821 WATER	ALCON SCALE/INDICATOR / COMMAND	
40,000 x 20 lb	662821 AGG A	662821 AGG A	ALCON SCALE/INDICATOR / COMMAND	AGG A

PARTS LIST

Customer Signature

Name:



Certificate ID: 00001 CEMENT191104121113

Test Date: 11/04/2019

DETROIT, MI

ISO Number: MS-FM-CFM-001


(*) Make: ALKON Model: COMMAND SN#: 62821 CEMENT Capacity: 10000 lb Graduation: 5 lb

AS FOUND TEST USING TEST WEIGHTS

AS LEFT TEST USING TEST WEIGHTS

AS LEFT BUILD TEST

OVERALL TEST RESULTS: PASS



Customer: SUPERIOR MATERIALS 32
SUP1173 8911 WEST JEFFERSON

Test Date: 11/04/2019

I&O Number: MS-FM-CEM-001

CALIBRATION DATE	DUE DATE	TEST INTERVAL	SCALE ID	SCALE CLASS
11/04/2019	05/05/2020	Semi-Annually	662821 WATER	II
SCALE LOCATION		EQUIPMENT CONDITIONS		
		Working Clean		
SELECT NUMBER OF PM DAYS:	CAPACITY	6000 UOM	lb	INCREMENT
				1

AS LEFT TEST USING TEST WEIGHTS

Weight Applied		Reading		Error		Weight Applied		Reading		Error	
0	lb	0	lb	0	lb	0	lb	0	lb	0	lb
6000	lb	6000	lb	0	lb	1000	lb	1000	lb	0	lb
0	lb	0	lb	0	lb	2000	lb	2000	lb	0	lb
	lb		lb		lb	3000	lb	3000	lb	0	lb
	lb		lb		lb	4000	lb	4000	lb	0	lb
	lb		lb		lb	5000	lb	5000	lb	0	lb
	lb		lb		lb	6000	lb	6000	lb	0	lb
	lb		lb		lb		lb		lb		lb
	lb		lb		lb		lb		lb		lb
	lb		lb		lb		lb		lb		lb

[illegible]

Page 1 of 2



GREAT LAKES SCALE COMPANY
35380 UNION LAKE RD.
HARRISON TOWNSHIP, MI 48045
Phone: (586) 776-0517

Certificate of Calibration

Customer: SUPERIOR MATERIALS 32
SUP1173 8911 WEST JEFFERSON

Certificate ID: 0001021 AGG A101104120003

Test Date: 11/04/2019

DETROIT, MI

ISO Number: MS-FM-CEM-001

(*) Make: ALKON Model: COMMAND S/N: 562821 AGG A Capacity: 40000 LB Graduation: 20 LB

CALIBRATION DATE	DUE DATE	TEST INTERVAL	SCALE ID	SCALE CLASS
11/04/2019	05/05/2020	Semi-Annually	562821 AGG A	III L
SCALE LOCATION		EQUIPMENT CONDITIONS		
AGG A		Working	Clean	
SELECT NUMBER OF PM DAYS:		CAPACITY	40000 UOM LB	INCREMENT 20

AS FOUND TEST USING TEST WEIGHTS

AS LEFT TEST USING TEST WEIGHTS

Weight Applied	Reading	Error	Weight Applied	Reading	Error
0	LB 0	LB 0		LB	LB
6000	LB 6000	LB 0		LB	LB
0	LB 0	LB 0		LB	LB
1000	LB 1000	LB 0		LB	LB
2000	LB 2000	LB 0		LB	LB
3000	LB 3000	LB 0		LB	LB
4000	LB 4000	LB 0		LB	LB
5000	LB 5000	LB 0		LB	LB
6000	LB 6000	LB 0		LB	LB
0	LB 0	LB 0		LB	LB

AS LEFT BUILD TEST

Test Weight Applied	Material Weight Applied	Reading	Error
2000	LB 6000	LB 8000	LB 0
4000	LB 6000	LB 10000	LB 0
6000	LB 6000	LB 12000	LB 0
2000	LB 12000	LB 14000	LB 0
4000	LB 12000	LB 16000	LB 0
6000	LB 12000	LB 18000	LB 0
2000	LB 18000	LB 20000	LB 0
4000	LB 18000	LB 22000	LB 0
6000	LB 18000	LB 24000	LB 0
2000	LB 24000	LB 26000	LB 0
4000	LB 24000	LB 28000	LB 0
6000	LB 24000	LB 30000	LB 0
2000	LB 32000	LB 34000	LB 0
4000	LB 32000	LB 36000	LB 0
6000	LB 32000	LB 38000	LB 0
	LB	LB	LB
	LB	LB	LB
	LB	LB	LB
	LB	LB	LB

OVERALL TEST RESULTS PASS



WORK ORDER

Great Lakes Scale

35380 UNION LAKE RD
HARRISON TOWNSHIP, MI 48045
Phone: (586) 776-0517
Fax: (586) 776-3169
Fed Tax ID: 38-3206225

Bill To: SUP0896

SUP0896
SUPERIOR MATERIALS HOLDINGS LLC
PO BOX 2900
FARMINGTON HILLS, MI, 48336
(248) 788-8000

Ship To: SUP1175

SUP1175
SUPERIOR MATERIALS 32
8911 WEST JEFFERSON
DETROIT, MI,
(248) 788-8000

Work Order# 0027354-1

Request Date 11/1/2019 2:06:00 PM

Schedule Date 11/4/2019 9:00:00 AM

Customer P.O.

Requester DAN THOMAS

Phone (248) 788-8048

Email dethomas@superiormaterials.net

CONTRACT TYPE: No Contract

DESCRIPTION:

TASK DESCRIPTION

SERVICE TYPE: CAL

SCALE CHECK WAYNE COUNTY 9 AM

Service Date 11/4/2019

2 hours minimum portal to portal

WORK PERFORMED

CALL COMPLETE

CALIBRATIONS COMPLETE. Test scales with county inspector. Couldn't start right away due to customer loading trucks. Then Hilo ran out of gas. Floors had to clean to move weights around. Agg was bed. Maint helped clean floor for agg. Setup on cement scale to check scale and belt guard was in way to drop chains. Customer told us to move to water so they could remove guard. Moved all equipment to water. Customer loaded trucks between scale checks. Had to wait to remove and install equipment. Cement was heavy customer recalibrated scale.

TECHNICIAN(S)

JOE BIELAZ, RAY MCCREARY

EQUIPMENT SERVICED	ASSET/UNIT #	SERIAL #	MODEL	LOCATION
10,000 x 5 lb	662821 CEMENT	662821 CEMENT	ALCON SCALE/INDICATOR / COMMAND	
6000 x 1	662821 WATER	662821 WATER	ALCON SCALE/INDICATOR / COMMAND	
40,000 x 20 lb	662821 AGG A	662821 AGG A	ALCON SCALE/INDICATOR / COMMAND	AGG A

PARTS LIST

Customer Signature

Andrew



GREAT LAKES SCALE COMPANY
35380 UNION LAKE RD.
HARRISON TOWNSHIP, MI 48045
Phone: (586) 776-0517

Customer: SUPERIOR MATERIALS 32
SUP1173 8911 WEST JEFFERSON

Certificate ID: 1802021 AGG A181104120003

Test Date: 11/04/2019

DETROIT, MI

I80 Number: MS-FM-CEM-001

TEST INFORMATION

TEST WEIGHT CLASSIFICATION	EXPANDED UNCERTAINTY
F	15
ENVIRONMENTAL CONDITIONS	TEMPERATURE
Acceptable	55
WAS THE SCALE WITHIN CUSTOMERS REQUIRED ACCURACY?	
Yes	
TEST LOCATION	OVERALL RESULT
Onsite	Pass w/o adjustment

Comments:

TRACEABILITY CERTIFICATE NUMBERS:

Kit	NIST	Date	Date Due
Description			
GL0601	MI-06-19-14292	6/13/2019	6/13/2021
TRUCK 6 - 1000 LB			
GL0602	MI-06-19-14292	6/13/2019	6/13/2021
TRUCK 6 - 1000 LB			
GL0603	MI-06-19-14292	6/13/2019	6/13/2021
TRUCK 6 - 1000 LB			
GL0604	MI-06-19-14292	6/13/2019	6/13/2021
TRUCK 6 - 1000 LB			
GL0605	MI-06-19-14292	6/13/2019	6/13/2021
TRUCK 6 - 1000 LB			
GL0606	MI-06-19-14292	6/13/2019	6/13/2021
TRUCK 6 - 1000 LB			

Technician(s): RAY MCCREARY; Joe bielaz

Signature:

Devices were calibrated with the certified test weights. Adjustments made to restore and/or maintain the accuracy of the device conform to the tolerances established by NIST or Manufacturers Specifications. Best measurement of uncertainty calculated using a coverage factor of K=2. This provides confidence level of 95%.



GREAT LAKES SCALE COMPANY
35380 UNION LAKE RD.
HARRISON TOWNSHIP, MI 48045
Phone: (586) 776-0517

Customer: SUPERIOR MATERIALS 32
SUP1173 8911 WEST JEFFERSON

DETROIT, MI

Certificate ID: 060321 WATER121104120029

Test Date: 11/04/2019

ISO Number: MS-FM-CEM-001

TEST INFORMATION

TEST WEIGHT CLASSIFICATION	EXPANDED UNCERTAINTY
F	1.28
ENVIRONMENTAL CONDITIONS	TEMPERATURE
Acceptable	55
WAS THE SCALE WITHIN CUSTOMERS REQUIRED ACCURACY?	
Yes	
TEST LOCATION	OVERALL RESULT
Onsite	Pass w/o adjustment

Comments:

TRACEABILITY CERTIFICATE NUMBERS:

Kit	NIST	Date	Date Due
Description			
GL0601	MI-06-19-14292	6/13/2019	6/13/2021
TRUCK 6 - 1000 LB			
GL0602	MI-06-19-14292	6/13/2019	6/13/2021
TRUCK 6 - 1000 LB			
GL0603	MI-06-19-14292	6/13/2019	6/13/2021
TRUCK 6 - 1000 LB			
GL0604	MI-06-19-14292	6/13/2019	6/13/2021
TRUCK 6 - 1000 LB			
GL0605	MI-06-19-14292	6/13/2019	6/13/2021
TRUCK 6 - 1000 LB			
GL0606	MI-06-19-14292	6/13/2019	6/13/2021
TRUCK 6 - 1000 LB			

Technician(s): RAY MCCREARY; Joe B.

Signature:

Devices were calibrated with the certified test weights. Adjustments made to restore and/or maintain the accuracy of the device conform to the tolerances established by NIST or Manufacturers Specifications. Best measurement of uncertainty calculated using a coverage factor of K=2. This provides confidence level of 95%.



GREAT LAKES SCALE COMPANY
35380 UNION LAKE RD.
HARRISON TOWNSHIP, MI 48045
Phone: (586) 776-0517

Customer: SUPERIOR MATERIALS 32
SUP1173 8911 WEST JEFFERSON

DETROIT, MI

Certificate ID: 00021 CEMENT191104121113

Test Date: 11/04/2019

ISO Number: MS-FM-CEM-001

TEST INFORMATION

TEST WEIGHT CLASSIFICATION	EXPANDED UNCERTAINTY
F	3.50
ENVIRONMENTAL CONDITIONS	TEMPERATURE
Acceptable	55
WAS THE SCALE WITHIN CUSTOMERS REQUIRED ACCURACY?	
Yes	
TEST LOCATION	OVERALL RESULT
Onsite	Pass adjustment needed

Comments:

Test and cal scale with county inspector

TRACEABILITY CERTIFICATE NUMBERS:

Kit	NIST	Date	Date Due
Description			
GL0601	MI-06-19-14292	6/13/2019	6/13/2021
TRUCK 6 - 1000 LB			
GL0602	MI-06-19-14292	6/13/2019	6/13/2021
TRUCK 6 - 1000 LB			
GL0603	MI-06-19-14292	6/13/2019	6/13/2021
TRUCK 6 - 1000 LB			
GL0604	MI-06-19-14292	6/13/2019	6/13/2021
TRUCK 6 - 1000 LB			
GL0605	MI-06-19-14292	6/13/2019	6/13/2021
TRUCK 6 - 1000 LB			
GL0606	MI-06-19-14292	6/13/2019	6/13/2021
TRUCK 6 - 1000 LB			

Technician(s): RAY MCCREARY; Joe B

Signature:

Devices were calibrated with the certified test weights. Adjustments made to restore and/or maintain the accuracy of the device conform to the tolerances established by NIST or Manufacturers Specifications. Best measurement of uncertainty calculated using a coverage factor of K=2. This provides confidence level of 95%.



The Chemical Company

CUSTOMER LOCATION

Superior Jefferson Plant

ADMIXTURE	REQUIRED	MEASURED	OVER/UNDER
Masterair AE200	32oz	32oz	0
MasterPozzolith 200	42oz	42oz	0
MasterPolyheed 997	50oz	50oz	0
MasterPolyheed 100	50oz	50oz	0
MasterRheobuild1000	60oz	60oz	0
Masterset AC 534	60oz	60oz	0
Masterglenium 7925	40oz	40oz	0
Masterset Delvo	-----	-----	-----
MasterLife CI30	3 Gal	3 Gal	0
Water	150gal	150gal	0

To Whom It May Concern:

This letter is to certify that Admixture dispensing equipment was tested to meet the requirements for measuring material according to ASTM C-94 the standard specifications for Ready Mixed Concrete.

TESTED AND APPROVED BY: *Jacob Honey*

DATE: 01/10/20

BASF Admixtures, Inc.
23700 Chagrin Boulevard
Cleveland, Ohio 44122 USA
216 836-7500 ph
www.masterbuilders.com

**Master
Builders**

Admixture Solutions

BOWSER-MORNER, INC.

Delivery Address: 4518 Taylorsville Rd • Dayton, Ohio 45424 Mailing Address: P.O. Box 51 • Dayton, Ohio 45401

AASHTO/ISO 17025 Accredited • USACE Validated



LABORATORY REPORT

Report To: Levy Co.
Attn.: Mitchell Holt
8800 Dix Rd.
Detroit, MI 48209

Report Date: 01/15/20
Job No.: 187540
Report No.: 019278A
No. of Pages: 3

Report On: Laboratory Determination of Alkali-Silica Reactivity (ASR)

Procedure: Length Change of Concrete Due to Alkali-Silica Reaction (ASTM C 1293)

Material and Source Information

Sample Identification: MDOT 2NS
Fine Aggregate Source: Ray Rd. (Pit #63-115)
Coarse Aggregate Source: #57 crLS MMA Phillipsburg, OH
Cement Source: Fairborn Cement Company
Date Received: 11/26/18
Date Cast: 01/15/19

Results are summarized below and detailed on the attached data sheets.

Average Length Change, %		ASTM C 1293 Specification, %
56 Days:	0.011	---
90 Days:	0.015	---
180 Days:	0.026	---
270 Days:	0.028	---
365 Days:	0.030	0.040 Max.

Bowser-Morner certifies that this test was performed in accordance with ASTM C1293 procedures.

Should you have any questions, or if we may be of further service, please contact me at (937) 236-8805, ext. 329.

Respectfully submitted,

BOWSER-MORNER, INC.

Scott D. Ruhkamp, Supervisor
Special Projects Section
Construction Materials Laboratory

SDR/sdr
019278A
1-File
1-mholt@edwlevy.com

Report To: Levy Co.
 Sample ID: MDOT 2NS
 Source: Ray Rd. (Pit #63-115)

Job No.: 187540
 Report No.: 019278A
 Date Received: 11/26/18


Concrete Mixture Summary				
Aggregates Used	Type	Source	Grading	
Coarse (Lab Standard)	#57 crLS	MMA Phillipsburg	Table 1, coarse	
Fine (Subject)	MDOT 2NS	Ray Rd. (Pit #63-115)	Table 1, fine	
Cement Used	Source	Type	Na ₂ O Equiv., %	
Fairborn Cement Co.	Fairborn, OH	Portland Type I	0.8	
Pozzolan Used	Source	Type	Na ₂ O Equiv., %	
n/a	n/a	n/a	n/a	
Admixtures Used	Source	Type	Dosage Rate	
n/a	n/a	n/a	n/a	
Concrete Proportions, SSD, lbs/cubic yard				
Component	Source	Specific Gravity	Mass, lbs	Volume, cubic yard
Portland Cement	Fairborn Cement Co.*	3.15	708	3.60195
Water	BMI Standard	1.00	297	4.75962
#57 crLS	MMA Phillipsburg*	2.648	1847	11.17801
MDOT 2NS	Ray Rd. (Pit #63-115)	2.655	1207	7.28548
Entrained Air, %:	n/a	n/a	2.3	0.62100
Total	n/a	n/a	4059	27.4
*The cement and coarse aggregate used in this test are BMI's laboratory standards and meet sections 7.1 and 7.2				
Sodium Hydroxide Added, %	W/Cm	Slump, inches	Air, %	
0.4	0.419	3 3/4	2.3	
Fresh Unit Weight, cubic yard	Mass Yield, %			
149.7	100.4			
Storage Containers				
6-gallon (23-liter) plastic pail with gamma seal lid conforming to ASTM C1293, sections 5.2.1 and 5.3.1				

Report To: Levy Co.
Sample ID: MDOT 2NS
Source: Ray Rd. (P11 #63-115)
Date Cast: 01/15/19

Job No.: 187540
Report No.: 019278A
Date Received: 11/26/18
Ref. Rod Length: 11.631805

Procedure: Length Change of Concrete Due to Alkali-Silica Reaction (ASTM C 1293)

Age, Days	ID	Reference Rod, inch	Specimen Readings, inch	Expansion, inch	Length Change, %	Avg. %
Initial 01/16/19	A	0.0000	-0.0041	11.6277	n/a	0.0000
	B	0.0000	-0.0120	11.6198	n/a	
	C	0.0000	-0.0093	11.6225	n/a	
7 01/23/19	A	0.0000	-0.0039	11.6279	0.0020	0.0017
	B	0.0000	-0.0119	11.6199	0.0010	
	C	0.0000	-0.0091	11.6227	0.0020	
28 02/13/19	A	0.0000	-0.0035	11.6283	0.0060	0.0067
	B	0.0000	-0.0115	11.6203	0.0050	
	C	0.0000	-0.0084	11.6234	0.0090	
56 03/13/19	A	0.0000	-0.0032	11.6286	0.0090	0.0107
	B	0.0000	-0.0110	11.6208	0.0100	
	C	0.0000	-0.0080	11.6238	0.0130	
90 04/17/19	A	0.0000	-0.0027	11.6291	0.0140	0.0150
	B	0.0000	-0.0106	11.6212	0.0140	
	C	0.0000	-0.0076	11.6242	0.0170	
180 07/17/19	A	0.0000	-0.0017	11.6301	0.0240	0.0257
	B	0.0000	-0.0095	11.6223	0.0250	
	C	0.0000	-0.0065	11.6253	0.0280	
270 10/16/19	A	0.0000	-0.0014	11.6304	0.0270	0.0277
	B	0.0000	-0.0094	11.6224	0.0260	
	C	0.0000	-0.0063	11.6255	0.0300	
365 01/15/20	A	0.0000	-0.0013	11.6305	0.0280	0.0300
	B	0.0000	-0.0090	11.6228	0.0300	
	C	0.0000	-0.0061	11.6257	0.0320	

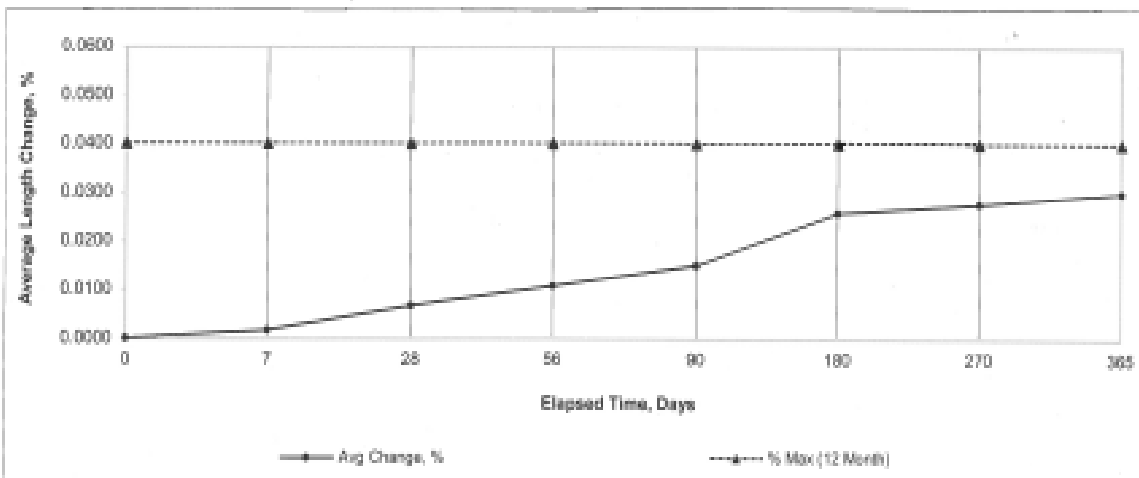



30701 West 10 Mile Rd.
Suite 500
Farmington Hills, Mi. 48336

ADMIXTURE GENERAL CERTIFICATION

Date: Wednesday, January 22, 2020
Contractor: MERLO CONSTRUCTION CO INC
Control Section: 82000 **Job No.:** 205935
QC/QA Spec. Prov.: 12SP-604A-09 **Date Effective:** 6/11/2018
Project/Location: VARIOUS LOCATIONS

We certify that the following described QPL materials have been tested and meets the specification requirements of the MICHIGAN DEPARTMENT OF TRANSPORTATION and ASTM, or MDOT Specs, and were provided and incorporated into the identified project.

The following admixtures are listed on the MDOT QUALIFIED PRODUCTS LIST (QPL) and may be used in the above listed project.

Table 903-1 (from 2012 Standard Specifications for Construction, Sec 903) ASTM C 494 Terms for Chemical Admixtures		
Type	Term	Manufacturer: BASF Construction Chemical Co.
A	Water-reducing admixtures	MasterPozzolith 200
C	Accelerating admixtures	MasterSet AC 534
D	Water-reducing and retarding admixtures	MasterPozzolith 200
E	Water-reducing and accelerating admixtures	NA
F	Water-reducing, high range admixtures	MasterRheobuild 1000
G	Water-reducing, high range, and retarding admixtures	NA

903.01 - Master Air AE 200

The Department refers to water-reducing, mid range admixtures, not included in ASTM C 494, as MR. Admixtures from BASF that fall under this "Type" are as follows:

MasterPolyheed 997

MasterPolyheed 100

All admixtures as used, meet the minimum dosage rates as set forth in MDOT's QPL.

Nancy Donahue
Technical Service
Superior Materials, LLC
(248) 640-2380 Cell
nxdonahue@superiormaterials.net

Serving All of Southeastern Michigan

Toll Free Order desk: (888) 988-4400 * Office: (248) 788-8000 * Fax: (248) 592-9074

BOWSER-MORNER, INC.

Delivery Address: 4518 Taylorsville Rd • Dayton, Ohio 45424 Mailing Address: P.O. Box 51 • Dayton, Ohio 45401

AASHTO/ISO 17025 Accredited • USACE Validated



LABORATORY REPORT

Report To: Levy Co.
Attn.: Mitchell Holt
8800 Dix Rd.
Detroit, MI 48209

Report Date: 01/15/20
Job No.: 187540
Report No.: 019278A
No. of Pages: 3

Report On: Laboratory Determination of Alkali-Silica Reactivity (ASR)

Procedure: Length Change of Concrete Due to Alkali-Silica Reaction (ASTM C 1293)

Material and Source Information

Sample Identification: MDOT 2NS
Fine Aggregate Source: Ray Rd. (Pit #63-115)
Coarse Aggregate Source: #57 crLS MMA Phillipsburg, OH
Cement Source: Fairborn Cement Company
Date Received: 11/26/18
Date Cast: 01/15/19

Results are summarized below and detailed on the attached data sheets.

Average Length Change, %		ASTM C 1293 Specification, %
56 Days:	0.011	---
90 Days:	0.015	---
180 Days:	0.026	---
270 Days:	0.028	---
365 Days:	0.030	0.040 Max.

Bowser-Morner certifies that this test was performed in accordance with ASTM C1293 procedures.

Should you have any questions, or if we may be of further service, please contact me at (937) 236-8805, ext. 329.

Respectfully submitted,

BOWSER-MORNER, INC.

Scott D. Ruhkamp, Supervisor
Special Projects Section
Construction Materials Laboratory

SDR/sdr
019278A
1-File
1-mholt@edwlevy.com

Report To: Levy Co.
 Sample ID: MDOT 2NS
 Source: Ray Rd. (Pit #63-115)

Job No.: 187540
 Report No.: 019278A
 Date Received: 11/26/18


Concrete Mixture Summary				
Aggregates Used	Type	Source	Grading	
Coarse (Lab Standard)	#57 crLS	MMA Phillipsburg	Table 1, coarse	
Fine (Subject)	MDOT 2NS	Ray Rd. (Pit #63-115)	Table 1, fine	
Cement Used	Source	Type	Na ₂ O Equiv., %	
Fairborn Cement Co.	Fairborn, OH	Portland Type I	0.8	
Pozzolan Used	Source	Type	Na ₂ O Equiv., %	
n/a	n/a	n/a	n/a	
Admixtures Used	Source	Type	Dosage Rate	
n/a	n/a	n/a	n/a	
Concrete Proportions, SSD, lbs/cubic yard				
Component	Source	Specific Gravity	Mass, lbs	Volume, cubic yard
Portland Cement	Fairborn Cement Co.*	3.15	708	3.60195
Water	BMI Standard	1.00	297	4.75962
#57 crLS	MMA Phillipsburg*	2.648	1847	11.17801
MDOT 2NS	Ray Rd. (Pit #63-115)	2.655	1207	7.28548
Entrained Air, %:	n/a	n/a	2.3	0.62100
Total	n/a	n/a	4059	27.4
*The cement and coarse aggregate used in this test are BMI's laboratory standards and meet sections 7.1 and 7.2				
Sodium Hydroxide Added, %	W/Cm	Slump, inches	Air, %	
0.4	0.419	3 3/4	2.3	
Fresh Unit Weight, cubic yard	Mass Yield, %			
149.7	100.4			
Storage Containers				
6-gallon (23-liter) plastic pail with gamma seal lid conforming to ASTM C1293, sections 5.2.1 and 5.3.1				

Report To: Levy Co.
Sample ID: MDOT 2NS
Source: Ray Rd. (P11 #63-115)
Date Cast: 01/15/19

Job No.: 187540
Report No.: 019278A
Date Received: 11/26/18
Ref. Rod Length: 11.631805

Procedure: Length Change of Concrete Due to Alkali-Silica Reaction (ASTM C 1293)

Age, Days	ID	Reference Rod, inch	Specimen Readings, inch	Expansion, inch	Length Change, %	Avg. %
Initial 01/16/19	A	0.0000	-0.0041	11.6277	n/a	0.0000
	B	0.0000	-0.0120	11.6198	n/a	
	C	0.0000	-0.0093	11.6225	n/a	
7 01/23/19	A	0.0000	-0.0039	11.6279	0.0020	0.0017
	B	0.0000	-0.0119	11.6199	0.0010	
	C	0.0000	-0.0091	11.6227	0.0020	
28 02/13/19	A	0.0000	-0.0035	11.6283	0.0060	0.0067
	B	0.0000	-0.0115	11.6203	0.0050	
	C	0.0000	-0.0084	11.6234	0.0090	
56 03/13/19	A	0.0000	-0.0032	11.6286	0.0090	0.0107
	B	0.0000	-0.0110	11.6208	0.0100	
	C	0.0000	-0.0080	11.6238	0.0130	
90 04/17/19	A	0.0000	-0.0027	11.6291	0.0140	0.0150
	B	0.0000	-0.0106	11.6212	0.0140	
	C	0.0000	-0.0076	11.6242	0.0170	
180 07/17/19	A	0.0000	-0.0017	11.6301	0.0240	0.0257
	B	0.0000	-0.0095	11.6223	0.0250	
	C	0.0000	-0.0065	11.6253	0.0280	
270 10/16/19	A	0.0000	-0.0014	11.6304	0.0270	0.0277
	B	0.0000	-0.0094	11.6224	0.0260	
	C	0.0000	-0.0063	11.6255	0.0300	
365 01/15/20	A	0.0000	-0.0013	11.6305	0.0280	0.0300
	B	0.0000	-0.0090	11.6228	0.0300	
	C	0.0000	-0.0061	11.6257	0.0320	

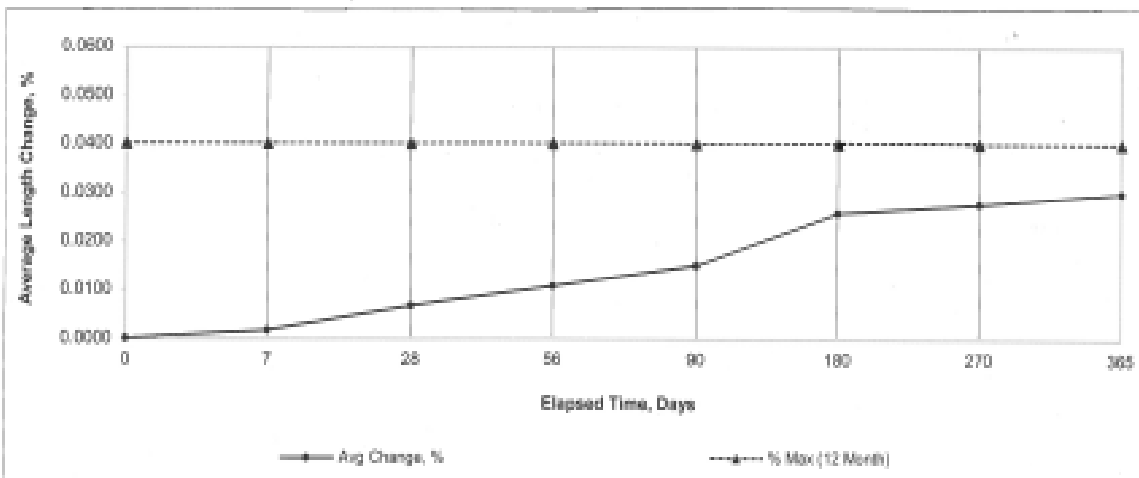

Portland Cement Type I/II

Production Period: 11/01/2019 to 11/30/2019

STANDARD REQUIREMENTS

Chemical Data			Physical Data		
Item	Spec. Limit	Results	Item	Spec. Limit	Results
SiO ₂ (%)		19.1	Air Content of mortar (volume %)	12.0 max	9
Al ₂ O ₃ (%)	6.0 max	5.1	Blaine fineness (m ² /kg)	260.0 min	409
Fe ₂ O ₃ (%)		3.26	Autoclave expansion (%)	0.8 max	0.05
CaO (%)		62.5			
MgO (%)	6.0 max	2.8	Compressive strength (MPa/psi):		
SO ₃ (%)*	3.0 max	3.83	1 day		17.6 [2555]
Loss of ignition (%)	3.5 max	1.5	3 days	12.0[1740] min	27.0 [3909]
Na ₂ O (%)		0.22	7 days	19.0[2760] min	30.9 [4470]
K ₂ O (%)		1.17	28 days	28.0[4060] min	39.2 [5679]
Insoluble residue (%)	1.5 max	0.35	Time of setting (minutes)		
CO ₂ (%)		1.4	(Vicat) Initial	45 - 375	88
Limestone (%)	5.0 max	3.3	(Vicat) Final		201
CaCO ₃ in limestone (%)	70.0 min	97.0			
Inorganic process addition(%)	5.0 max	0.0			
			Mortar Bar Expansion (ASTM C1038) (%)*	0.02 max	0.009
Potential phase composition			Base Cement Phase Composition		
C ₃ S (%)		56	C ₃ S (%)		56
C ₂ S (%)		12	C ₂ S (%)		12
C ₃ A (%)	8 max	8	C ₃ A (%)		8
C ₄ AF (%)		10	C ₄ AF (%)		10

OPTIONAL REQUIREMENTS

Item	Spec. Limit	Results	Item	Spec. Limit	Results
Equiv. Alkalies	A	0.99	False Set (%)	50 min	
			Retained 325 (%)		5.11

Additional Data

Type	Limestone	Inorganic Processing Addition
Amount	3.3	0.0
SiO ₂ (%)	2.1	
Al ₂ O ₃ (%)	0.6	
Fe ₂ O ₃ (%)	0.2	
CaO (%)	49.2	
SO ₃ (%)	0.4	

This cement meets ASTM C150, A3000 compendium, A3003, A3004, A3005 and CSA A3001 for Type I and Type II Portland Cement

*It is permissible to exceed the max value for SO₃ content, provided it is demonstrated by C-1038 that the cement will not develop expansion exceeding 0.02% in 14 Days

A Test result provided for information only.

December 17, 2019

St. Marys Cement
Detroit Plant

9333 Dearborn Avenue

Detroit, MI 48209

Tel: (313) 842-4600 - Fax: (313) 849-4512

Linda Harris

Linda M. Harris
Quality Control Manager

Slag Cement Grade 100 - Cemplus

Production Period: 11/01/2019 to 11/30/2019

STANDARD REQUIREMENTS - SLAG

Chemical Data			Physical Data		
Item	Spec. Limit	Results	Item	Spec. Limit	Results
Sulfide Sulfur (S) (%)	2.5 max	1.0	Air Content of mortar (volume %)	12 max	5
Sulfate Sulfur (as SO ₃) (%)		2.4	Blaine fineness (m ² /kg)	260 min	547
Added Sulfate Sulfur (as SO ₃) (%)			Retained 325 (%)		2.76
Inorganic process addition (%)	5.0 max		Compressive strength (MPa/psi):		
			7 days		22.9 [3316]
			28 days (previous month)		42.5 [6161]
			Slag Activity Index (%) (SAI)		
			7 Day		77.6
			28 Day	95 min	115.4

STANDARD REQUIREMENTS - REFERENCE CEMENT

Chemical Data			Physical Data		
Item	Spec. Limit	Results	Item	Spec. Limit	Results
Equiv. Alkalies	A	0.78	Blaine fineness (m ² /kg)	260 min	390
Potential phase composition			Compressive strength (MPa/psi):		
C ₃ S (%)		58	7 days		29.5 [4278]
C ₂ S (%)		15	28 days		36.8 [5339]
C ₃ A (%)		8			
C ₄ AF (%)		8			

ADDITIONAL DATA

Item		Item	Results
Type	Inorganic Processing Addition	Specific Gravity (g/cm ³)	2.91
Amount	0.0	Autoclave expansion (%)	0.04
SiO ₂ (%)			
Al ₂ O ₃ (%)			
Fe ₂ O ₃ (%)			
CaO (%)			
SO ₃ (%)			

This cement meets ASTM C909 and AASHTO M302 Specifications for Grade 100 Slag Cement and CSA A3001 for Type S Slag Cement

A Test result provided for information only.

December 17, 2019 St.

Marys Cement Detroit

Plant

9333 Dearborn Avenue

Detroit, MI 48209

Tel: (313) 842-4600 - Fax: (313) 849-4512

Linda Harris

Linda M. Harris

Quality Control Manager



8800 Dix Ave., Detroit, MI 48209

Weekly Product Conformance Report

For Week of December 30 2019 to January 04 2020

Product: 2NS Natural Sand

Location: American Aggregate, Ray Road Plant

State Pit Number: 63-115

U.S.Sieve	3/8"	#4	#8	#16	#30	#50	#100	LBW	FM
Metric Sieve	9.5mm	4.75mm	2.36mm	1.18mm	600µm	300µm	150µm		
MDOT Specification	100	95-100	85-95	35-75	20-55	10-30	0-10	0-3.0	2.70-3.10
Percent Passing									
2018 Shipping Average	100	96	79	61	46	24	6	0.7	2.88
November Average	100	96	79	62	47	24	4	0.5	2.87
Week of 12/30/2019	100	97	78	62	48	26	6	1.2	2.83

Average Physical Property Data

ASTM C 29, Loose Unit Weight (2018 Average) - 111 lb/ft³

ASTM C 29, Rodded Unit Weight (2018 Average) - 117 lb/ft³

ASTM C 128, Bulk Specific Gravity Dry (2018 Average) - 2.660

ASTM C 128, Bulk Specific Gravity SSD (2018 Average) - 2.69

ASTM C 128, Absorption (2018 Average) - 1.0%

ASTM C 142, Clay Lumps and Friable Particles In Aggregate - 0.3% - TTL

ASTM C 123, Lightweight Particles In Aggregate (Coal & Lignite @ 2.00 Gs) - 0.3% - TTL

ASTM C 88, Soundness of Aggregate by Use of Sodium Sulfate - 3% loss - TTL

ASTM C 40, Organic Impurities In Fine Aggregate for Concrete < 1

ASTM C 1252, Uncompacted Void Content, Method A - 39.5%

MTM 118, Fine Aggregate Angularity - 1.9

This information is not to be taken as warranty or representation for which we assume legal responsibility nor as permission or recommendation to practice any patented invention without a license. It is offered solely for your consideration, investigation and verification.

Weekly Summary 20191230 - 2020 Ray Road



**SOLUTIONS FOR
YOUR ENVIRONMENT™**

8800 Dix Ave., Detroit, MI 48209

Weekly Product Conformance Report

For Week of December 30 2019 to January 04 2020

Product: 6AA Limestone

Source: Lafarge North America, Presque Isle Quarry

Location: SCA, Detroit Dock

State Pit Number: 71-47

U.S.Sieve	1 1/2"	1"	3/4"	1/2"	3/8"	#4	LBW
Metric Sieve	37.5mm	25.0mm	19.0mm	12.5mm	9.5mm	4.75mm	
MDOT Specification	100	95-100	-	30-60	-	0-8	0-2.0
Percent Passing							
2018 Shipping Average	100	100	86	46	23	3	1.2
November Average	100	97	78	41	25	6	1.5
Week of 12/30/2019	100	98	79	49	25	4	1.3

Average Physical Property Data

MTM 110, Soft Particles (2017) - 0.0% (Specification 2.0% maximum) – Lafarge Data

MTM 110, Clay-Ironstone Particles (2017) - 0.0% (Specification 1.0% maximum) – Lafarge Data

MTM 110, Chert Particles (2017) - 0.0% – Lafarge Data

MTM 110, Sum of Soft Particles and Chert (2017) - 0.0% (Specification 4.0% maximum) – Lafarge Data

MTM 115, Freeze-Thaw Dilation - 0.016% (Tested 2014) – MDOT

ASTM C 29, Loose Unit Weight (2018 Average) - 89 lb/ft³

ASTM C 29, Rodded Unit Weight (2018 Average) - 98 lb/ft³

ASTM C 127, Bulk Specific Gravity Dry (2018) - 2.56

ASTM C 127, Bulk Specific Gravity SSD (2018) - 2.59

ASTM C 127, Absorption (2018) - 1.5%

ASTM C 142, Clay Lumps and Friable Particles in Aggregate - 0.2%

ASTM C 131, Abrasion and Impact in the Los Angeles Machine - 33%

ASTM C 88, Soundness of Aggregate by Use of Sodium Sulfate - 3% loss – Lafarge Data

ASTM C 123, Light Weight Particles (Chert [Less Than 2.40 sp gr SSD]) in Aggregate - 0.0% – TTL

ASTM C 123, Light Weight Particles (Coal and Lignite) in Aggregate - 0.0% – TTL



The Chemical Company

3

03 30 00	Cast-in-Place Concrete
03 40 00	Precast Concrete
03 70 00	Mass Concrete

MasterAir® AE 200

Air-Entraining Admixture

Formerly Micro Air*

Description

MasterAir AE 200 air-entraining admixture provides concrete with extra protection by creating air bubbles that are ultrastable, small and closely spaced – a characteristic especially useful in the types of concrete known for their difficulty to entrain and maintain the air content desired.

Even when used at a lower dosage than standard air-entraining admixtures, MasterAir AE 200 admixture meets the requirements of ASTM C 260, AASHTO M 154, and CRD-C 13.

Applications

Recommended for use in:

- Concrete exposed to cyclic freezing and thawing
- Production of high-quality normal or lightweight concrete (heavyweight concrete normally does not contain entrained air)

Features

- Ready-to-use in the proper concentration for rapid, accurate dispensing
- Greatly improved stability of air-entrainment
- Ultra stable air bubbles

Benefits

- Increased resistance to damage from cyclic freezing and thawing
- Increased resistance to scaling from deicing salts
- Improved plasticity and workability
- Improved air-void system in hardened concrete
- Improved ability to entrain and retain air in low-slump concrete, concrete containing high-carbon content fly ash, concrete using large amounts of fine materials, concrete using high-alkali cements, high-temperature concrete, and concrete with extended mixing times
- Reduced permeability – increased watertightness
- Reduced segregation and bleeding

Performance Characteristics

Concrete durability research has established that the best protection for concrete from the adverse effects of freezing and thawing cycles and deicing salts results from: proper air content in the hardened concrete, a suitable air-void system in terms of bubble size and spacing and adequate concrete strength, assuming the use of sound aggregates and proper mixing, transporting, placing, consolidation, finishing and curing techniques. MasterAir AE 200 admixture can be used to obtain adequate freezing and thawing durability in a properly proportioned concrete mixture, if standard industry practices are followed.

MASTER®
» BUILDERS
SOLUTIONS

Air Content Determination: The total air content of normal weight concrete should be measured in strict accordance with ASTM C 231, "Standard Test Method for Air Content of Freshly Mixed Concrete by the Pressure Method" or ASTM C 173/C 173M, "Standard Test Method for Air Content of Freshly Mixed Concrete by the Volumetric Method."

The air content of lightweight concrete should only be determined using the Volumetric Method. The air content should be verified by calculating the gravimetric air content in accordance with ASTM C 138/C 138M, "Standard Test Method for Density (Unit Weight), Yield, and Air Content (Gravimetric) of Concrete." If the total air content, as measured by the Pressure Method or Volumetric Method and as verified by the Gravimetric Method, deviates by more than 1.5%, the cause should be determined and corrected through equipment calibration or by whatever process is deemed necessary.

Guidelines for Use

Dosage: There is no standard dosage for MasterAir AE 200 admixture. The exact quantity of air-entraining admixture needed for a given air content of concrete varies because of differences in concrete making materials and ambient conditions. Typical factors that might influence the amount of air entrained include: temperature, cementitious materials, sand gradation, sand-aggregate ratio, mixture proportions, slump, means of conveying and placement, consolidation and finishing technique.

The amount of MasterAir AE 200 admixture used will depend upon the amount of entrained air required under actual job conditions. In a trial mixture, use 0.125 to 1.5 fl oz/cwt (8-98 mL/100 kg) of cement. In mixtures containing water-reducing or set-control admixtures, the amount of MasterAir AE 200 admixture needed is somewhat less than the amount required in plain concrete. Due to possible changes in the factors that can affect the dosage of MasterAir AE 200 admixture, frequent air content checks should be made during the course of the work. Adjustments to the dosage should be based on the amount of entrained air required in the mixture at the point of placement. If an unusually high or low dosage of MasterAir AE 200 admixture is required to obtain the desired air content, consult your Local sales representative. In such cases, it may be necessary to determine that, in addition to a proper air content in the fresh concrete, a suitable air-void system is achieved in the hardened concrete.

Dispensing and Mixing: Add MasterAir AE 200 admixture to the concrete mixture using a dispenser designed for air-entraining admixtures; or add manually using a suitable measuring device that ensures accuracy within plus or minus 3% of the required amount. For optimum, consistent performance, the air-entraining admixture should be dispensed on damp, fine aggregate or with the initial batch water. If the concrete mixture contains lightweight aggregate, field evaluations should be conducted to determine the best method to dispense the air-entraining admixture.

Precaution

In a 2005 publication from the Portland Cement Association (PCA R&D Serial No. 2789), it was reported that problematic air-void clustering that can potentially lead to above normal decreases in strength was found to coincide with late additions of water to air-entrained concretes. Late additions of water include the conventional practice of holding back water during batching for addition at the jobsite. Therefore, caution should be exercised with delayed additions to air-entrained concrete. Furthermore, an air content check should be performed after post-batching addition of any other materials to an air-entrained concrete mixture.

Product Notes

Corrosivity – Non-Chloride, Non-Corrosive: MasterAir AE 200 admixture will neither initiate nor promote corrosion of reinforcing and prestressing steel embedded in concrete, or of galvanized steel floor and roof systems. No calcium chloride or other chloride-based ingredients are used in the manufacture of this admixture.

Compatibility: MasterAir AE 200 admixture may be used in combination with any BASF admixture, unless stated otherwise on the data sheet for the other product. When used in conjunction with other admixtures, each admixture must be dispensed separately into the mixture.

Storage and Handling

Storage Temperature: MasterAir AE 200 admixture should be stored and dispensed at 35 °F (2 °C) or higher. Although freezing does not harm this product, precautions should be taken to protect it from freezing. If it freezes, thaw and reconstitute by mild mechanical agitation. Do not use pressurized air for agitation.

Shelf Life: MasterAir AE 200 admixture has a minimum shelf life of 18 months. Depending on storage conditions, the shelf life may be greater than stated. Please contact your Local sales representative regarding suitability for use and dosage recommendations if the shelf life of MasterAir AE 200 admixture has been exceeded.

Safety: MasterAir AE 200 admixture is a caustic solution. Chemical goggles and gloves are recommended when transferring or handling this material. (See SDS and/or product label for complete information.)

Packaging

MasterAir AE 200 admixture is supplied in 55 gal (208 L) drums, 275 gal (1040 L) totes and by bulk delivery.

Related Documents

Safety Data Sheets: MasterAir AE 200 admixture

Additional Information

For suggested specification information or for additional product data on MasterAir AE 200 admixture, contact your local sales representative.

The Admixture Systems business of BASF's Construction Chemicals division is the leading provider of solutions that improve placement, pumping, finishing, appearance and performance characteristics of specialty concrete used in the ready-mixed, precast, manufactured concrete products, underground construction and paving markets. For over 100 years we have offered reliable products and innovative technologies, and through the Master Builders Solutions brand, we are connected globally with experts from many fields to provide sustainable solutions for the construction industry.

Limited Warranty Notice

BASF warrants this product to be free from manufacturing defects and to meet the technical properties on the current Technical Data Guide, if used as directed within shelf life. Satisfactory results depend not only on quality products but also upon many factors beyond our control. BASF MAKES NO OTHER WARRANTY OR GUARANTEE, EXPRESS OR IMPLIED, INCLUDING WARRANTIES OF MERCHANTABILITY OR FITNESS FOR A PARTICULAR PURPOSE WITH RESPECT TO ITS PRODUCTS. The sole and exclusive remedy of Purchaser for any claim concerning this product, including but not limited to, claims alleging breach of warranty, negligence, strict liability or otherwise, is shipment to purchaser of product equal to the amount of product that fails to meet this warranty or refund of the original purchase price of product that fails to meet this warranty, at the sole option of BASF. Any claims concerning this product must be received in writing within one (1) year from the date of shipment and any claims not presented within that period are waived by Purchaser. BASF WILL NOT BE RESPONSIBLE FOR ANY SPECIAL, INCIDENTAL, CONSEQUENTIAL (INCLUDING LOST PROFITS) OR PUNITIVE DAMAGES OF ANY KIND.

Purchaser must determine the suitability of the products for the intended use and assumes all risks and liabilities in connection therewith. This information and all further technical advice are based on BASF's present knowledge and experience. However, BASF assumes no liability for providing such information and advice including the extent to which such information and advice may relate to existing third party intellectual property rights, especially patent rights, nor shall any legal relationship be created by or arise from the provision of such information and advice. BASF reserves the right to make any changes according to technological progress or further developments. The Purchaser of the Product(s) must test the product(s) for suitability for the intended application and purpose before proceeding with a full application of the product(s). Performance of the product described herein should be verified by testing and carried out by qualified experts.

* Micro Air became MasterAir AE 200 under the Master Builders Solutions brand, effective January 1, 2014.

© BASF Corporation 2014 ■ 01/14 ■ PRE-DAT-0009

BASF Corporation
Admixture Systems
www.master-builders-solutions.basf.us

United States
23700 Chagrin Boulevard
Cleveland, Ohio 44122-5544
Tel: 800 829-0930 ■ Fax: 216 830-8821

Canada
1800 Clark Boulevard
Brampton, Ontario L6T 4M7
Tel: 800 387-5982 ■ Fax: 905 792-0651





The Chemical Company

3

03 30 00	Cast-in-Place Concrete
03 40 00	Precast Concrete
03 70 00	Mass Concrete

MasterPozzolith® 200

Water-Reducing Admixture

Formerly Pozzolith 200 N *

Description

MasterPozzolith 200 ready-to-use, liquid admixture is used for making more uniform and predictable quality concrete. It meets ASTM C 494/C 494M requirements for Type A, water-reducing, Type B, retarding, and Type D, water-reducing and retarding, admixtures.

Applications

Recommended for use in:

- Prestressed concrete
- Precast concrete
- Reinforced concrete
- Shotcrete
- Lightweight concrete
- Pumped concrete
- 4x4™ Concrete
- Pervious concrete
- Self-consolidating concrete (SCC)

Features

- Reduced water content required for a given workability
- Controlled setting characteristics – normal or retarded

Benefits

- Improved workability
- Reduced segregation
- Improved finishing characteristics for flatwork and cast surfaces
- Increased compressive and flexural strengths

Guidelines for Use

Dosage: MasterPozzolith 200 admixture is recommended for use at a dosage of 3-4 fl oz/cwt (195-260 mL/100 kg) of cementitious materials for Type A applications and up to 6 fl oz/cwt (390 mL/100 kg) for Type B and D requirements. Because of variations in job conditions and concrete materials, dosages other than the recommended amounts may be required. In such cases, contact your local sales representative.

Product Notes

Corrosivity – Non-Chloride, Non-Corrosive: MasterPozzolith 200 admixture will neither initiate nor promote corrosion of reinforcing steel in concrete. This admixture does not contain intentionally-added calcium chloride or other chloride-based ingredients.

Compatibility: MasterPozzolith 200 admixture may be used in combination with any BASF admixtures. When used in conjunction with other admixtures, each admixture must be dispensed separately into the mixture.

MASTER®
»BUILDERS
SOLUTIONS

Storage and Handling

Storage Temperature: MasterPozzolith 200 admixture should be stored above freezing temperatures. If MasterPozzolith 200 admixture freezes, thaw at 35 °F (2 °C) or above and completely reconstitute by mild mechanical agitation. **Do not use pressurized air for agitation.**

Shelf Life: MasterPozzolith 200 admixture has a minimum shelf life of 18 months. Depending on storage conditions, the shelf life may be greater than stated. Please contact your local sales representative regarding suitability for use and dosage recommendations if the shelf life of MasterPozzolith 200 admixture has been exceeded.

Packaging

MasterPozzolith 200 admixture is supplied in 55 gal (208 L) drums, 275 gal (1040 L) totes and by bulk delivery.

Related Documents

Safety Data Sheets: MasterPozzolith 200 admixture

Additional Information

For additional information on MasterPozzolith 200 admixture or its use in developing a concrete mixture with special performance characteristics, contact your local sales representative.

The Admixture Systems business of BASF's Construction Chemicals division is the leading provider of solutions that improve placement, pumping, finishing, appearance and performance characteristics of specialty concrete used in the ready-mixed, precast, manufactured concrete products, underground construction and paving markets. For over 100 years we have offered reliable products and innovative technologies, and through the Master Builders Solutions brand, we are connected globally with experts from many fields to provide sustainable solutions for the construction industry.

Limited Warranty Notice

BASF warrants this product to be free from manufacturing defects and to meet the technical properties on the current Technical Data Guide, if used as directed within shelf life. Satisfactory results depend not only on quality products but also upon many factors beyond our control. **BASF MAKES NO OTHER WARRANTY OR GUARANTEE, EXPRESS OR IMPLIED, INCLUDING WARRANTIES OF MERCHANTABILITY OR FITNESS FOR A PARTICULAR PURPOSE WITH RESPECT TO ITS PRODUCTS.** The sole and exclusive remedy of Purchaser for any claim concerning this product, including but not limited to, claims alleging breach of warranty, negligence, strict liability or otherwise, is shipment to purchaser of product equal to the amount of product that fails to meet this warranty or refund of the original purchase price of product that fails to meet this warranty, at the sole option of BASF. Any claims concerning this product must be received in writing within one (1) year from the date of shipment and any claims not presented within that period are waived by Purchaser. **BASF WILL NOT BE RESPONSIBLE FOR ANY SPECIAL, INCIDENTAL, CONSEQUENTIAL (INCLUDING LOST PROFITS) OR PUNITIVE DAMAGES OF ANY KIND.**

Purchaser must determine the suitability of the products for the intended use and assumes all risks and liabilities in connection therewith. This information and all further technical advice are based on BASF's present knowledge and experience. However, BASF assumes no liability for providing such information and advice including the extent to which such information and advice may relate to existing third party intellectual property rights, especially patent rights, nor shall any legal relationship be created by or arise from the provision of such information and advice. BASF reserves the right to make any changes according to technological progress or further developments. The Purchaser of the Product(s) must test the product(s) for suitability for the intended application and purpose before proceeding with a full application of the product(s). Performance of the product described herein should be verified by testing and carried out by qualified experts.

* Pozzolith 200 N became MasterPozzolith 200 under the Master Builders Solutions brand, effective January 1, 2014.

© BASF Corporation 2014 ■ 01/14 ■ PFE-DAT-0066

BASF Corporation
Admixture Systems
www.master-builders-solutions.basf.us

United States
23700 Chagrin Boulevard
Cleveland, Ohio 44122-5544
Tel: 800 629-0060 ■ Fax: 216 830-8821

Canada
1800 Clark Boulevard
Brampton, Ontario L6T 4M7
Tel: 905 387-5882 ■ Fax: 905 792-0851



MasterPolyheed® 997

Mid-Range Water-Reducing Admixture

Formerly PolyHeed 997*

Description

MasterPolyheed 997 admixture is a patented multi-component, mid-range water-reducing admixture. MasterPolyheed 997 admixture meets ASTM C 494/C 494M requirements for Type A, water-reducing, and Type F, high-range water-reducing, admixtures.

Applications

Recommended for use in:

- All concrete applications where superior workability, pumpability and finishability qualities are desired, in particular, flatwork, pumped concrete and pervious concrete
- Concrete containing manufactured sand and harsh concrete mixtures

Features

- True mid-range water reduction (5-15%) and excellent performance across a wide slump range, especially the difficult slump range of 5-8 in. (125-200 mm)
- Superior workability, pumpability and finishability qualities even in concrete mixtures containing low amounts of cementitious materials
- Superior finishing characteristics for residential/commercial flatwork and formed surfaces

Benefits

- Significantly reduced placement and finishing time resulting in lower in-place concrete costs
- Higher strength at all ages
- Enhanced concrete durability
- Increased service life of concrete structures

Performance Characteristics

Mixture Data: 500 lb/yc³ (295 kg/m³) of Type I cement; slump 6-7 in. (150-180 mm); 5-6% air; concrete temperature 70 °F (21 °C); ambient temperature, 70 °F (21 °C).

Setting Time Performance¹

Mixture	Initial Set (h:min)	Difference (h:min)
Reference	6:01	—
MasterPolyheed 997 admixture @		
5 fl oz/cwt (325 mL/100 kg)	6:22	+0:21
10 fl oz/cwt (650 mL/100 kg)	6:57	+0:56
15 fl oz/cwt (980 mL/100 kg)	7:31	+1:30

Compressive Strength, psi (MPa)

Mixture	7-Day	28-Day
Plain	2360 (16.3)	3320 (22.9)
MasterPolyheed 997 admixture @		
5 fl oz/cwt (325 mL/100 kg)	3060 (21.1)	3930 (27.1)
10 fl oz/cwt (650 mL/100 kg)	3740 (25.8)	4610 (31.8)
15 fl oz/cwt (980 mL/100 kg)	4620 (31.9)	5460 (37.7)

¹Note: The data shown are based on controlled laboratory tests. Reasonable variations from the results shown here may be experienced as a result of differences in concrete making materials and jobsite conditions.

Guidelines for Use

Dosage: MasterPolyheed 997 admixture has a recommended dosage range of 3-15 fl oz /cwt (195-980 mL/100 kg) of cementitious material for most concrete mixes.

As the dosage of MasterPolyheed 997 admixture increases to 15 fl oz/cwt (980 mL/100 kg) of cementitious materials, normal concrete setting characteristics are maintained and early and ultimate compressive strengths increase.

BASF does not recommend the use of dosages outside the recommended range without trial testing. Consult your local sales representative for assistance in determining the dosage for optimum performance.

Product Notes

Corrosivity – Non-Chloride, Non-Corrosive: MasterPolyheed 997 admixture will neither initiate nor promote corrosion of reinforcing or prestressing steel embedded in concrete, or of galvanized steel floor and roof systems. MasterPolyheed 997 admixture does not contain intentionally added calcium chloride or other chloride-based ingredients.

Compatibility: MasterPolyheed 997 admixture may be used in combination with any BASF admixtures. When used in conjunction with other admixtures, each admixture must be dispensed separately into the concrete mixture.

Storage and Handling

Storage Temperature: If MasterPolyheed 997 admixture freezes, thaw at 35 °F (2 °C) or above and completely reconstitute by mild mechanical agitation. **Do not use pressurized air for agitation.**

Shelf Life: MasterPolyheed 997 admixture has a minimum shelf life of 18 months. Depending on storage conditions, the shelf life may be greater than stated. Please contact your local sales representative regarding suitability for use and dosage recommendations if the shelf life of MasterPolyheed 997 admixture has been exceeded.

Packaging

MasterPolyheed 997 admixture is supplied in 55 gal (208 L) drums, 275 gal (1040 L) totes and by bulk delivery.

Related Documents

Safety Data Sheets: MasterPolyheed 997 admixture

Additional Information

For additional information on MasterPolyheed 997 admixture or its use in developing concrete mixtures with special performance characteristics, contact your local sales representative.

The Admixture Systems business of BASF's Construction Chemicals division is the leading provider of solutions that improve placement, pumping, finishing, appearance and performance characteristics of specialty concrete used in the ready-mixed, precast, manufactured concrete products, underground construction and paving markets. For over 100 years we have offered reliable products and innovative technologies, and through the Master Builders Solutions brand, we are connected globally with experts from many fields to provide sustainable solutions for the construction industry.

Limited Warranty Notice

BASF warrants this product to be free from manufacturing defects and to meet the technical properties on the current Technical Data Guide, if used as directed within shelf life. Satisfactory results depend not only on quality products but also upon many factors beyond our control. BASF MAKES NO OTHER WARRANTY OR GUARANTEE, EXPRESS OR IMPLIED, INCLUDING WARRANTIES OF MERCHANTABILITY OR FITNESS FOR A PARTICULAR PURPOSE WITH RESPECT TO ITS PRODUCTS. The sole and exclusive remedy of Purchaser for any claim concerning this product, including but not limited to, claims alleging breach of warranty, negligence, strict liability or otherwise, is shipment to purchaser of product equal to the amount of product that fails to meet this warranty or refund of the original purchase price of product that fails to meet this warranty, at the sole option of BASF. Any claims concerning this product must be received in writing within one (1) year from the date of shipment and any claims not presented within that period are waived by Purchaser. BASF WILL NOT BE RESPONSIBLE FOR ANY SPECIAL, INCIDENTAL, CONSEQUENTIAL (INCLUDING LOST PROFITS) OR PUNITIVE DAMAGES OF ANY KIND.

Purchaser must determine the suitability of the products for the intended use and assumes all risks and liabilities in connection therewith. This information and all further technical advice are based on BASF's present knowledge and experience. However, BASF assumes no liability for providing such information and advice including the extent to which such information and advice may relate to existing third party intellectual property rights, especially patent rights, nor shall any legal relationship be created by or arise from the provision of such information and advice. BASF reserves the right to make any changes according to technological progress or further developments. The Purchaser of the Product(s) must test the product(s) for suitability for the intended application and purpose before proceeding with a full application of the product(s). Performance of the product described herein should be verified by testing and carried out by qualified experts.

* Polyheed 997 became MasterPolyheed 997 under the Master Builders Solutions brand, effective January 1, 2014.

© BASF Corporation 2014 ■ 01/14 ■ PFE-DAT-0050

BASF Corporation
Admixture Systems
www.master-builders-solutions.basf.us

United States
23700 Chagrin Boulevard
Cleveland, Ohio 44122-5544
Tel: 800 629-0000 ■ Fax: 216 830-8821

Canada
1900 Clark Boulevard
Brampton, Ontario L8T 4M7
Tel: 905 897-5862 ■ Fax: 905 792-0861

