

REQUEST FOR INFORMATION

RFI # **007**

Page 1 of 2

GENERAL INFORMATION

RFI SUBJECT Drinking Fountain Drainage	CONTROL SECTION
JOB DESCRIPTION PW 7017 Puritan	JOB NUMBER PW 7017
CONTRACTOR Major Cement Co.	
LOCATION Purtian	DATE 04/14/21

INFORMATION REQUEST

The project documents do not seem to be clear on drainage for the drinking fountain. Please confirm if drinking fountain drainage is required and if so, provide direction on where / how we should drain the fountain.

Provide a 1 1/2" Sch. 40 PVC drain line connection from the drinking fountain to the catch basin as shown on the enclosed PDF drawing and as noted on the drinking fountain submittal and construction details.

Brian Charlton
SmithGroup
04-19-2021

CITY OF DETROIT RESPONSE

Approved by (CED Representative):

Alan C. To
5/3/2021



City of Detroit

City of Detroit

REVISIONS

04/14/2020	100% CD
04/01/2020	100% CD
03/04/2020	95% CD
02/03/2020	90% CD
12/27/2019	60% CD
12/06/2019	30% CD

Drawn By	AOF
Designer	AOF
Reviewer	DPE
Manager	KK3

Hard copy is intended to be 24"x36" when plotted. Scale(s) indicated and graphic quality may not be accurate for any other size.


PROJECT NO.

191185

SHEET NO.

C501

©Copyright 2020
All Rights Reserved

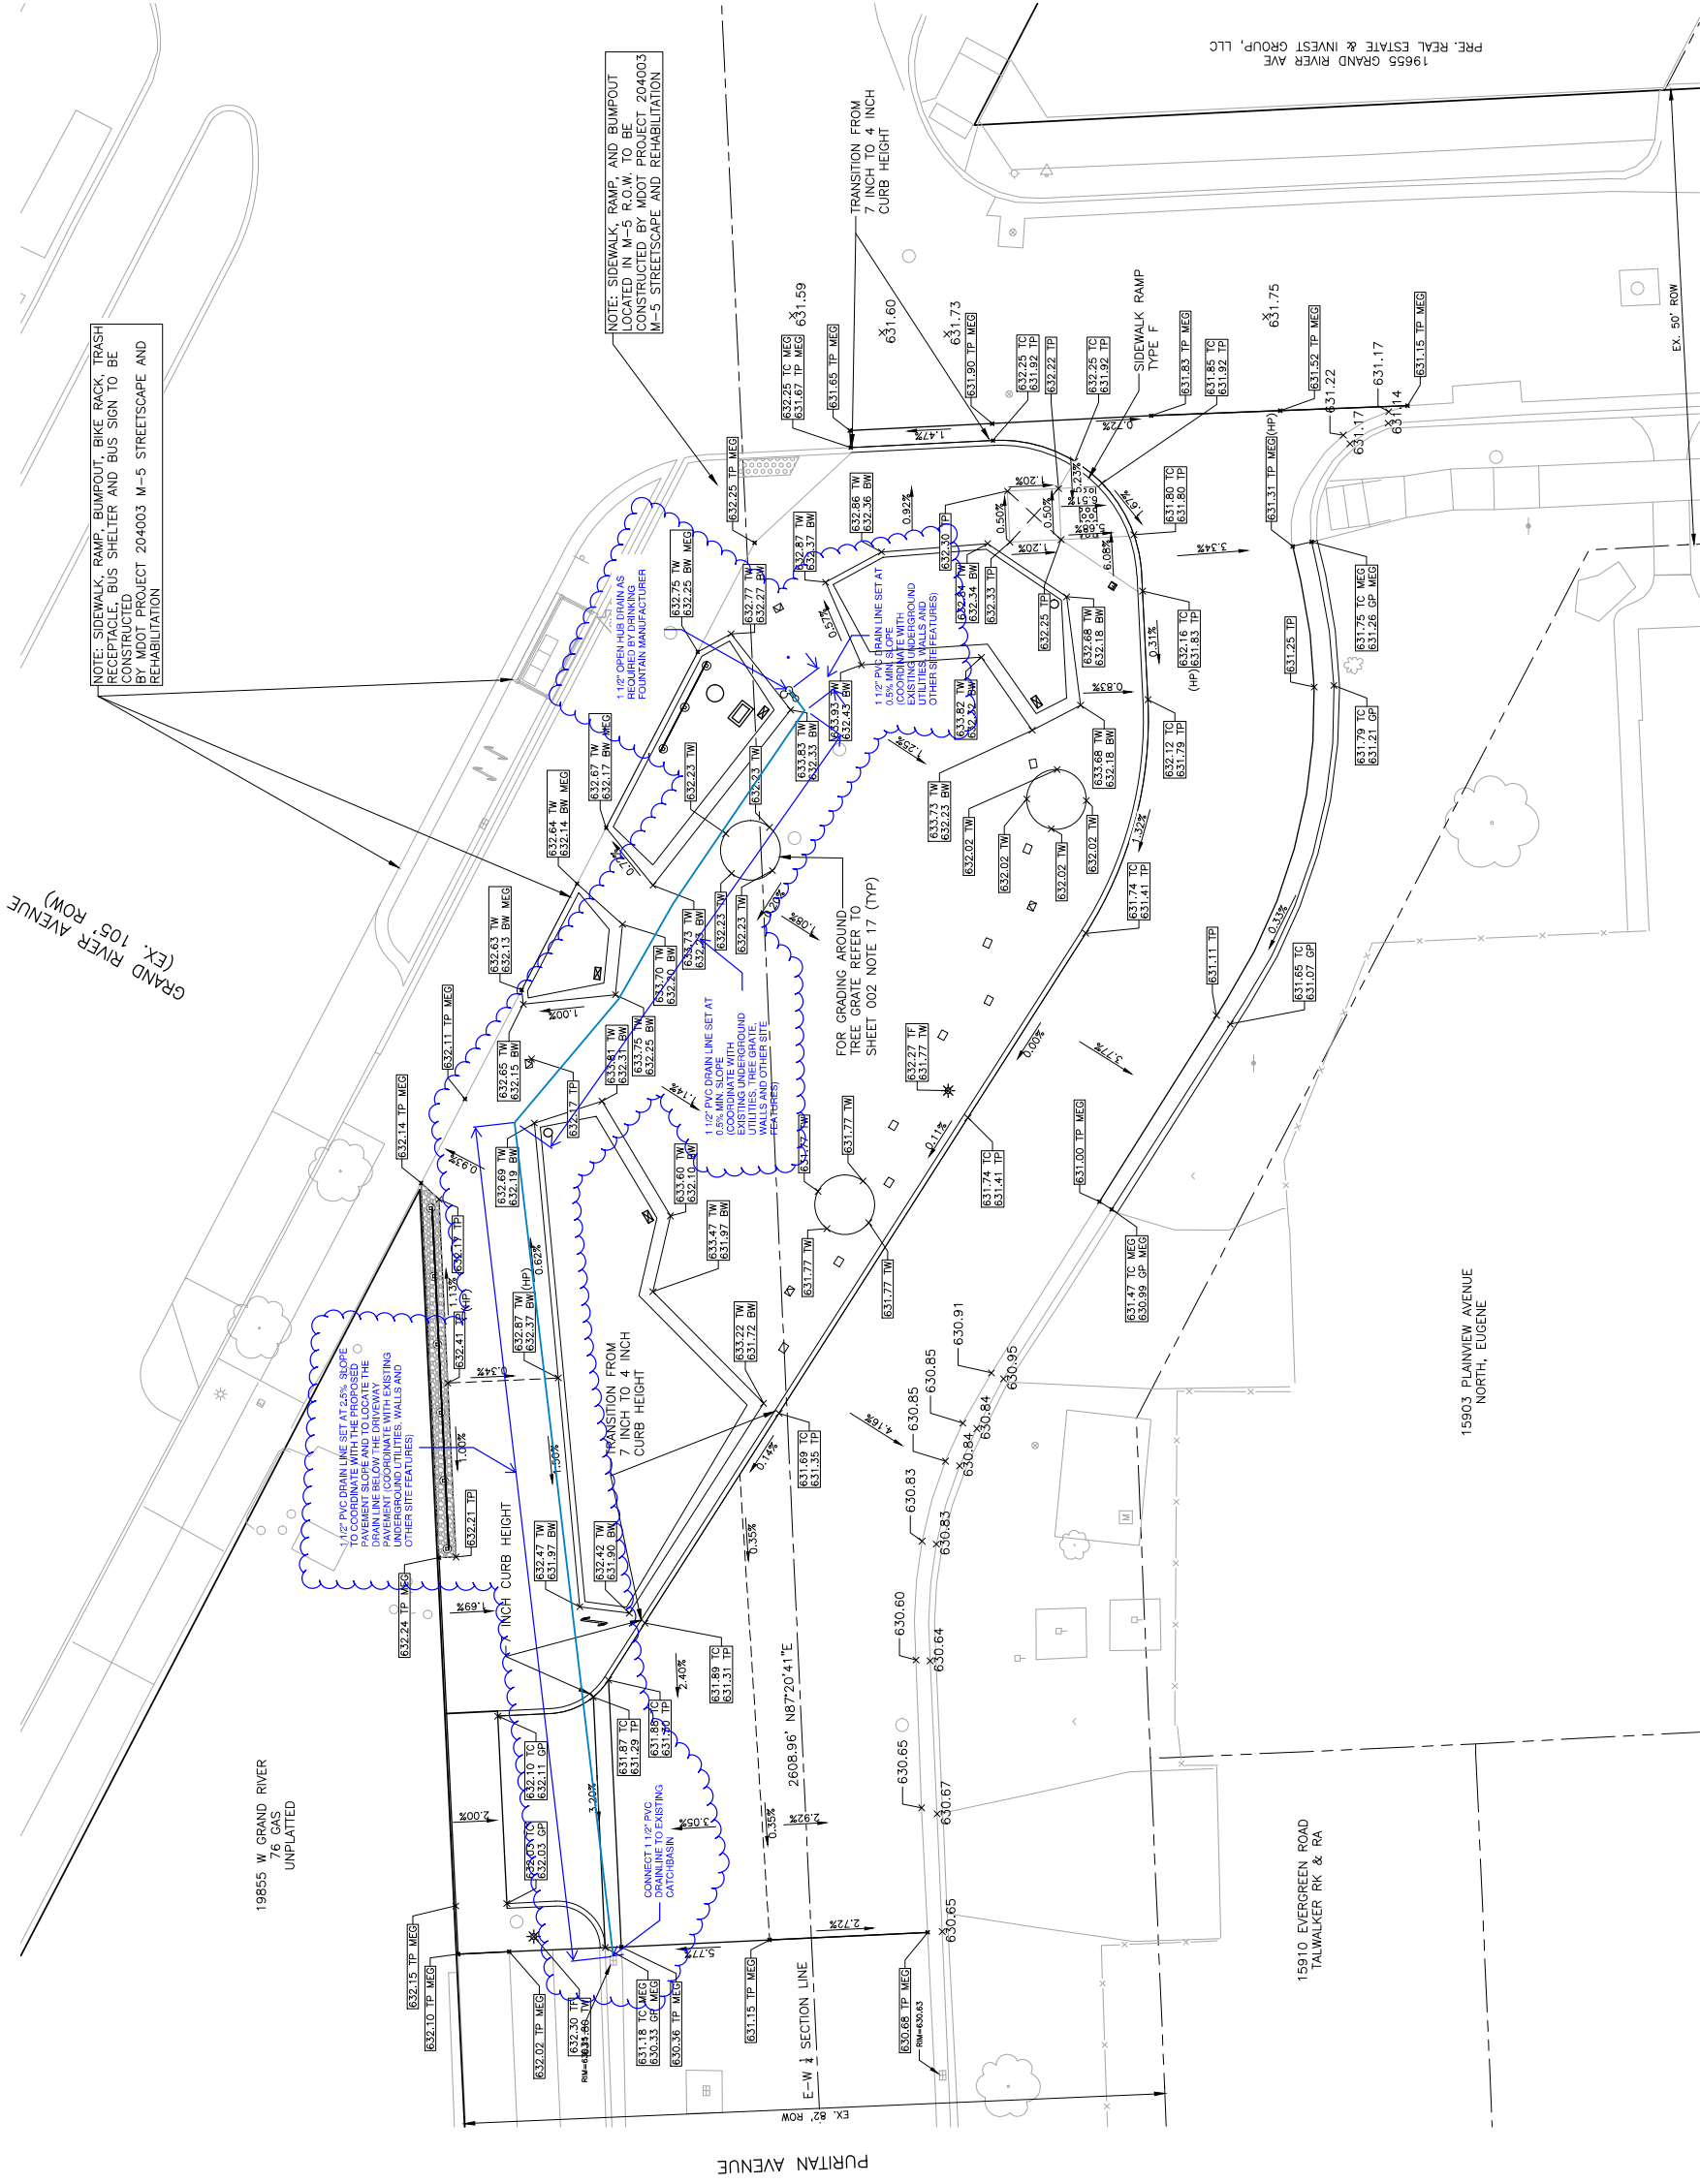

PLAINVIEW AVENUE

GRADING PLAN



NORTH
